




# Transportation Investment Act

## River Valley 1 CRP Update – April 11, 2023

Kenneth Franks, State TIA Administrator  
William Eastin, TIA Regional Coordinator



## TIA Regions

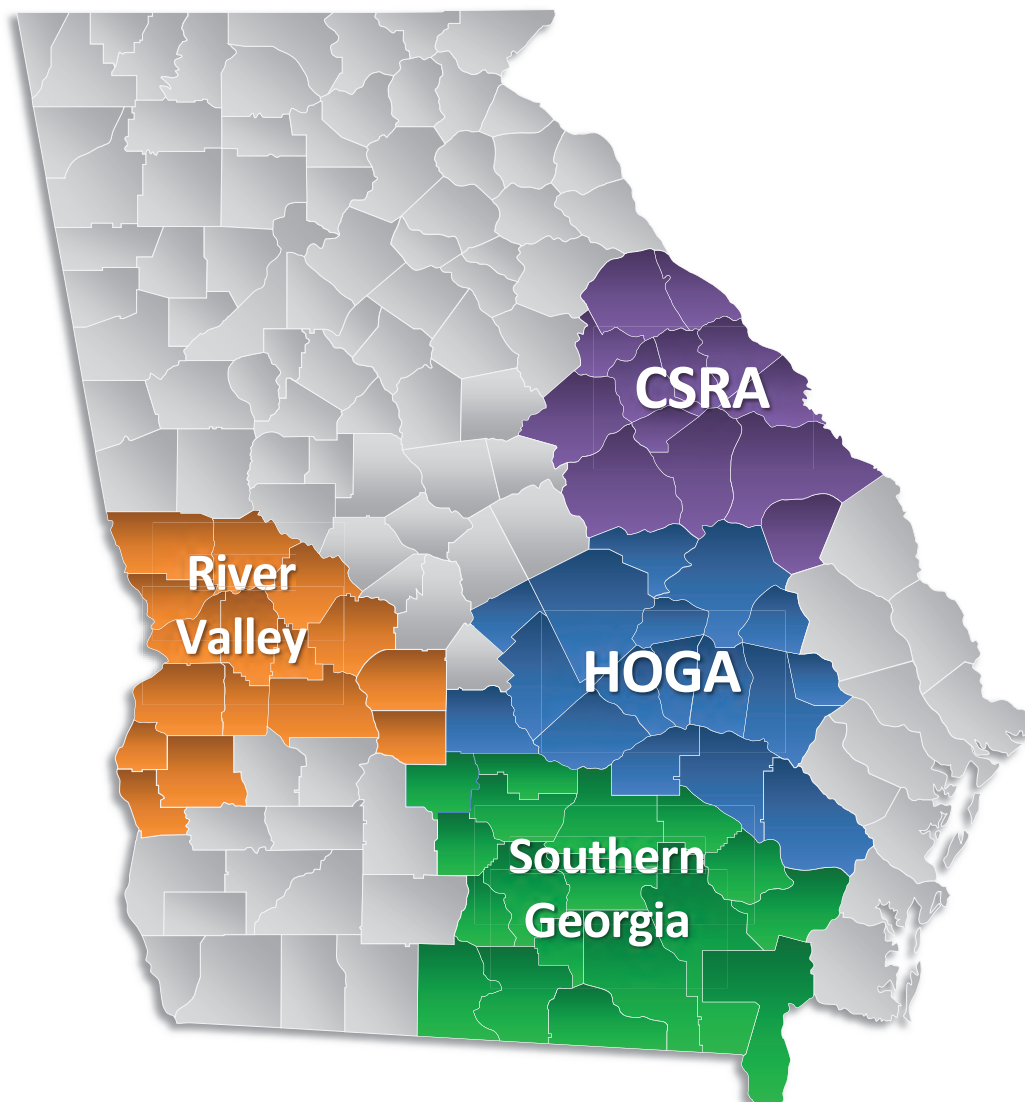


## Final TIA 1 Collections Thru Dec 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$512,301,207	\$384,225,905	\$128,075,302
CSRA	\$746,921,743	\$560,191,307	\$186,730,436
Heart of Georgia	\$335,375,226	\$251,531,419	\$83,843,807
Southern Georgia	\$269,296,711	\$201,972,533	\$67,324,178
Totals	\$1,863,894,887	\$1,397,921,164	\$465,973,722

## Final TIA 1 Collections Thru Dec 2022

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$594,061,269	\$512,301,207	-13.8%
CSRA	\$841,044,916	\$746,921,743	-11.2%
Heart of Georgia	\$398,870,417	\$335,375,226	-15.9%
Southern Georgia	\$211,297,964	\$269,296,711	27.4%

# TIA 1 Timeline

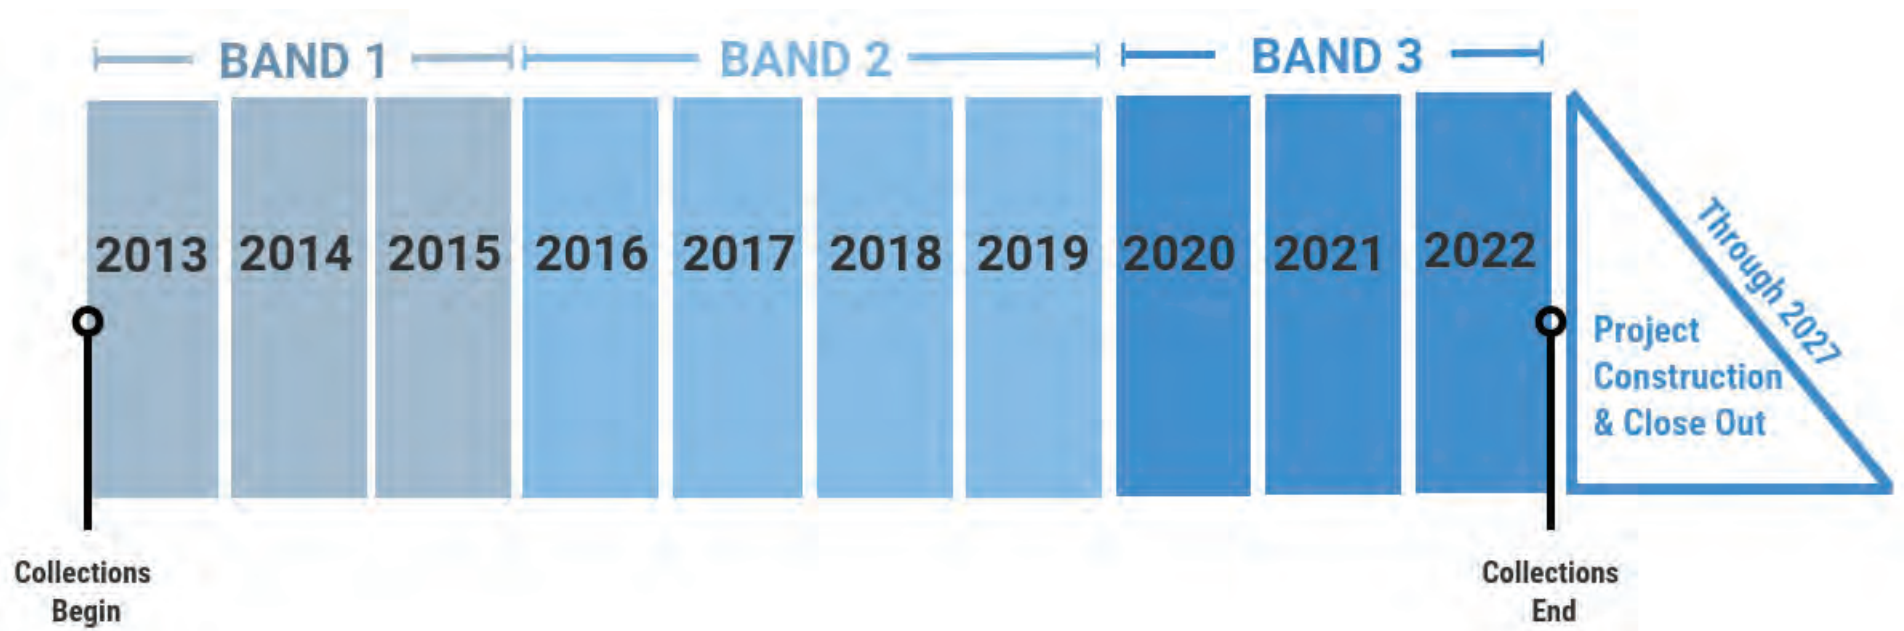

## River Valley Project Overview



**23**

Total Projects

**\$410,754,730**

Final Investment List  
Project Total

**5**

In Construction

**17**

Projects Completed

**\$248,409,060**

Total Expenditure to Date  
(as of 04/05/2023)

## River Valley – TIA 1 Construction Updates

### **US 27 Widening & Roundabout at SR 315 (Band 3)**

- Robinson Paving was low bidder
  - \$39,058,669 (12/2022 letting)
- ROW acquisition on going

### **Buena Vista Road DDI (Band 2)**

- CW Matthews – 9/2020 letting
- Bridge and wall work in progress
  - Will transfer traffic to new bridge and begin demo of remaining bridge.

### **Old Cusseta Rd @ I-185 Interchange (Band 3)**

- Robinson Paving was low bidder
  - \$39,683,951 (9/2022 letting)
- ROW acquisition on going
  - 1 parcel left to acquire
  - Demolitions underway
- Received CST NTP

### **US 280 Widening (Band 3)**

- Reeves Construction – 8/2020 letting
- Paving on going
- Grading ditches
- Plan to switch to new pavement in next couple weeks



## Buena Vista Road DDI





## Buena Vista Road DDI





## Cusseta Rd Interchange





## Cusseta Rd Interchange





## Cusseta Rd Interchange





## US 280 Widening





## US 280 Widening





## US 280 Widening



# Columbus TIA Project Updates

## Spider Web

- Construction split into two phases
- Phase 1 sustainably complete
- Phase 2 bids have been rejected will be and readvertised with new specs to potentially lower the cost

## METRA

- Operations and maintenance ongoing
- Park and Ride facility under construction

