




# Transportation Investment Act

## River Valley 1 CRP Update – August 15, 2023

**Kenneth Franks, State TIA Administrator**  
**William Eastin, TIA Regional Coordinator**



# TIA Regions

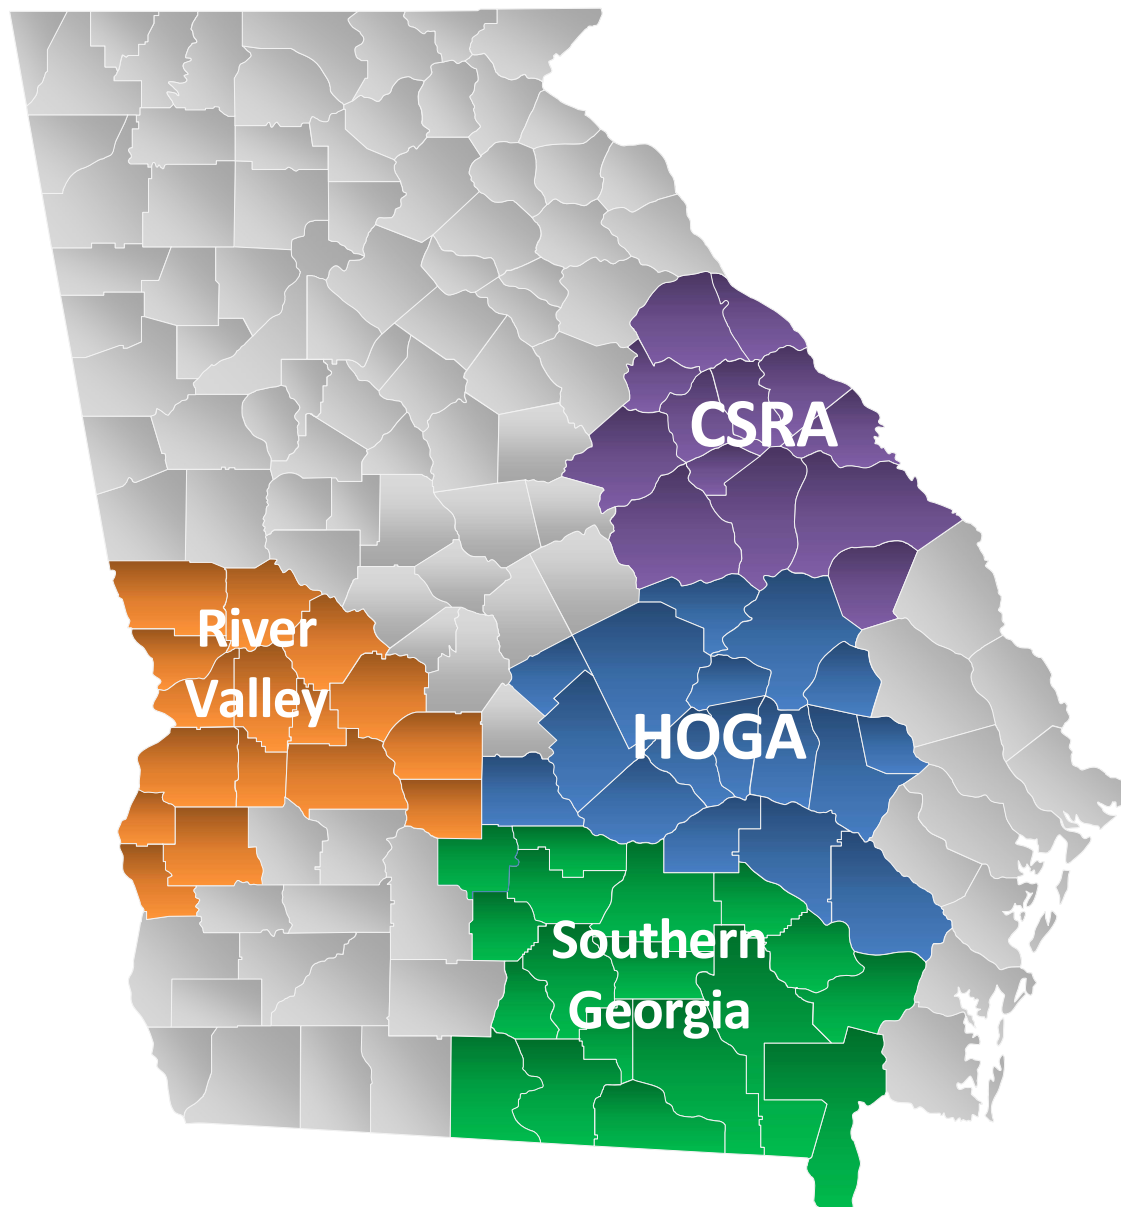

# Final TIA 1 Collections Jan 2013 to Dec 2022


Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$512,301,207	\$384,225,905	\$128,075,302
CSRA	\$746,921,743	\$560,191,307	\$186,730,436
Heart of Georgia	\$335,375,226	\$251,531,419	\$83,843,807
Totals	\$1,863,894,887	\$1,397,921,164	\$465,973,722

# Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$594,061,269	\$512,301,207	-13.8%
CSRA	\$841,044,916	\$746,921,743	-11.2%
Heart of Georgia	\$398,870,417	\$335,375,226	-15.9%
Southern Georgia*	\$236,517,791	\$306,277,646	29.5%

\* Ongoing Southern Georgia Collections Oct 2018 to June 2023

# TIA 1 Timeline

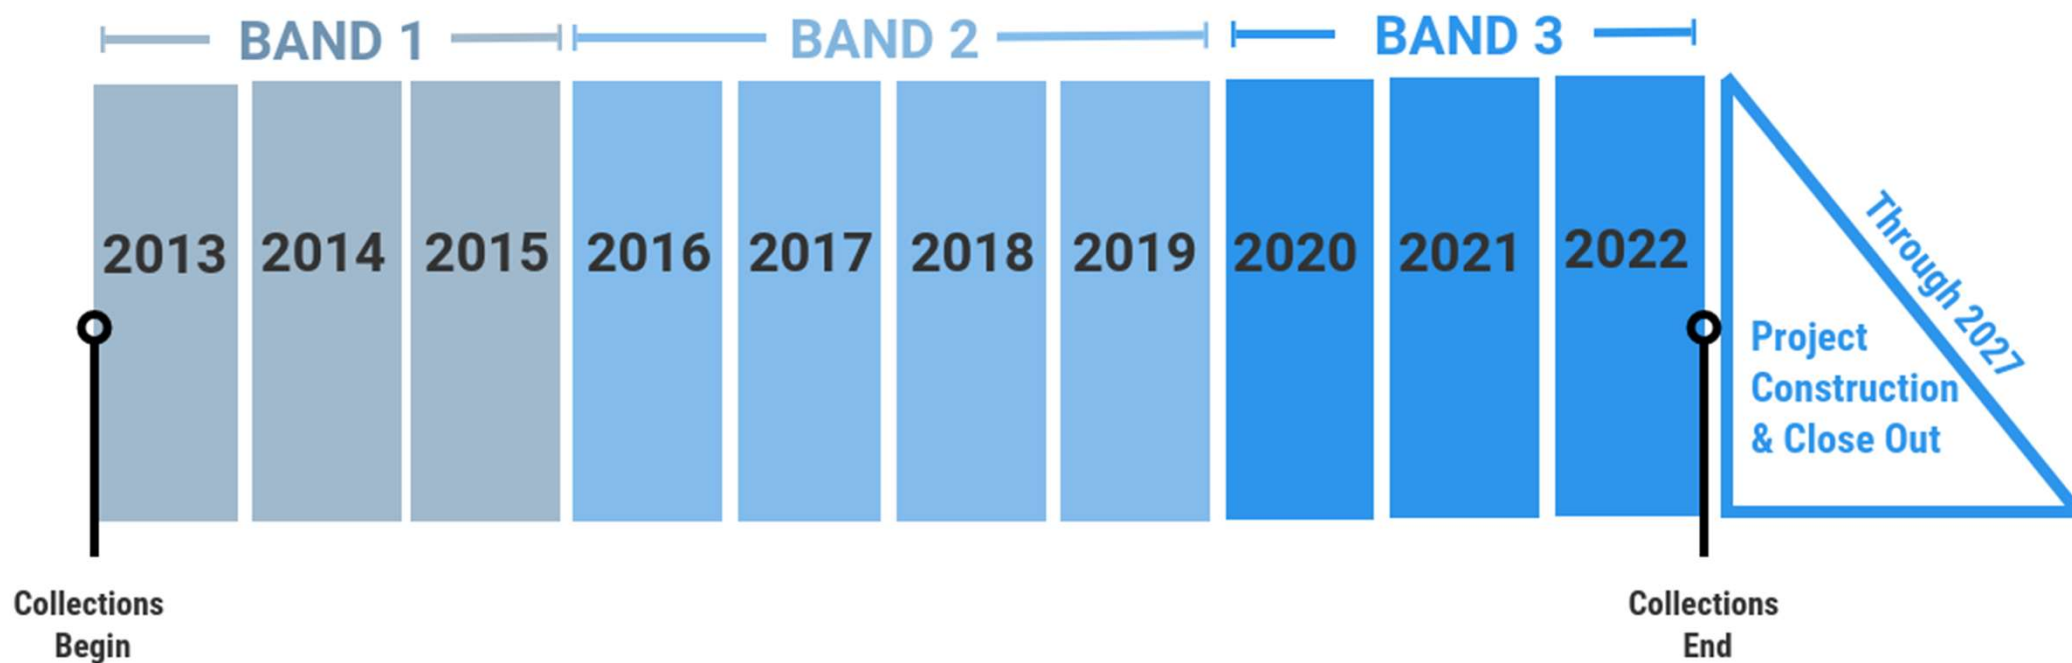

# River Valley Project Overview



**23**

Total Projects

**\$410,754,730**

Final Investment List  
Project Total

**5**

In Construction

**17**

Projects Completed

**\$261,149,268**

Total Expenditure to Date  
(as of **08/11/2023**)

# River Valley – TIA 1 Construction Updates

## US 27 Widening & Roundabout at SR 315 (Band 3)

- Robinson Paving – 12/2022 letting
- ROW acquisition on going
- Clearing and utility relocations starting

## Buena Vista Road DDI (Band 2)

- CW Matthews – 9/2020 letting
- Bridge and ramp work in progress
  - Will transfer traffic to new bridge and begin demo of remaining bridge.

## Old Cusseta Rd @ I-185 Interchange (Band 3)

- Robinson Paving – 9/2022 letting
- Received CST NTP
- Clearing and utility relocations underway

## US 280 Widening (Band 3)

- Reeves Construction – 8/2020 letting
- Paving on going
- Coordinating final items with Veterans Memorial Park
- Switching over traffic starting at east end
- Ongoing ditch and culvert work



# Buena Vista Road DDI





# Buena Vista Road DDI





# Old Cusseta Rd Interchange





# Old Cusseta Rd Interchange





# US 280 Widening





# US 280 Widening





# US 280 Widening




# Columbus TIA Project Updates

## Spider Web

- Construction split into two phases
- Phase 1 substantially complete
- Phase 2 bids have been rejected will be and readvertised with alternatives to potentially lower the cost

## METRA

- Operations and maintenance ongoing
- Park and Ride facility under construction

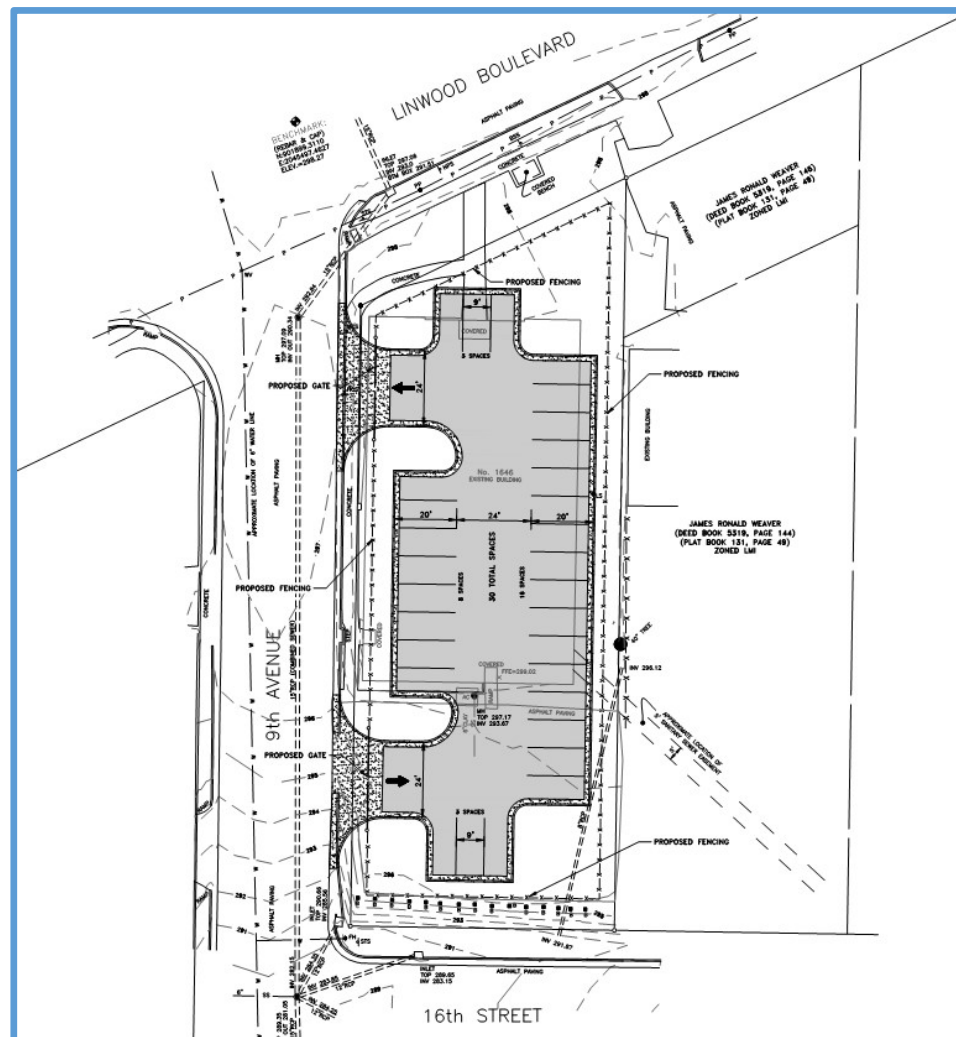



# METRA Park n Ride

