



Georgia Department of Transportation


Transportation Investment Act

River Valley

April 12th, 2022 CRP Update




TIA Regions

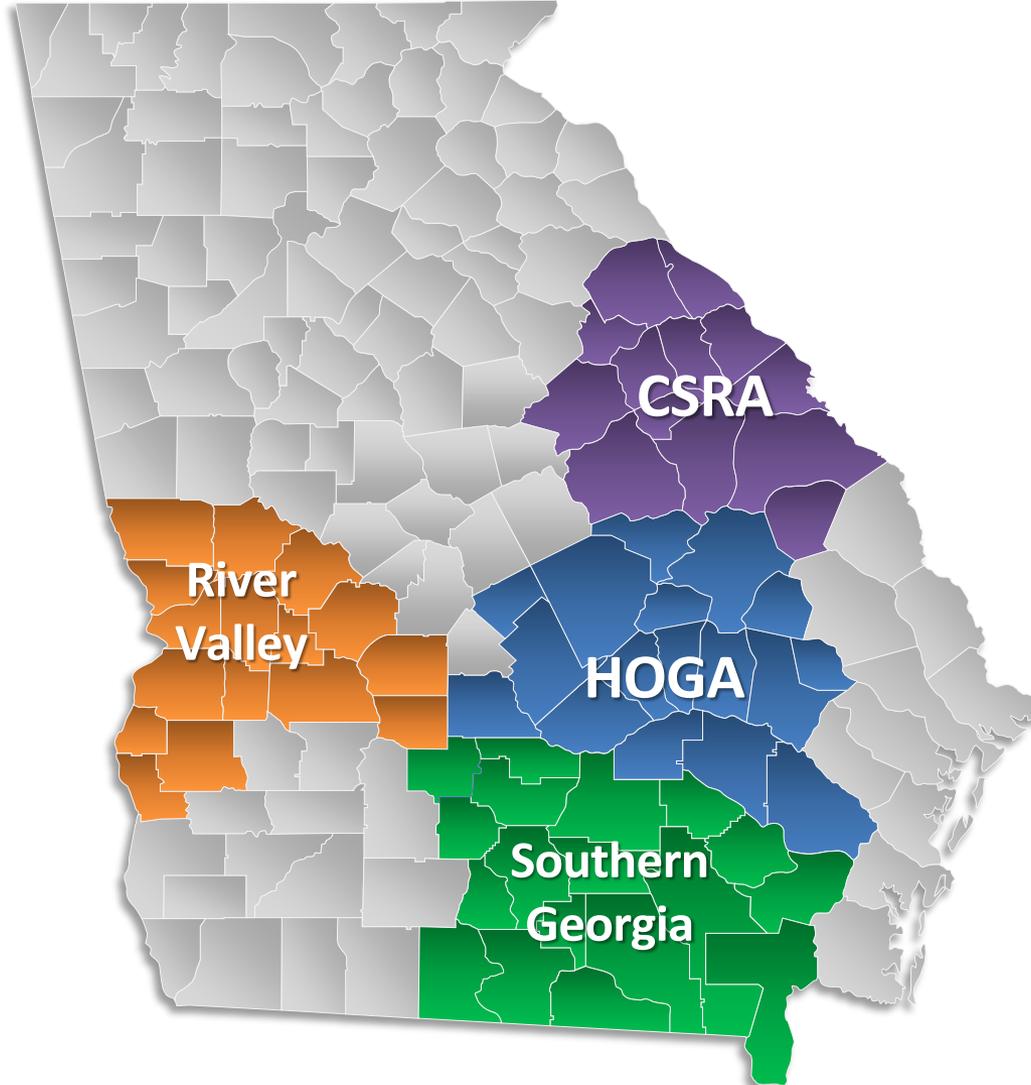

COVID-19 (Coronavirus)

Impacts to the TIA Program



River Valley TIA 2

Projected Timeline

- Regional Roundtable approved the investment list on December 15th, 2021
 - 10-Year Forecast: \$664,868,522
 - 45 Projects
- May 24th, 2022
 - Election Date


TIA Collections Thru February 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$456,337,978	\$342,253,483	\$114,084,495
CSRA	\$663,521,218	\$497,640,913	\$165,880,305
Heart of Georgia	\$296,855,528	\$222,641,646	\$74,213,882
Southern Georgia	\$207,199,058	\$155,399,293	\$51,799,764
Totals	\$1,623,913,781	\$1,217,935,335	\$405,978,446


TIA Collections Thru February 2022

Region	Original Revenue Forecast	Actual Revenue Collected	% Behind Forecast
River Valley	\$539,764,775	\$456,337,978	-15.5%
CSRA	\$763,785,466	\$663,521,218	-13.1%
Heart of Georgia	\$362,061,224	\$296,855,528	-18.0%
Southern Georgia	\$168,394,180	\$207,199,058	23.0%

TIA Timeline

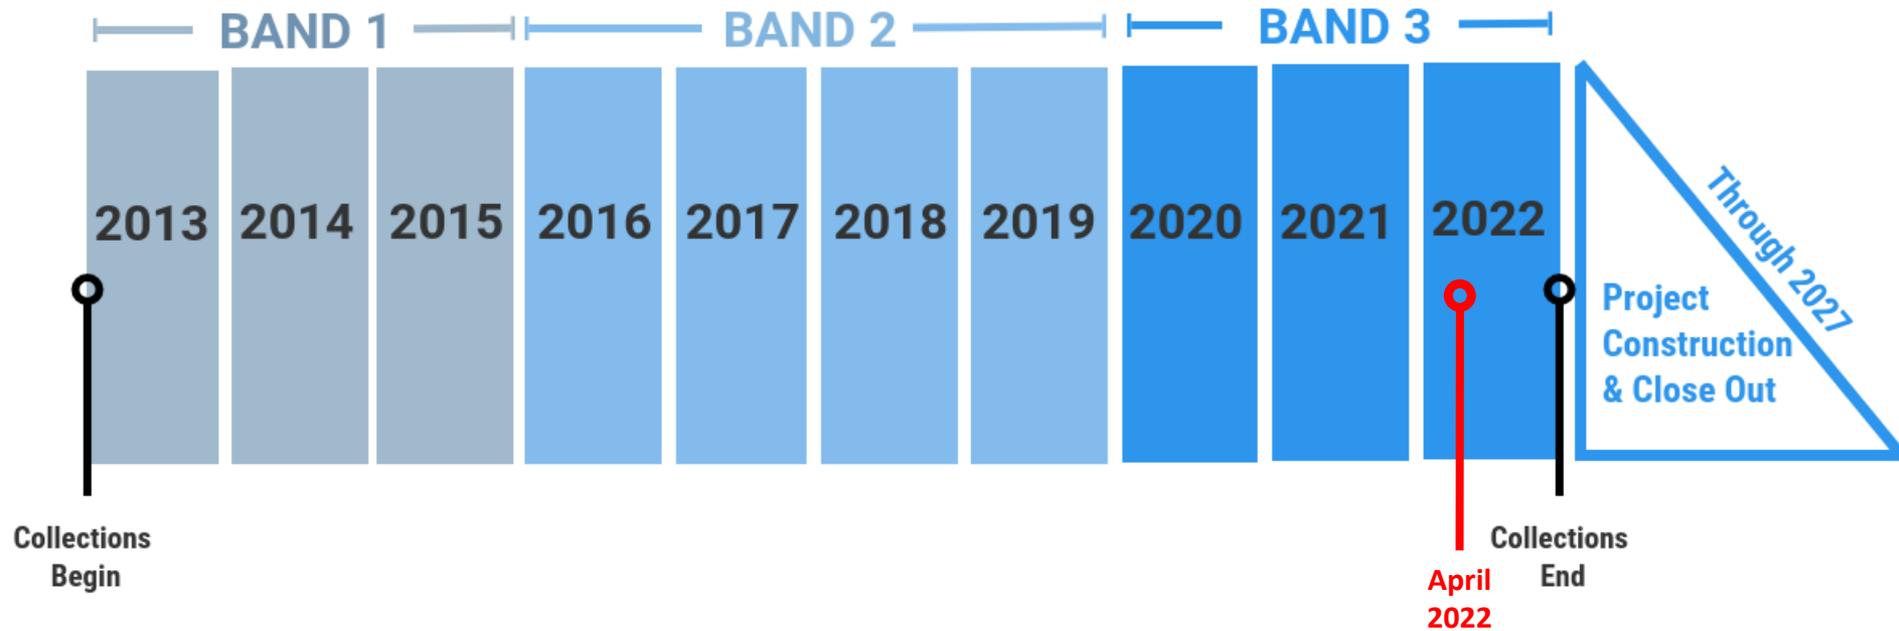

River Valley Project Overview

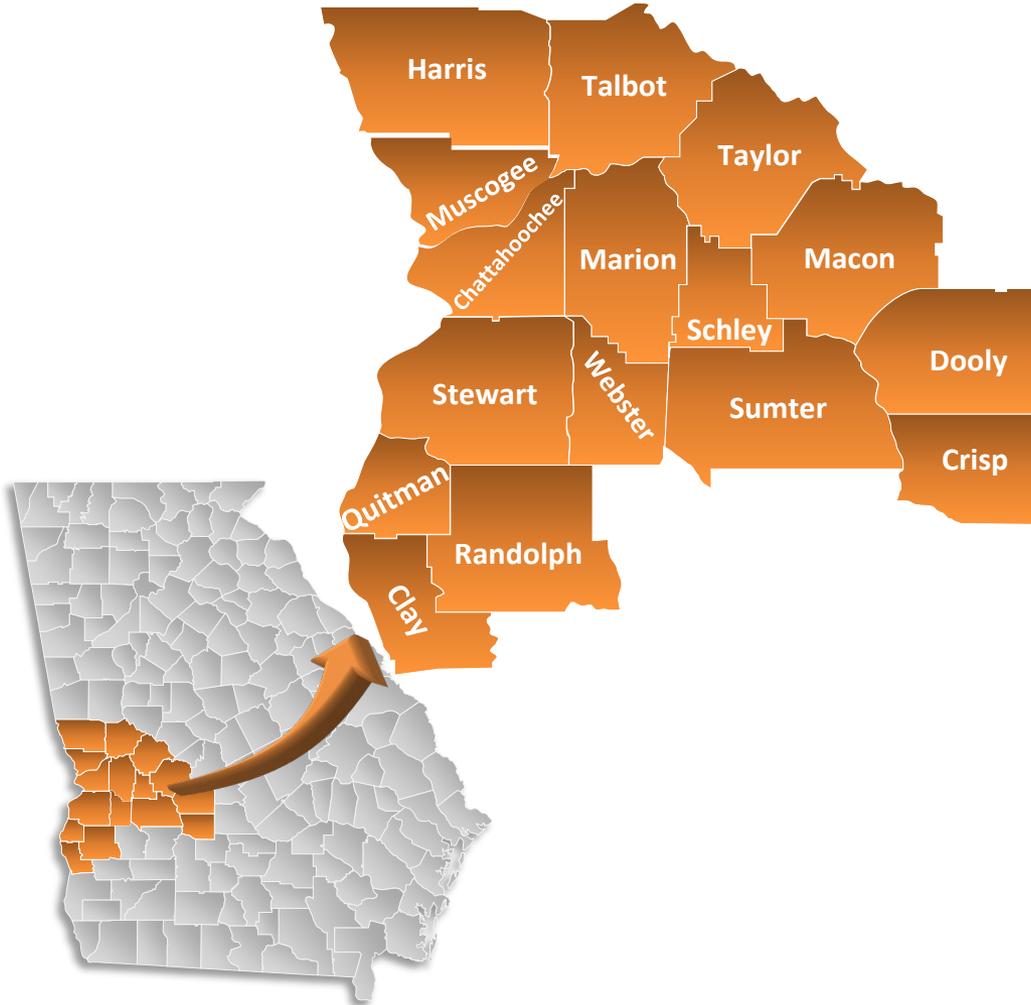

23

Total Projects

\$410,754,730

Final Investment List
Project Total

3

In Construction

17

Projects Completed

\$206,749,218

Total Expenditure to Date
(as of **02/28/2022**)

TIA River Valley Preconstruction Updates

Old Cusseta Rd @ I-185 Interchange (Band 3)

- ROW acquisition underway
- Holding Final Field Plan review this month

US 27 Widening & Roundabout at SR 315 (Band 3)

- ROW acquisition underway
- Holding Final Field Plan review this month
- Letting may shift to end of 2022

TIA River Valley Construction Updates

Buena Vista Road DDI (Band 2)

- CW Matthews was low bidder
 - \$25,629,825
 - May 2020 letting
- Utility relocations in progress
- Walls and bridge in progress

US 280 Widening (Band 3)

- Reeves Construction was the low bidder
 - \$22,878,060
 - August 2020 letting
- Finalizing utility work
- Gum Creek bridge work in progress
- NPS/DNR coordination complete

SR 219 Passing Lanes (Band 2)

- SE Site Development was the low bidder
 - \$11,579,327
 - July 2018 letting
- All lanes open to traffic
- Scheduling final inspection

Buena Vista Rd DDI



Buena Vista Rd DDI



US 280 Widening



US 280 Widening




US 280 Widening



Columbus TIA Project Updates

Spider Web

- Construction split into two phases
- Phase 1 low bid was Robinson Paving
 - \$5,285,606
 - To be completed early/mid 2022
- Phase 2 design plans finalized
- ROW acquisition complete
- Phase 2 to be advertised in 2022

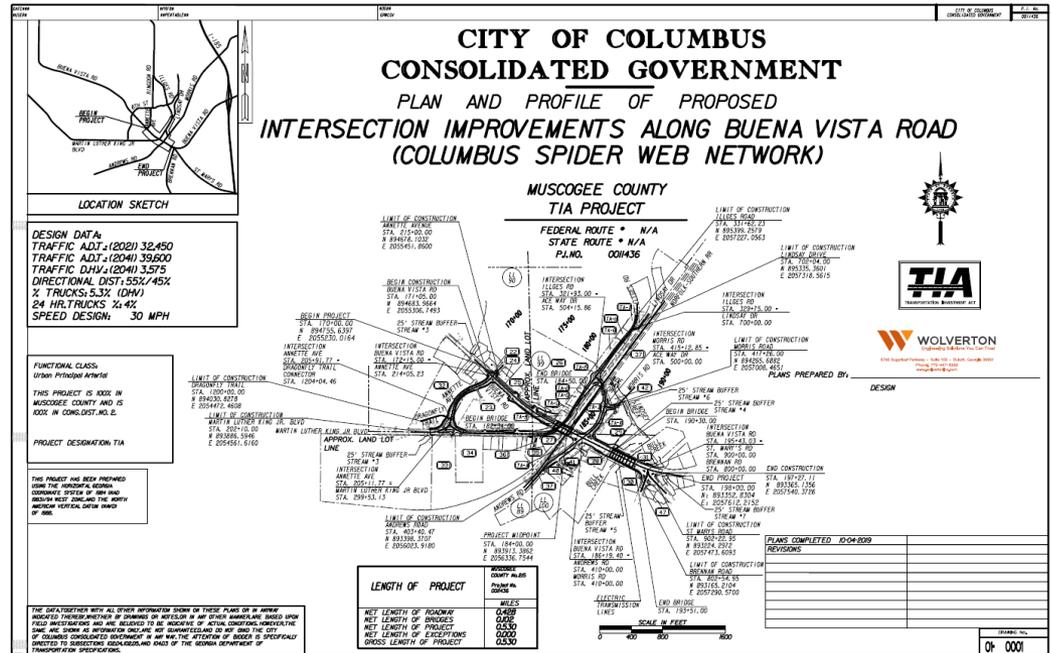

The TIA Office

Kenneth Franks

TIA Administrator
(404) 631-1568
kfranks@dot.ga.gov

Eric Wilkinson

Assistant TIA Administrator
CSRA, HOGA, & SG
(478) 538-8522
ewilkinson@dot.ga.gov

Brent Moseley

TIA Regional Coordinator
SG & HOGA
(912) 661-7157
bmosley@dot.ga.gov

William Eastin

TIA Regional Coordinator
River Valley & SG
(404) 631-1810
weastin@dot.ga.gov

www.ga-tia.com
