

Transportation Investment Act


River Valley 1 CRP Update – December 2, 2025

Kenneth Franks, State TIA Administrator William Eastin, TIA Regional Coordinator





TIA Regions

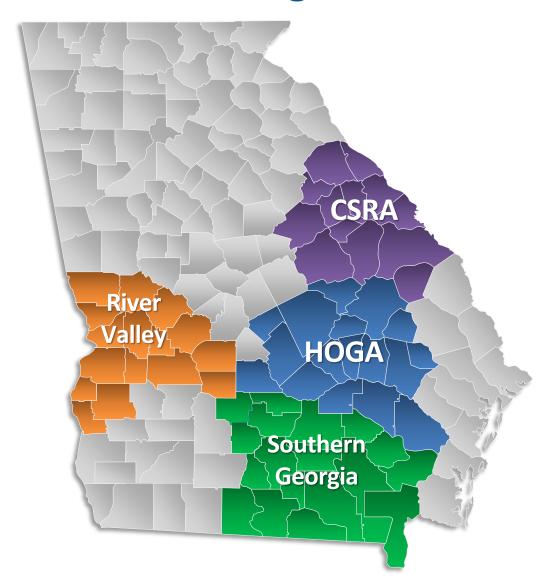





Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$512,301,207	\$384,225,905	\$128,075,302
CSRA	\$746,921,743	\$560,191,307	\$186,730,436
Heart of Georgia	\$335,375,226	\$251,531,419	\$83,843,807
Southern Georgia*	\$489,309,139	\$366,981,854	\$122,327,285
Totals	\$2,083,907,315	\$1,562,930,485	\$520,976,830

^{*}Ongoing Southern Georgia Collections from Oct 2018 to Sept 2025





Final TIA 1 Collections Jan 2013 to Dec 2022


Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$594,061,269	\$512,301,207	-13.8%
CSRA	\$841,044,916	\$746,921,743	-11.2%
Heart of Georgia	\$398,870,417	\$335,375,226	-15.9%
Southern Georgia*	\$353,807,727	\$489,309,139	38.3%

^{*}Ongoing Southern Georgia Collections from Oct 2018 to Sept 2025





TIA 1 Timeline

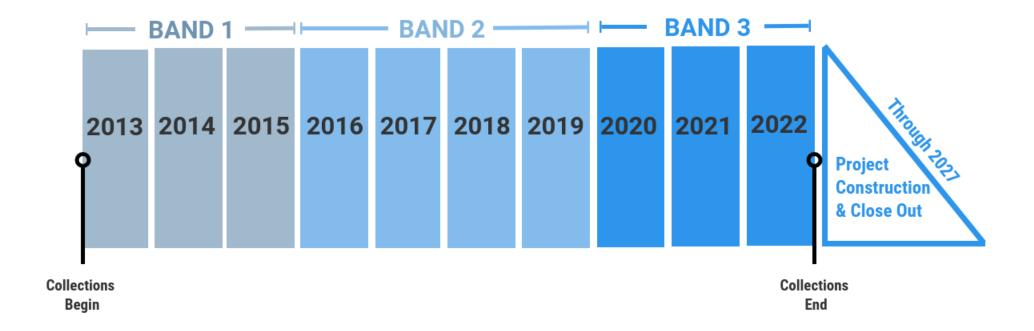





River Valley Project Overview



23

Total Projects

\$410,754,730

Final Investment List Project Total

4

In Construction

1

Operations Project

18

Projects Completed

\$331,838,134

Total Expenditure to Date (as of Nov 26, 2025)





River Valley – TIA 1 Construction Updates

US 27 Widening & Roundabout at SR 315 (Band 3)

- Robinson Paving 12/2022 letting
- Grading, and utility relocations ongoing
- Working staging for side road work
- Working on base and drainage for new roundabout
- Paving plan revision underway

Buena Vista Road DDI (Band 2)

- CW Matthews 9/2020 letting
- Ramp paving underway
- Working GAB, C&G, and sidewalk
- Proceeding with interchange landscaping
- Contractor granted 6 month time extension

Old Cusseta Rd @ I-185 Interchange (Band 3)

- Robinson Paving 9/2022 letting
- Paving of Cusseta Rd underway
- Drainage structure and wall work continues
- Bridge painting underway





Old Cusseta Rd Interchange







Old Cusseta Rd Interchange





Old Cusseta Rd Interchange





US 27 Widening







US 27 Widening







Columbus TIA Project Updates

Spider Web

- Construction split into two phases
- Phase 2 Closure starting 4/8
 - 2 year construction contract

METRA

- Operations and maintenance ongoing
- Park and Ride facility complete.
- New agreement executed







Spiderweb





Spiderweb







Transportation Investment Act


River Valley 2 CRP Update – December 2, 2025

Kenneth Franks, State TIA Administrator William Eastin, TIA Regional Coordinator





TIA Regions

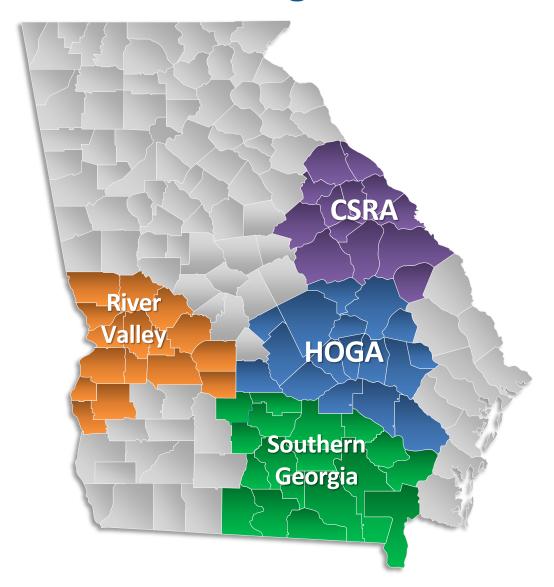





TIA 2 Collections Jan 2023 to Sept 2025

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$192,363,198	\$144,272,398	\$48,090,800
CSRA	\$300,769,101	\$225,576,826	\$75,192,275
Heart of Georgia	\$138,738,300	\$104,053,725	\$34,684,575
Totals	\$631,870,599	\$473,902,949	\$157,967,650





TIA 2 Collections Jan 2023 to Sept 2025

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$165,016,955	\$192,363,198	16.6%
CSRA	\$233,543,282	\$300,769,101	28.8%
Heart of Georgia	\$98,806,789	\$138,738,300	40.4%





River Valley 2 Project Overview



45

Total Projects

\$399,860,962

Final Investment List Project Total

31

In Planning and Design

4

In Construction

4

Projects Completed


\$27,224,249

Total Expenditure to Date (as of Nov 26, 2025)





TIA 2 Timeline

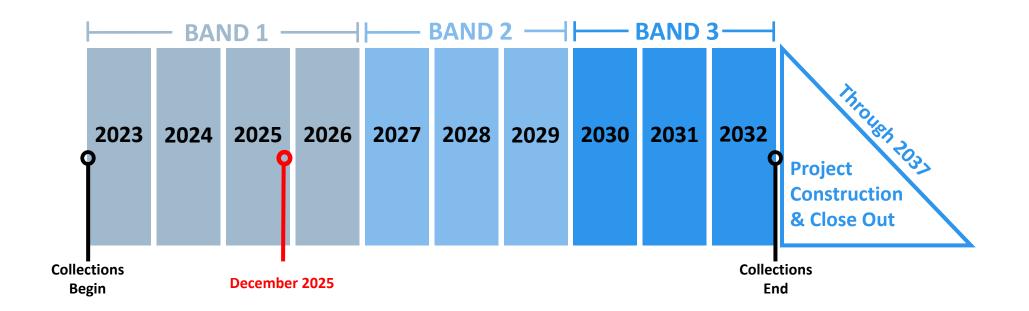





River Valley - TIA 2 (2023-2032) Resurfacing Updates

Quitman County


- Lower Lumpkin Rd (June 2024 Let)
 - Striping and grassing complete
 - Final inspection this month

Clay and Randolph Counties

- Cotton Hill Rd (December 2024 Let)
 - Oxford To begin Sept/Oct

Dooly and Crisp Counties

- Coney Rd (December 2025 Let)
 - Currently advertised

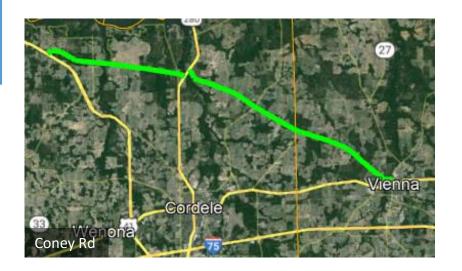





River Valley - TIA 2 (2023-2032) Preconstruction Updates

Concept Development

Harris County

- SR 315 from Hart Dr to Hamilton,
 Mulberry Grove Rd Improvements
- SR 315 @ SR 219 Intersection Improvements

Muscogee County

- Buena Vista Road Improvements
 - Concept Development
- University Ave Road Diet / Streetscape
 - Concept Development
- 2nd Ave Improvements
 - Concept Development





River Valley - TIA 2 (2023-2032) Preconstruction Updates

Schley and Webster Counties
Churchill Rd and SR 153 Bridges (Band 1)

ROW process and final design underway

Marion County
Buena Vista Downtown Improvements –
Band 1

- Working on final plans and ROW
- Letting March 2026


Muscogee County
Williams Rd and Cusseta Rd –
Band 3

• Finalizing contracts with both design firms





US 280 Corridor

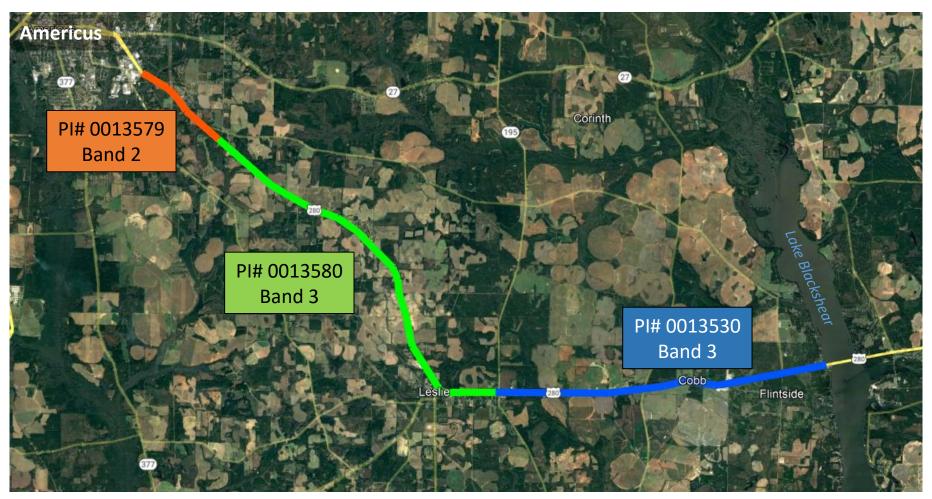





River Valley - TIA 2 (2023-2032) US 280 Preconstruction Updates

US 280 widening from Felder Street to District Line Rd - Band 2

Working on Preliminary Plans

US 280 widening from District Line Rd to SR 195 - Band 3

- Working on concept
- Environmental screening
- PIOH 8/21 in Leslie

US 280 widening from SR 195 to Lake Blackshear - Band 3

- Working on concept
- Environmental screening
- PIOH 8/21 in Leslie





Lower Lumpkin Rd – Quitman County







Chalybeate Springs Road – Talbot County





River Valley - TIA 2 (2023-2032) Local Delivery Updates

Montezuma Airport

- Final plans near complete
 Pave Rustin Lake Rd Taylor County
- Final plans near complete
 Man O' War Trail Harris County
- Agreement executed, working on design

Muscogee County

- Steam Mill Rd
- Columbus Airport
- 5th Ave Trail
- Columbus River Walk
- Liberty Theater Enhancement
- South Lumpkin Rd Streetscape
- Whitesville Rd
- 13th Ave Roundabout
- Morris Rd
- Forrest Rd
- METRA



The TIA Office

Kenneth Franks

TIA Administrator (404) 631-1568

kfranks@dot.ga.gov

Eric Wilkinson

Assistant TIA Administrator (478) 538-8522

ewilkinson@dot.ga.gov

Jeramy Durrence

TIA Regional Coordinator CSRA, HOGA, & SG (404)694-6545 jdurrence@dot.ga.gov **Brent Moseley**

TIA Regional Coordinator SG & HOGA (912) 661-7157 bmoseley@dot.ga.gov William Eastin

TIA Regional Coordinator River Valley & SG (404) 904-4204

weastin@dot.ga.gov

www.ga-tia.com

