



Georgia Department of Transportation


Transportation Investment Act

River Valley 1 CRP Update – April 8, 2025

Kenneth Franks, State TIA Administrator
William Eastin, TIA Regional Coordinator



TIA Regions

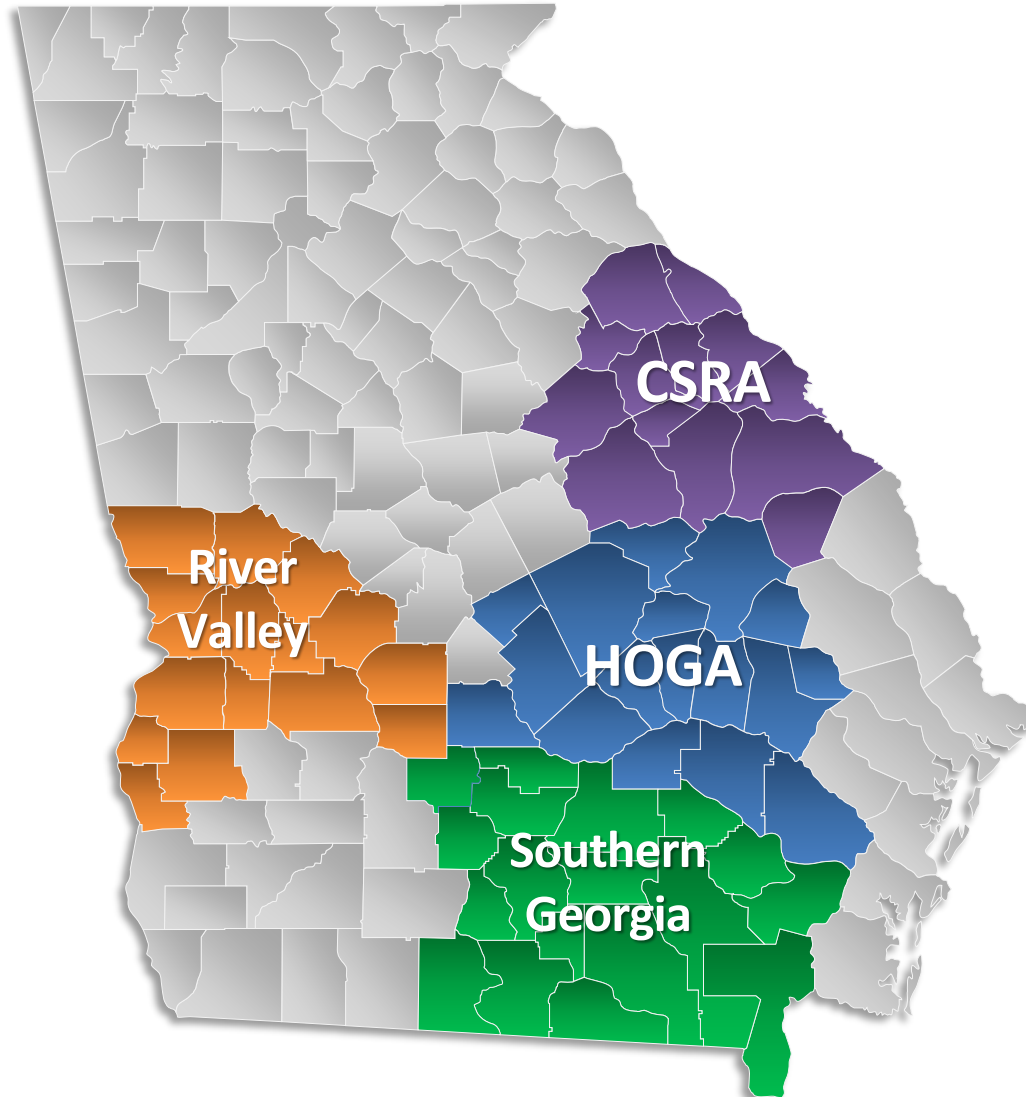

Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$512,301,207	\$384,225,905	\$128,075,302
CSRA	\$746,921,743	\$560,191,307	\$186,730,436
Heart of Georgia	\$335,375,226	\$251,531,419	\$83,843,807
Southern Georgia*	\$432,551,392	\$324,413,544	\$108,137,848
Totals	\$2,027,149,568	\$1,520,362,175	\$506,787,393


*Ongoing Southern Georgia Collections from Oct 2018 to Jan 2025

Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$594,061,269	\$512,301,207	-13.8%
CSRA	\$841,044,916	\$746,921,743	-11.2%
Heart of Georgia	\$398,870,417	\$335,375,226	-15.9%
Southern Georgia*	\$318,849,519	\$432,551,392	35.7%

*Ongoing Southern Georgia Collections from Oct 2018 to Jan 2025

TIA 1 Timeline

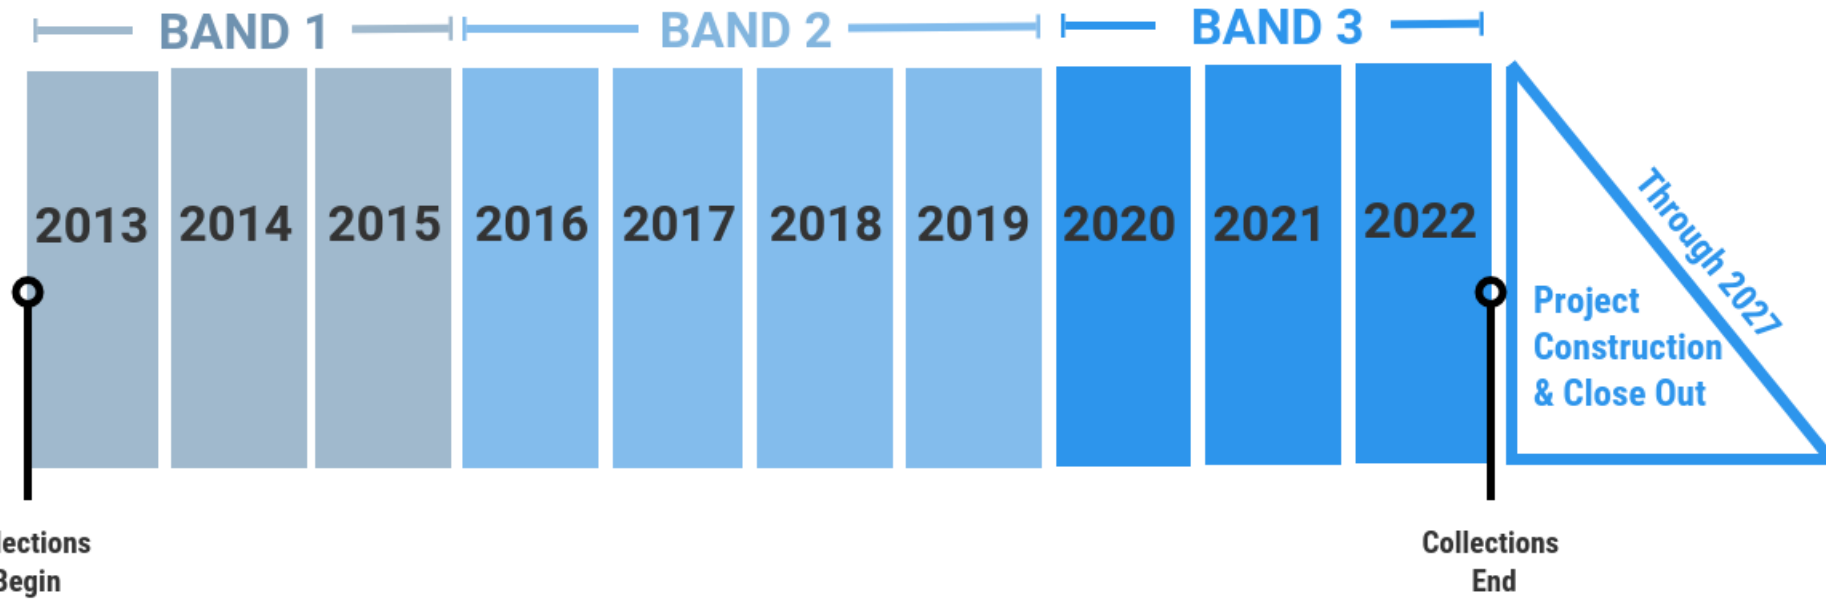

River Valley Project Overview



23

Total Projects

\$410,754,730

Final Investment List
Project Total

4

In Construction

1

Operations Project

18

Projects Completed

\$311,187,903

Total Expenditure to Date
(as of **April 7, 2025**)

River Valley – TIA 1 Construction Updates

US 27 Widening & Roundabout at SR 315 (Band 3)

- Robinson Paving – 12/2022 letting
- ROW acquisition complete
- Clearing, grading, and utility relocations ongoing
- Culverts complete

Buena Vista Road DDI (Band 2)

- CW Matthews – 9/2020 letting
- Bridge work continues
 - Pouring deck in next couple weeks
- Ramp paving and curb and gutter work continues

Old Cusseta Rd @ I-185 Interchange (Band 3)

- Robinson Paving – 9/2022 letting
- Utility relocations ongoing (W/S, gas, and telecom)
- Removing sound barrier and will start bridge work.

US 280 Widening (Band 3)

- Reeves Construction – 8/2020 letting
- Complete and open to traffic

Buena Vista Road DDI



Buena Vista Road DDI



Old Cusseta Rd Interchange



Old Cusseta Rd Interchange



Old Cusseta Rd Interchange



Aerial from early April

Image © 2024 Airbus

US 280 Widening



Complete

US 27 Widening



US 27 Widening



Columbus TIA Project Updates

Spider Web

- Construction split into two phases
- Phase 2 Closure starting 4/8
 - 2 year construction contract

METRA

- Operations and maintenance ongoing
- Park and Ride facility complete.
- New agreement executed






Transportation Investment Act

River Valley 2 CRP Update – April 8, 2025

Kenneth Franks, State TIA Administrator
William Eastin, TIA Regional Coordinator



TIA Regions

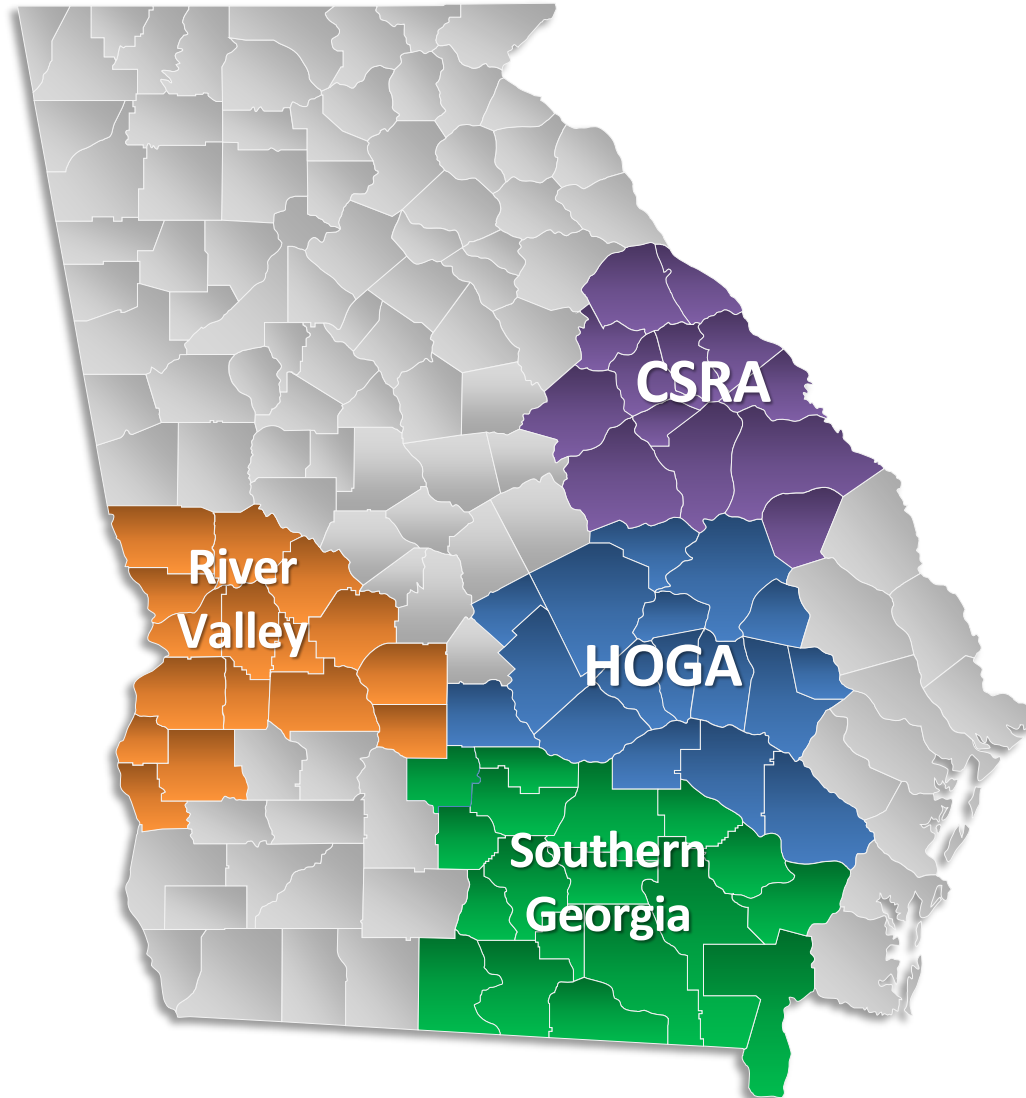


TIA 2 Collections Jan 2023 to Feb 2025

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$150,287,712	\$112,715,784	\$37,571,928
CSRA	\$233,132,307	\$174,849,230	\$58,283,077
Heart of Georgia	\$107,233,620	\$80,425,215	\$26,808,405
Totals	\$490,653,639	\$367,990,229	\$122,663,410

TIA 2 Collections Jan 2023 to Feb 2025

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$129,030,957	\$150,287,712	16.5%
CSRA	\$181,152,375	\$233,132,307	28.7%
Heart of Georgia	\$78,171,205	\$107,233,620	37.2%

River Valley 2 Project Overview

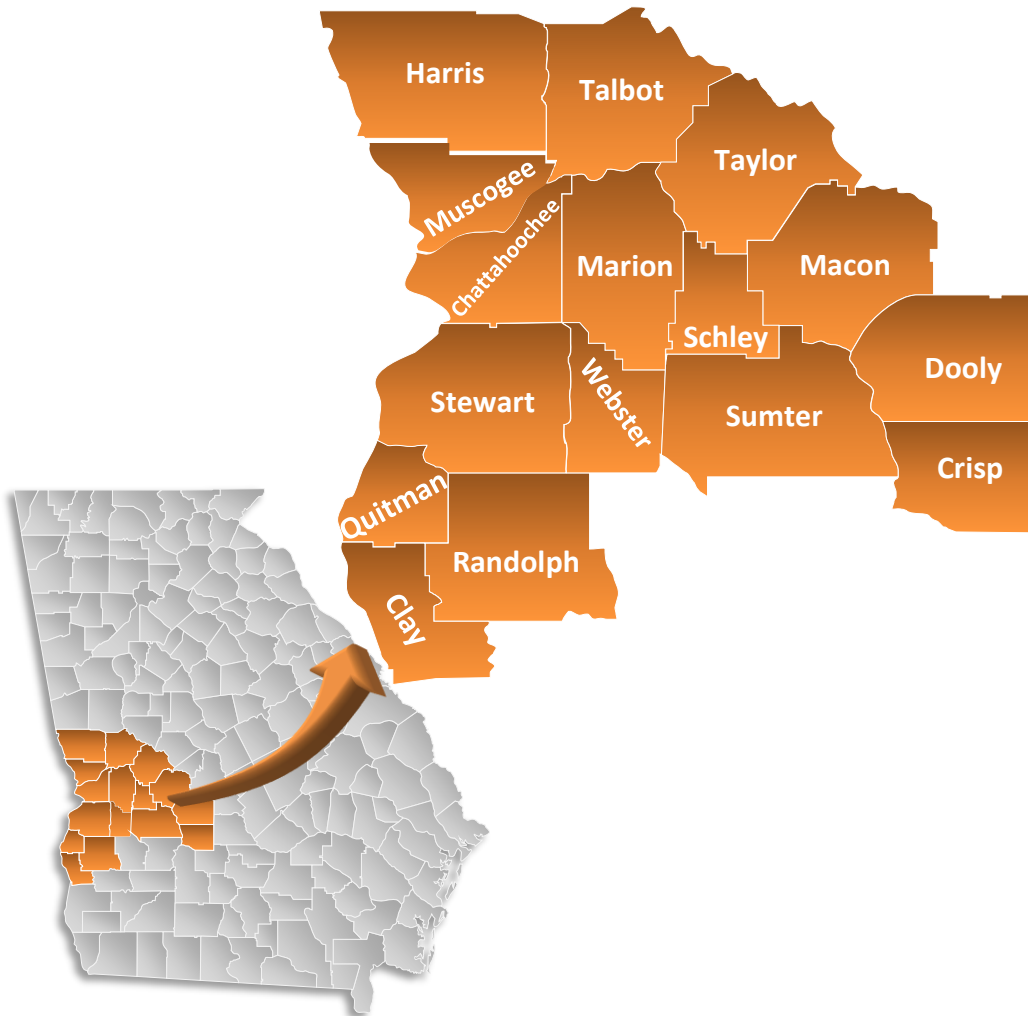

45

Total Projects

\$399,860,962

Final Investment List
Project Total

29

In Planning and Design

4

In Construction


1

Projects Completed

\$16,972,662

Total Expenditure to Date
(as of **April 7, 2025**)

TIA 2 Timeline

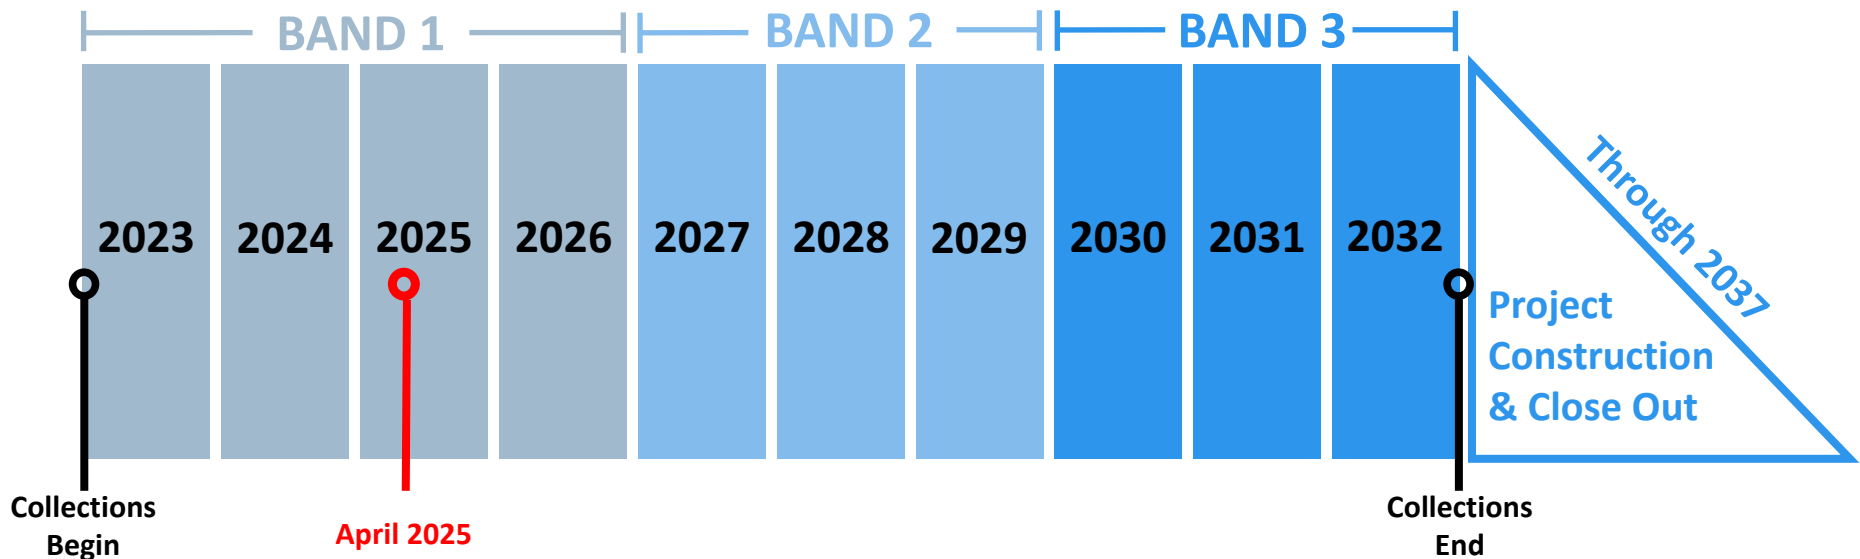

River Valley - TIA 2 (2023-2032)

Resurfacing Updates

Talbot County

- **Chalybeate Springs Rd (March 2024 Let)**
 - Robinson Paving
 - 98% - held final inspection

Quitman County


- **Lower Lumpkin Rd (June 2024 Let)**
 - Oxford – To begin this month

Clay and Randolph Counties

- **Cotton Hill Rd (December 2024 Let)**
 - Oxford – To begin this Summer

Dooly and Crisp Counties

- **Coney Rd (December 2026 Let)**
 - Four sections from Cotton St in Vienna to SR 300 in Crisp County

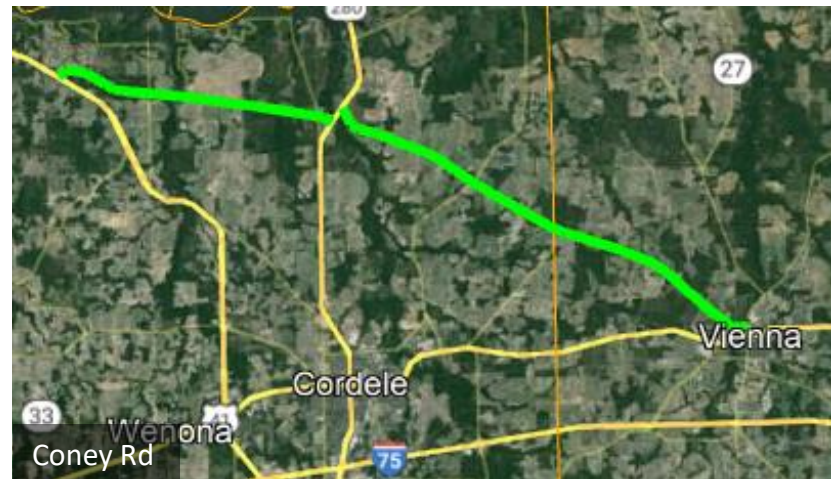

River Valley - TIA 2 (2023-2032)

Preconstruction Updates

Concept Development

Harris County

- SR 315 from Hart Dr to Hamilton, Mulberry Grove Rd Improvements
- SR 315 @ SR 219 Intersection Improvements

Chattahoochee/Marion Counties

- SR 26 Passing Lanes

Randolph/Quitman Counties

- US 82 Passing Lanes

Muscogee County

- Buena Vista Road Improvements
- Manchester Expy/US 27 Alt @ County Line Rd Interchange Reconstruction
- Andrews Road Improvements
- Brennan Road Improvements
- US 80 Ramp Improvements
- University Ave Road Diet / Streetscape
- 2nd Ave Improvements

River Valley - TIA 2 (2023-2032)

Preconstruction Updates

Schley and Webster Counties

Churchill Rd and SR 153 Bridges (Band 1)

- ROW process underway
- Design underway

Marion County

Buena Vista Downtown Improvements – Band 1


- Working on final plans
- Letting Jan 2026

Harris County

Manchester Expy @ Central Church Rd - Band 1

- Working on Final Plans
- Letting July 2025

US 280 Corridor

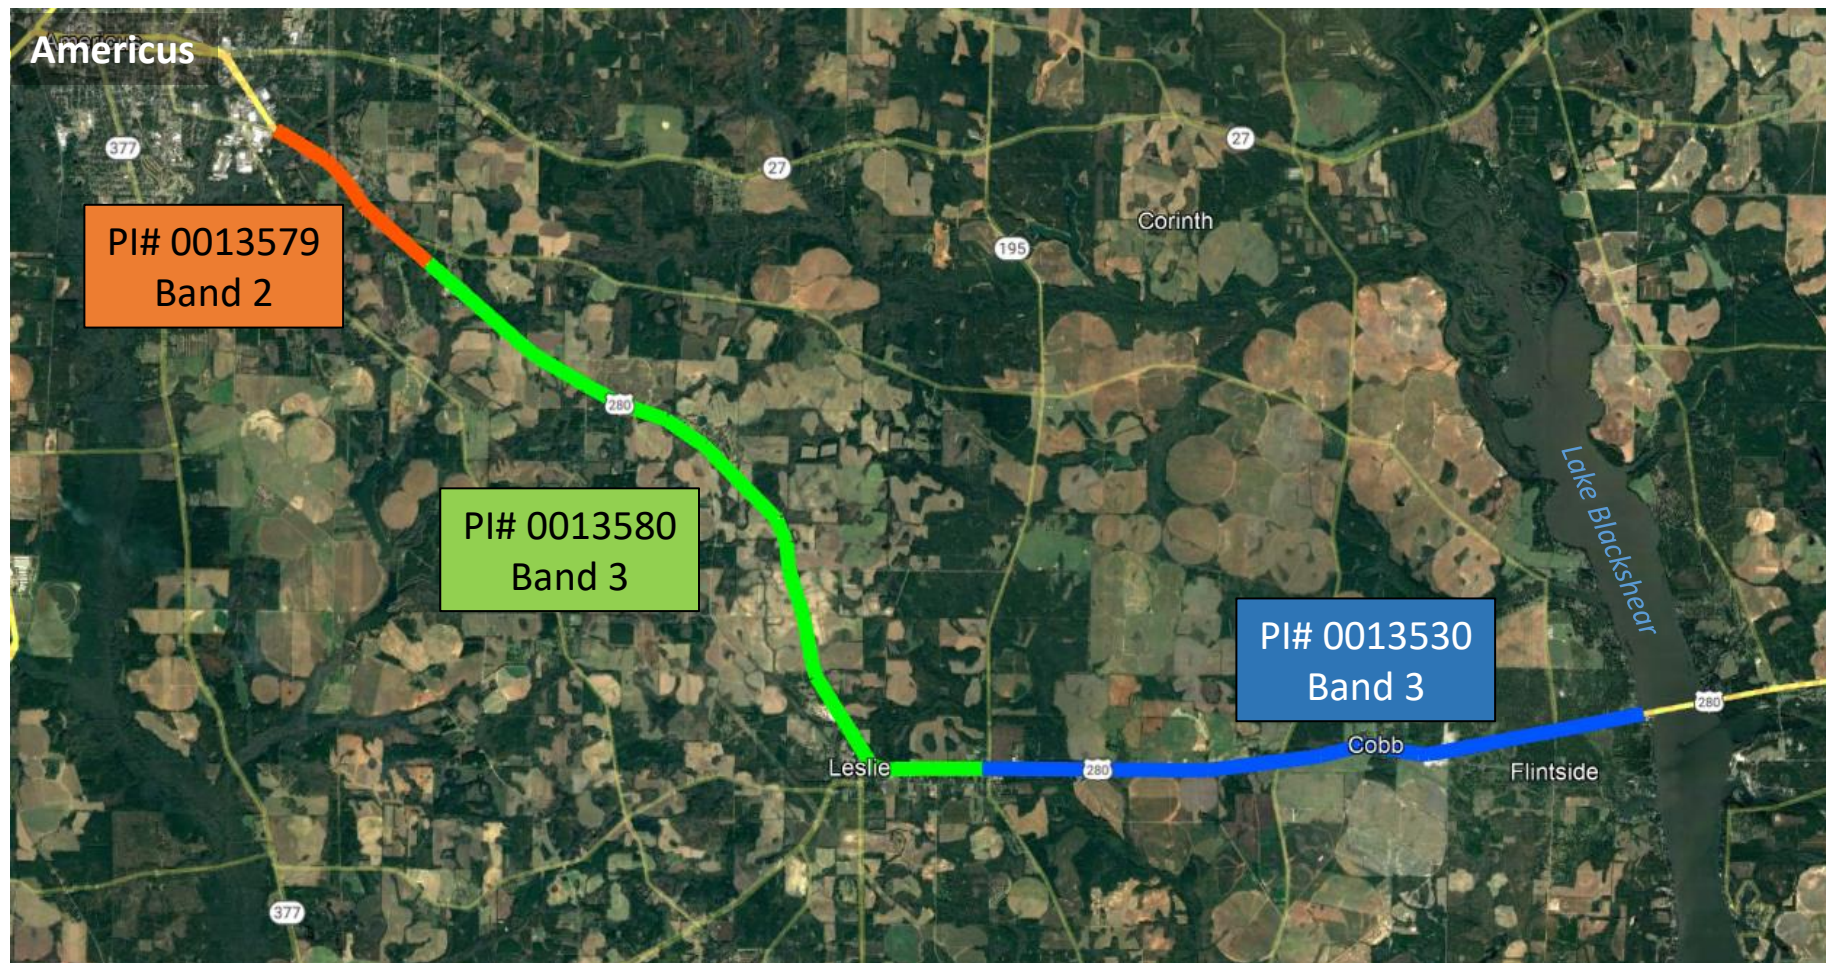

River Valley - TIA 2 (2023-2032)

US 280 Preconstruction Updates

US 280 widening from Felder Street to District Line Rd - Band 2

- Working on environmental doc (NELT)
 - Approved Jan 2025
 - Working on Preliminary Plans

US 280 widening from District Line Rd to SR 195 - Band 3

- Working on concept
- Environmental screening
- PIOH this Summer

US 280 widening from SR 195 to Lake Blackshear (Band 3)

- Working on concept
- Environmental screening
- PIOH this Summer

River Valley - TIA 2 (2023-2032)

Local Let Projects

Columbus

- Steam Mill Rd
- Whitesville Road Widening
- Columbus River Walk Repaving and Maintenance
- South Lumpkin Rd Streetscape
- 13th Ave/17th St/Linwood Blvd Intersection Improvements
- Liberty Theater Block Enhancement
- 5th Avenue Trail Connector
- Morris Rd
- Forrest Rd

Macon County Buck Creek Bypass

- Construction complete

Montezuma Airport

- Working on bid package

Taylor County

- Ed Davis Rd/Rustin Lake Rd
- Finalizing bid package

Stewart County

- Hospital Rd - Oxford Construction
 - 70% complete

Hospital Rd – Stewart County



Chalybeate Springs Rd – Talbot County



The TIA Office

Kenneth Franks

TIA Administrator

(404) 631-1568

kfranks@dot.ga.gov

Eric Wilkinson

Assistant TIA

Administrator

(478) 538-8522

ewilkinson@dot.ga.gov

Jeramy Durrence

TIA Regional Coordinator

CSRA, HOGA, & SG

(404)694-6545

jdurrence@dot.ga.gov

Brent Moseley

TIA Regional Coordinator

SG & HOGA

(912) 661-7157

bmoseley@dot.ga.gov

William Eastin

TIA Regional Coordinator

River Valley & SG

(404) 904-4204

weastin@dot.ga.gov

www.ga-tia.com
