




Transportation Investment Act

River Valley 1 CRP Update – August 11, 2025

Kenneth Franks, State TIA Administrator
William Eastin, TIA Regional Coordinator



TIA Regions

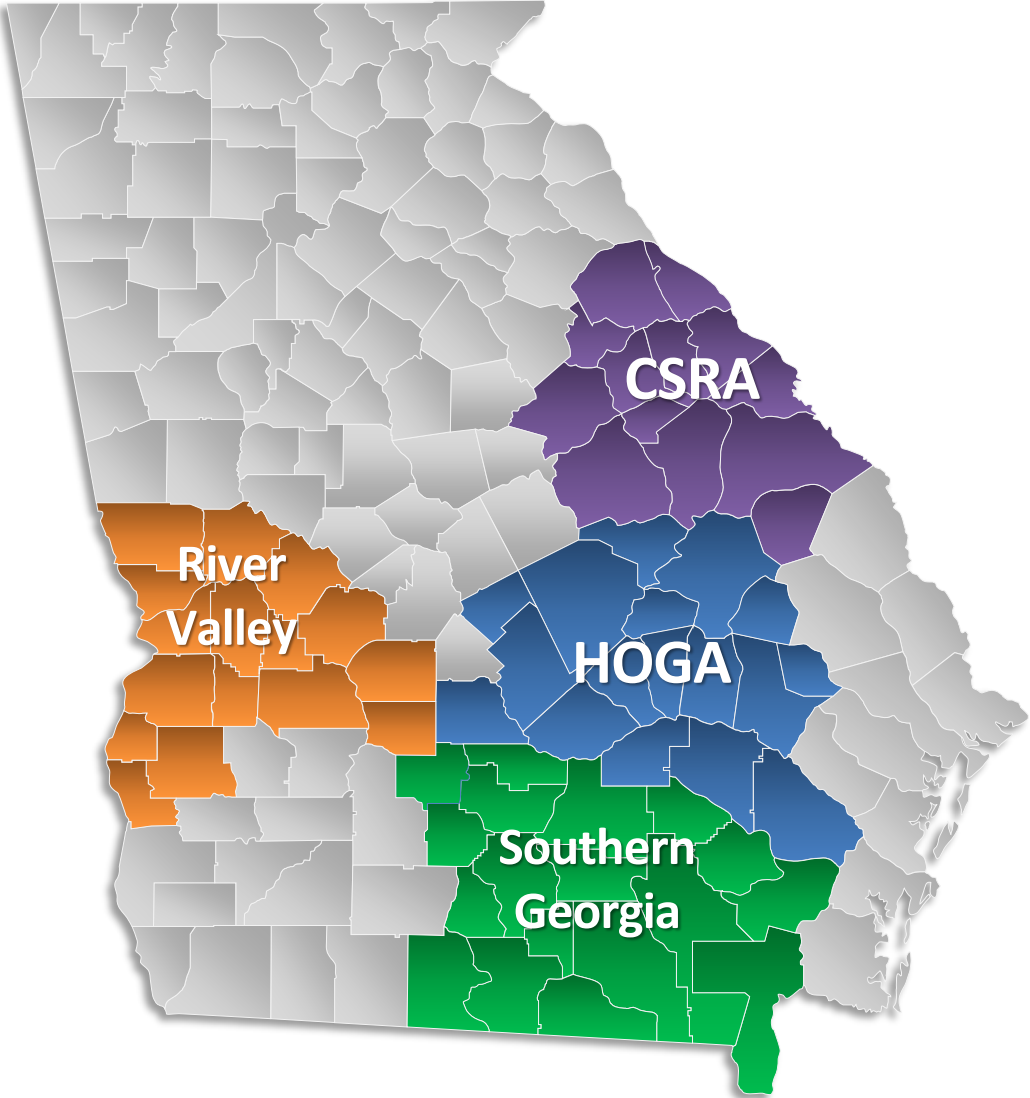

Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$512,301,207	\$384,225,905	\$128,075,302
CSRA	\$746,921,743	\$560,191,307	\$186,730,436
Heart of Georgia	\$335,375,226	\$251,531,419	\$83,843,807
Southern Georgia*	\$460,930,961	\$345,698,221	\$115,232,740
Totals	\$2,055,529,137	\$1,541,646,852	\$513,882,285


*Ongoing Southern Georgia Collections from Oct 2018 to May 2025

Final TIA 1 Collections Jan 2013 to Dec 2022

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$594,061,269	\$512,301,207	-13.8%
CSRA	\$841,044,916	\$746,921,743	-11.2%
Heart of Georgia	\$398,870,417	\$335,375,226	-15.9%
Southern Georgia*	\$340,561,841	\$460,930,961	35.3%

*Ongoing Southern Georgia Collections from Oct 2018 to May 2025

TIA 1 Timeline

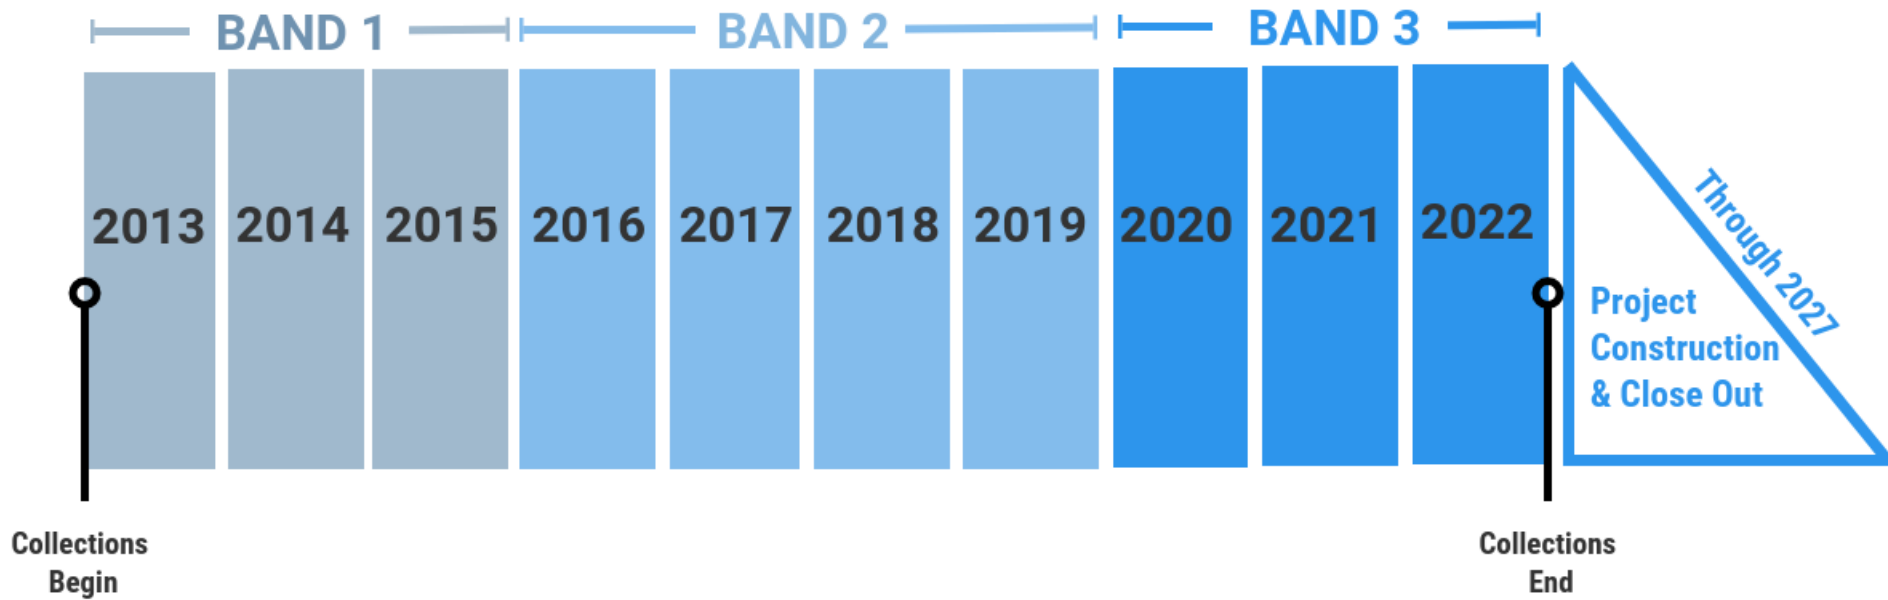

River Valley Project Overview



23

Total Projects

\$410,754,730

Final Investment List
Project Total

4

In Construction

1

Operations Project

18

Projects Completed

\$323,110,900

Total Expenditure to Date
(as of **Aug 7, 2025**)

River Valley – TIA 1 Construction Updates

US 27 Widening & Roundabout at SR 315 (Band 3)

- Robinson Paving – 12/2022 letting
- Grading, and utility relocations ongoing
- Staring base installation on south side
- Storm drain work ongoing
- Paving plan revision underway

Buena Vista Road DDI (Band 2)

- CW Matthews – 9/2020 letting
- Wall design work on the interstate median
- Working on storm drains, C&G, and sidewalk
- Contractor requested time and cost

Old Cusseta Rd @ I-185 Interchange (Band 3)

- Robinson Paving – 9/2022 letting
- Utility relocations and storm drain work ongoing
- Bridge beam setting and paving of Old Cusseta Rd this month

Buena Vista Road DDI



Buena Vista Road DDI



Old Cusseta Rd Interchange



Old Cusseta Rd Interchange



US 27 Widening



US 27 Widening



Columbus TIA Project Updates

Spider Web

- Construction split into two phases
- Phase 2 Closure starting 4/8
 - 2 year construction contract

METRA

- Operations and maintenance ongoing
- Park and Ride facility complete.
- New agreement executed



Spiderweb






Transportation Investment Act

River Valley 2 CRP Update – August 11, 2025

Kenneth Franks, State TIA Administrator
William Eastin, TIA Regional Coordinator



TIA Regions

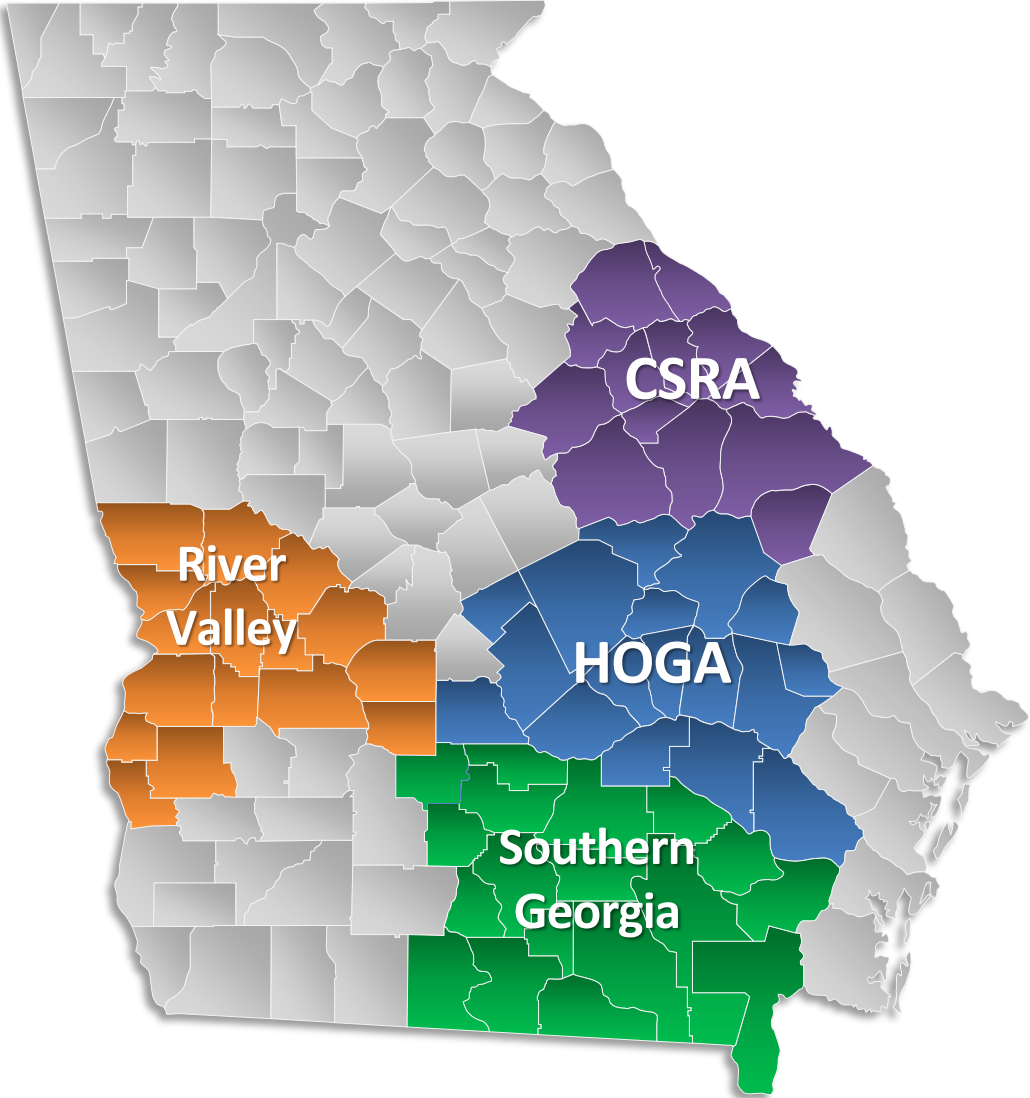

TIA 2 Collections Jan 2023 to June 2025

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
River Valley	\$174,392,106	\$130,794,080	\$43,598,027
CSRA	\$272,207,711	\$204,155,783	\$68,051,928
Heart of Georgia	\$125,368,853	\$94,026,640	\$31,342,213
Totals	\$571,968,670	\$428,976,503	\$142,992,168

TIA 2 Collections Jan 2023 to Feb 2025

Region	Original Revenue Forecast	Actual Revenue Collected	% of Original Forecast
River Valley	\$149,331,689	\$174,392,106	16.78%
CSRA	\$211,745,584	\$272,207,711	28.55%
Heart of Georgia	\$89,898,074	\$125,368,853	39.46%

River Valley 2 Project Overview



45

Total Projects

\$399,860,962

Final Investment List

Project Total

33

In Planning and Design

4

In Construction

3


Projects Completed

\$22,837,069

Total Expenditure to Date

(as of **August 7, 2025**)

TIA 2 Timeline

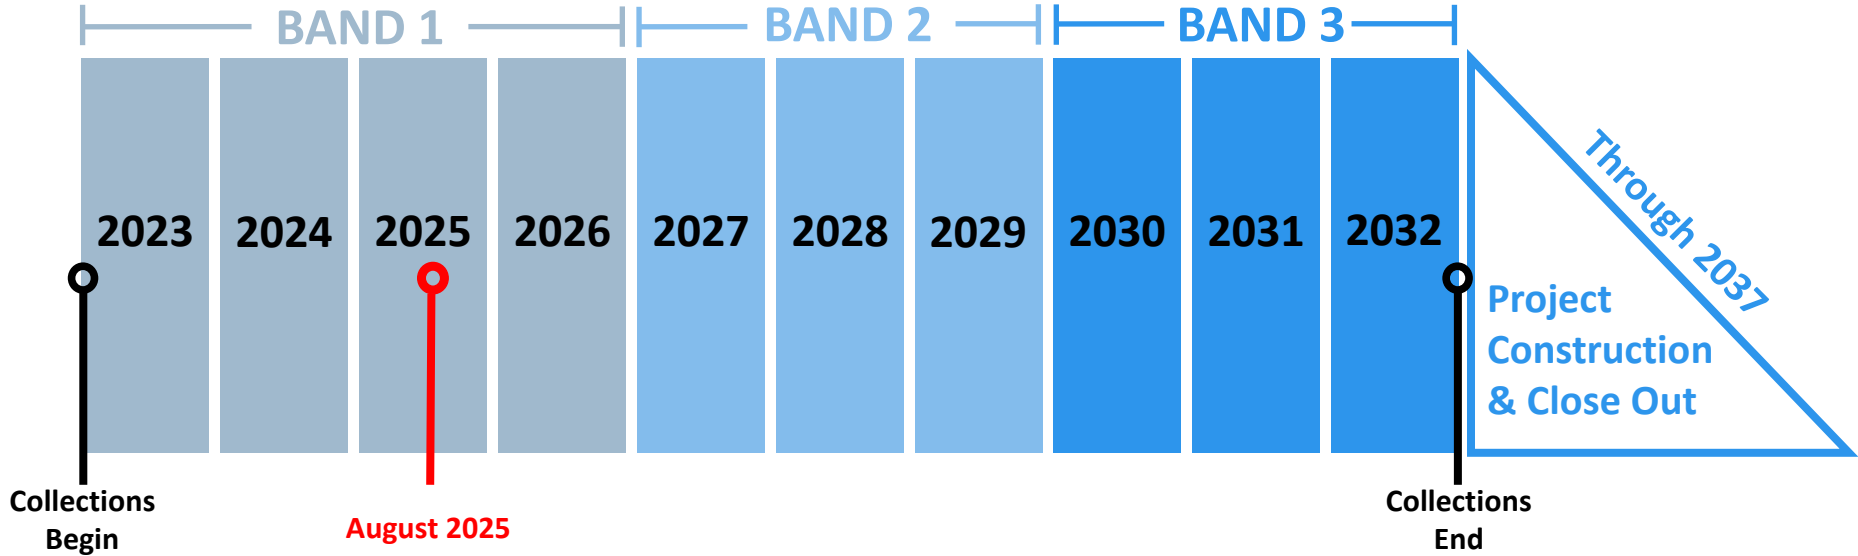

River Valley - TIA 2 (2023-2032)

Resurfacing Updates

Talbot County

- Chalybeate Springs Rd (March 2024 Let)
 - Complete

Quitman County


- Lower Lumpkin Rd (June 2024 Let)
 - Striping and grassing complete
 - Final inspection this month

Clay and Randolph Counties

- Cotton Hill Rd (December 2024 Let)
 - Oxford – To begin Sept/Oct

Dooly and Crisp Counties

- Coney Rd (December 2025 Let)
 - Preparing plan package

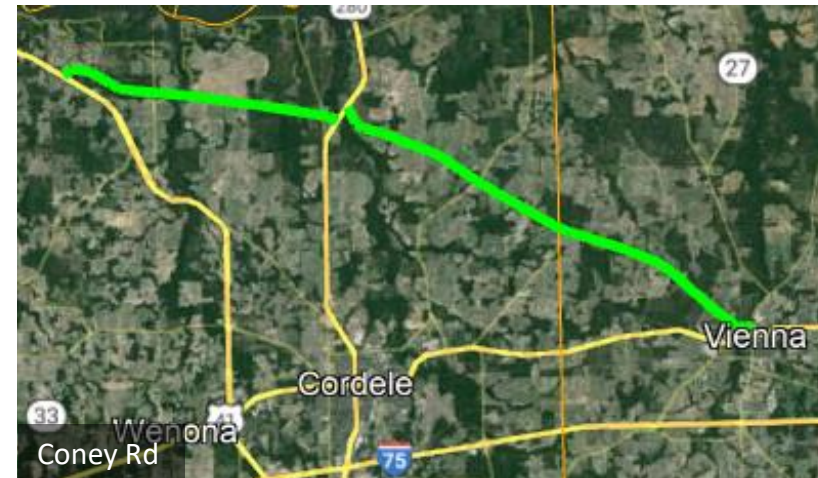

River Valley - TIA 2 (2023-2032)

Preconstruction Updates

Concept Development

Harris County

- SR 315 from Hart Dr to Hamilton, Mulberry Grove Rd Improvements
- SR 315 @ SR 219 Intersection Improvements
 - Public Meeting this Thursday 8/14 at Creekside School

Muscogee County

- Buena Vista Road Improvements
 - Concept Development
- University Ave Road Diet / Streetscape
 - Concept Development
- 2nd Ave Improvements
 - Concept Development

River Valley - TIA 2 (2023-2032)

Preconstruction Updates

Schley and Webster Counties Churchill Rd and SR 153 Bridges (Band 1)

- ROW process and final design underway

Harris County Manchester Expy @ Central Church Rd - Band 1

- Let July 2025
 - Low bid – Piedmont Paving
 - \$360,474.51


Marion County Buena Vista Downtown Improvements – Band 1

- Working on final plans and ROW
- Letting Jan 2026

Muscogee County Williams Rd and Cusseta Rd – Band 3

- Phase 2 design procurement

US 280 Corridor

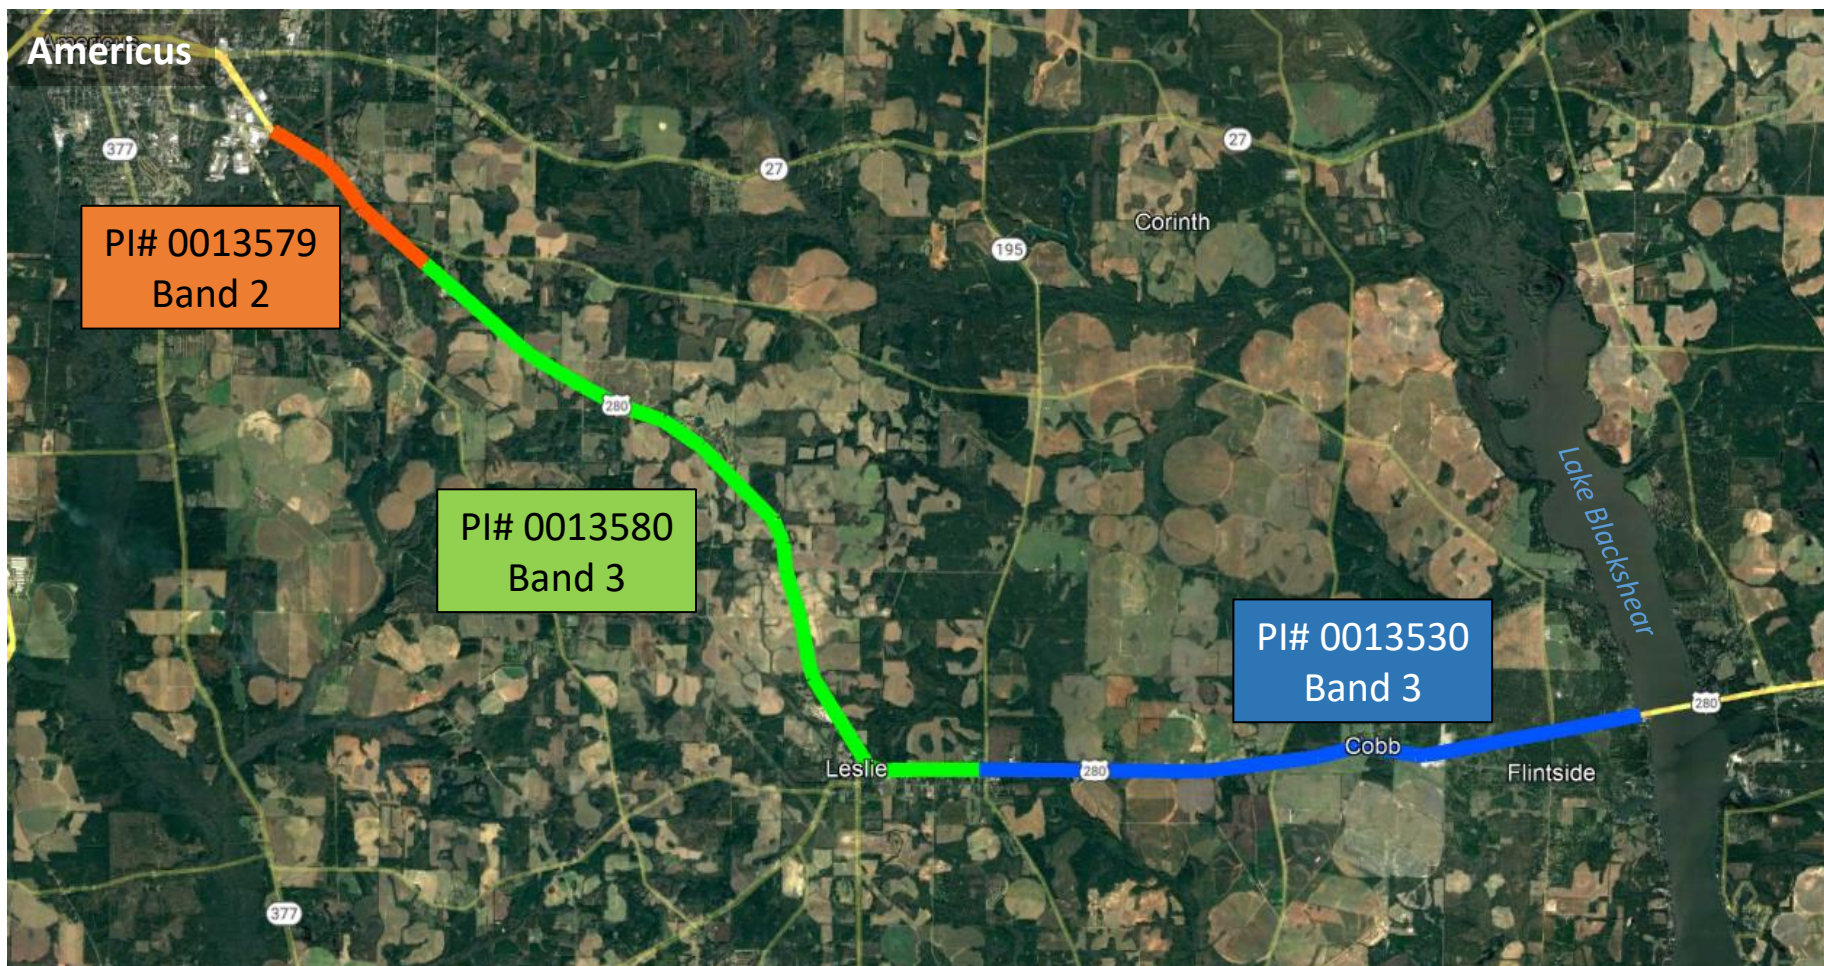

River Valley - TIA 2 (2023-2032)

US 280 Preconstruction Updates

US 280 widening from Felder Street to District Line Rd - Band 2

- Working on Preliminary Plans

US 280 widening from District Line Rd to SR 195 - Band 3

- Working on concept
- Environmental screening
- PIOH 8/21 in Leslie

US 280 widening from SR 195 to Lake Blackshear - Band 3

- Working on concept
- Environmental screening
- PIOH 8/21 in Leslie

Lower Lumpkin Rd – Quitman County



The TIA Office

Kenneth Franks

TIA Administrator
(404) 631-1568
kfranks@dot.ga.gov

Eric Wilkinson

Assistant TIA
Administrator
(478) 538-8522
ewilkinson@dot.ga.gov

Jeramy Durrence

TIA Regional Coordinator
CSRA, HOGA, & SG
(404)694-6545
jdurrence@dot.ga.gov

Brent Moseley

TIA Regional Coordinator
SG & HOGA
(912) 661-7157
bmoseley@dot.ga.gov

William Eastin

TIA Regional Coordinator
River Valley & SG
(404) 904-4204
weastin@dot.ga.gov

www.ga-tia.com
