




# Transportation Investment Act

Southern Georgia

March 21, 2023 CRP Update



## TIA Regions

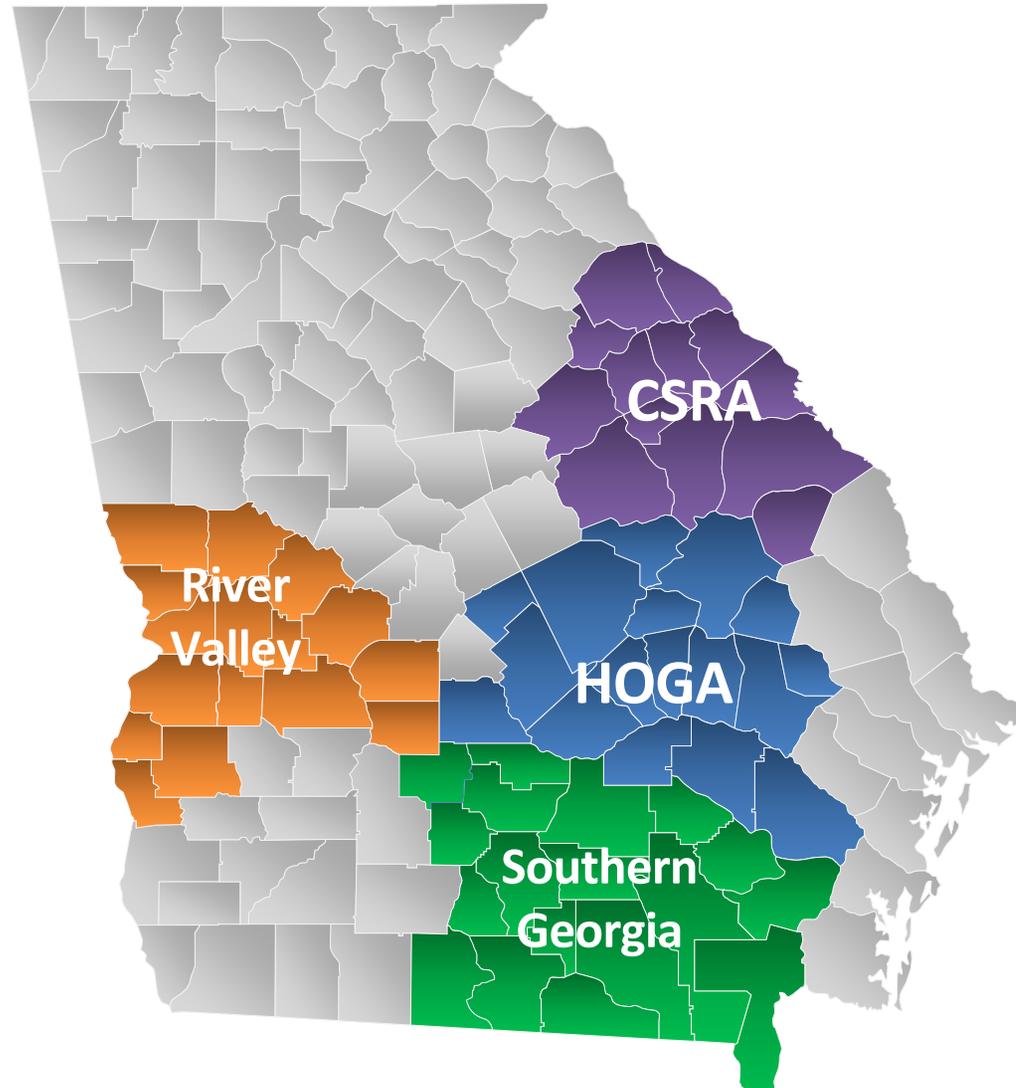


## TIA Collections thru Jan 2023

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
<b>CSRA</b>	\$8,213,567*	\$6,160,175*	\$2,053,392*
<b>River Valley</b>	\$5,023,984*	\$3,767,988*	\$1,255,996*
<b>Heart of Georgia</b>	\$3,486,897*	\$2,615,173*	\$871,724*
<b>Southern Georgia</b>	<b>\$275,014,233*</b>	<b>\$206,260,675*</b>	<b>\$68,753,558*</b>
<b>Totals</b> (*rounded amounts)	\$291,738,681	\$218,804,011	\$72,934,670

## TIA Collections thru Jan 2023


Region	Original Revenue Forecast	Actual Revenue Collected	% Behind Forecast
CSRA	\$6,311,892*	\$8,213,567*	30.1%
River Valley	\$4,554,854*	\$5,023,984*	10.3%
Heart of Georgia	\$2,696,420*	\$3,486,897*	29.3%
<b>Southern Georgia</b>	<b>\$215,166,245*</b>	<b>\$275,014,233*</b>	<b>27.8%</b>
Totals (*rounded amounts)	\$228,729,411	\$291,738,681	27.5%

## Southern Georgia Timeline

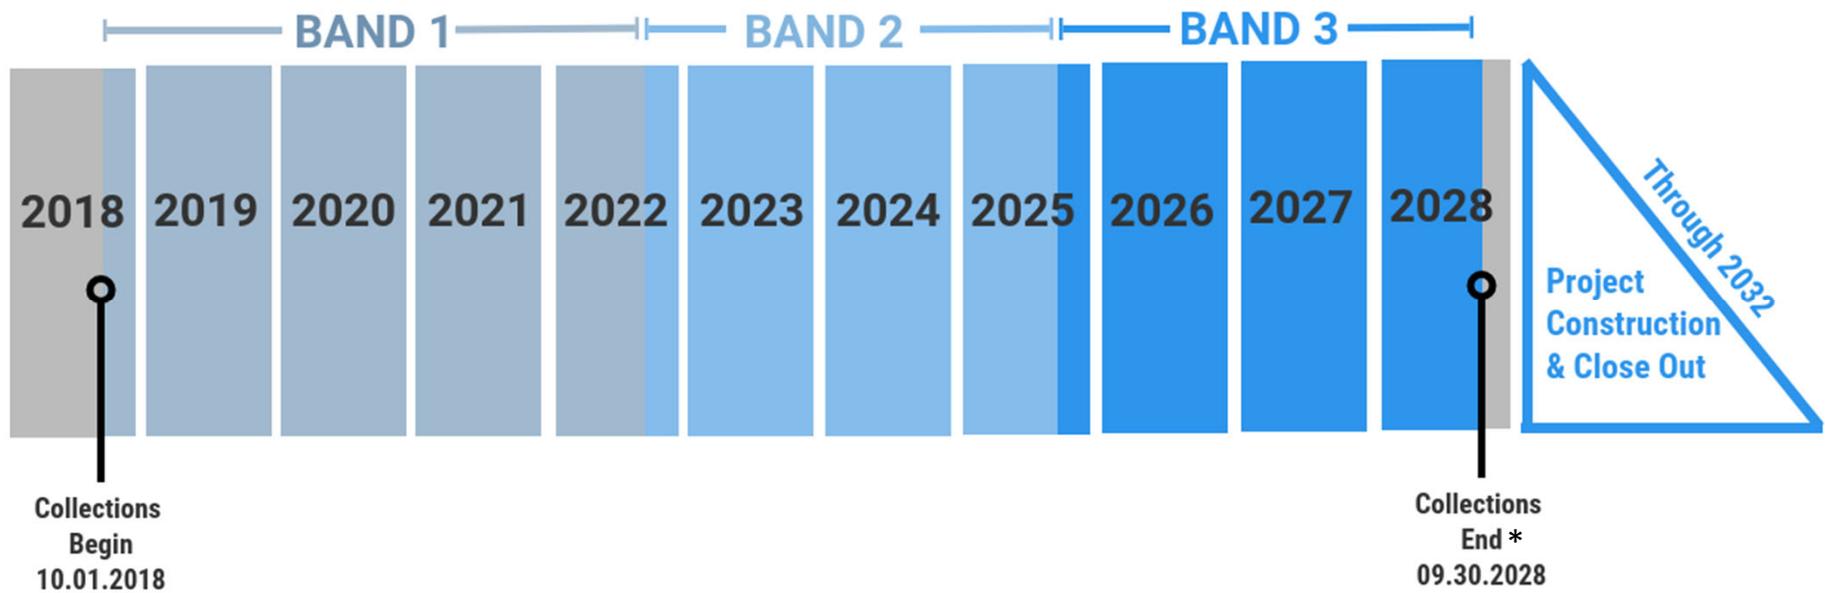

\* Should revenue meet the projected max prior to the legislated end date, collections will end early.

## Southern GA Project Overview

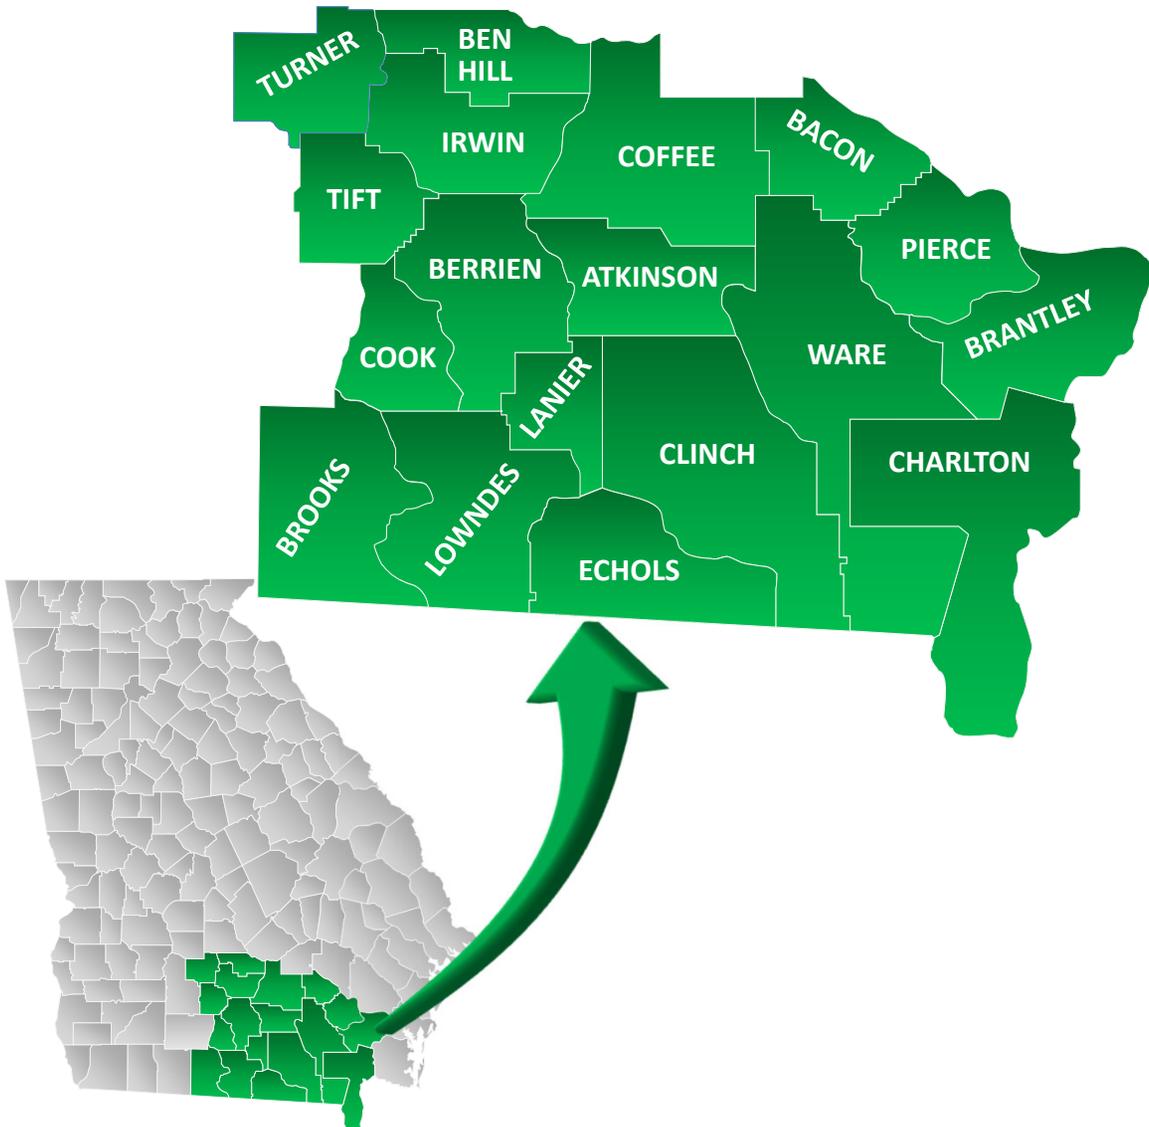

**151**

Total Projects

**\$408,763,452**

Final Investment List  
Project Total

**25**

In Construction

**77**

Projects Completed

**\$107,956,739**

Total Expenditure to Date  
(as of 3/20/23)

## Projects Let since Nov

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget	Low Bid
0016171	Cogdell Road Widen and Resurface	Atkinson	Jan 2023	Minor Widen	\$2,359,000	\$2,030,456.72
0016287	S Patterson Street at Griffin Avenue Intersection and Drainage Improvements	Lowndes / Valdosta	Feb 2023	Intsct Imp	\$1,258,000	\$709,635.15
0016245	S. Gaskin Avenue Sidewalk and Drainage Improvements	Coffee / Douglas	Feb 2023	Sidewalks	\$657,100	\$901,418.27
0016198	Cherry Street	Brantley / Nahunta	Feb 2023	Grade, Drain, Base & Pave	\$367,317	\$212,652.82
0016181	Johnson Lake Road Widening and Safety Improvements	Bacon	Mar 2023	Minor Widen	\$3,000,000	\$2,545,301.50

**\$7,641,417    6,399,464**

# TIA Letting Forecast

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0016253	Alabama Road Truck Route Improvements	Cook / Adel	Mar 2023	Grd Drn Bs Pv	\$3,312,000
0016285	Old Clyattville Road Widening - Valdosta	Lowndes / Valdosta	Apr 2023	Widening	\$6,217,514
0016290	Baytree Road at Gornto Road Intersection and Signal Improvements	Lowndes / Valdosta	Apr 2023	Intsct Imp	\$2,734,000
0016275	Briggston Road Paving and Drainage Improvements	Lowndes	Apr 2023	Grd Drn Bs Pv	\$2,525,000
0016299	Scotterville Road Bridge Replacement over Little Creek	Tift	Apr 2023	Bridge	\$1,410,000
0016201	DeVane Road Bridge Replacement, Widen and Resurface	Brooks	May 2023	Bridge	\$4,000,000
0016300	Omega-Eldorado Road Bridge Replacement over Arnold Creek	Tift	May 2023	Bridge	\$1,911,000

**7 Projects**  
**Total TIA Budget = \$22,109,514**

## Projects under Construction

PI Number	Project Name	County	Project Type
421345-	SR 32 from west of CR 296 east to the West City Limits of Douglas	Coffee	Widening
0016312	Albany Avenue Widen and Resurfacing	Ware / Waycross	Minor Widen
0016276	Hightower Road/Cooper Road NE Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv
0010297	I-75 @ SR 31 - Phase II (Exit 11)	Lowndes	Interchange
0016241	Youngie Fussell Road / Bridgetown Road Widen and Resurface	Coffee	Minor Widen
0016293	Horseshoe Road / Fletcher Road Area Resurfacing Bundle	Pierce	Resurfacing
0015536	SR520 / US82 @ Satilla River Overflow 14 mi east of Hoboken	Brantley	Bridge
0016302	8th Street Widening for Turn Lane	Tift / Tifton	Turn Lanes
0016203	Barwick Road Sidewalks and Drainage Improvements	Brooks	Sidewalks

# I-75 @ SR 31 - Exit 11, Lowndes County



# North Highland St, City of Quitman



# Henry Tift Myers Airport, Tift County





# Old 41, Lowndes County




## Evergreen Road Ben Hill County & Fitzgerald




## Oak Lane, City of Argyle

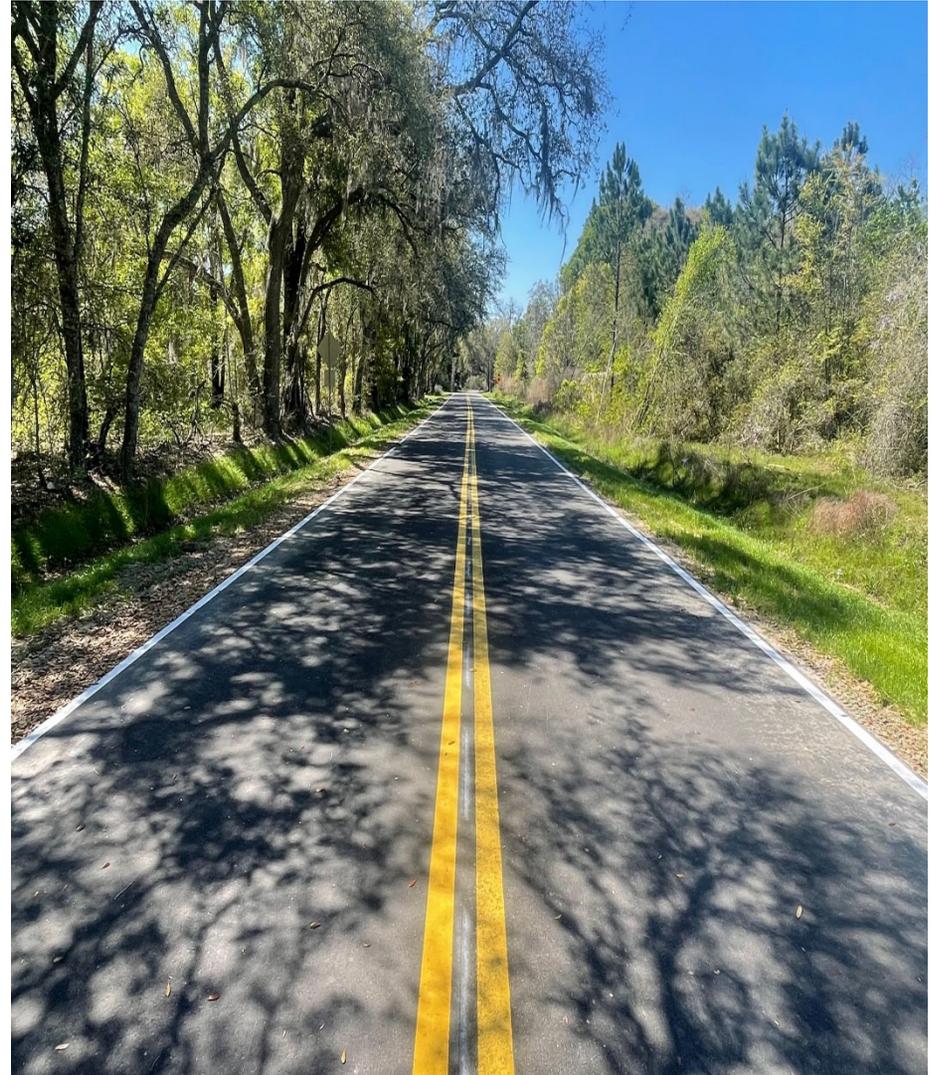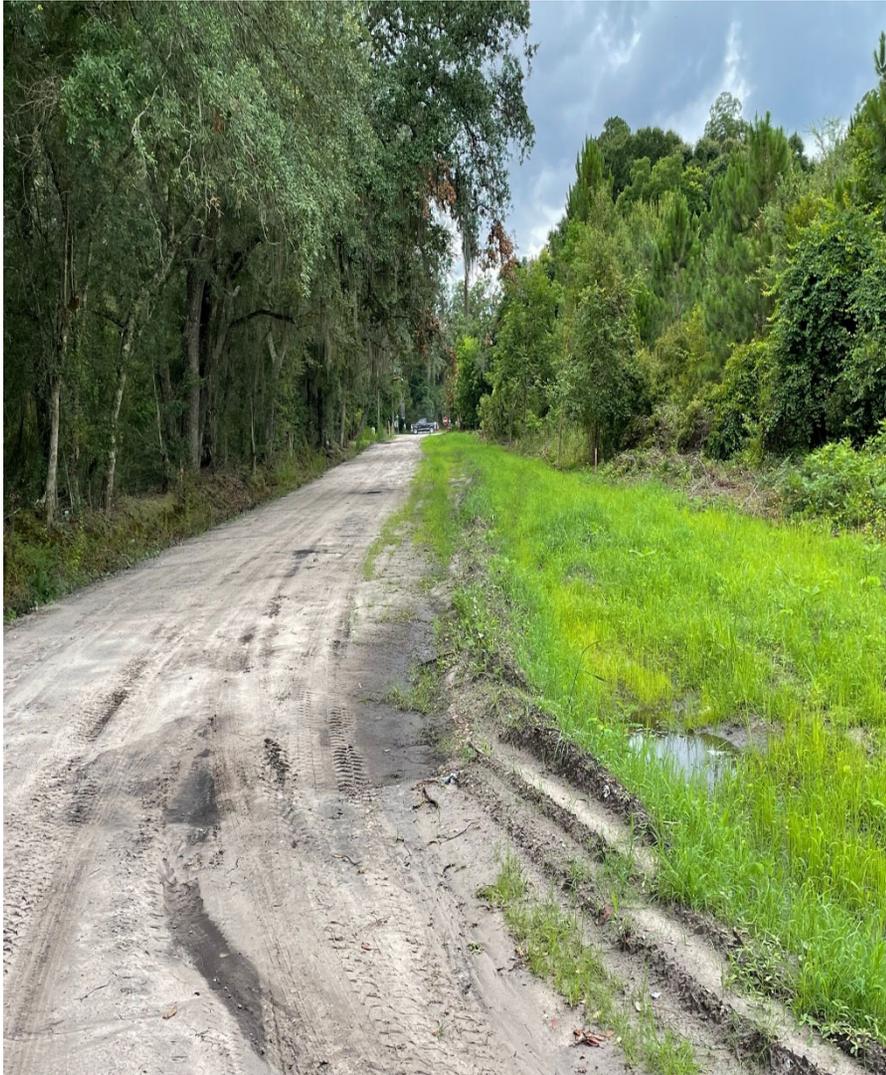

## Valdel Road, Cook County

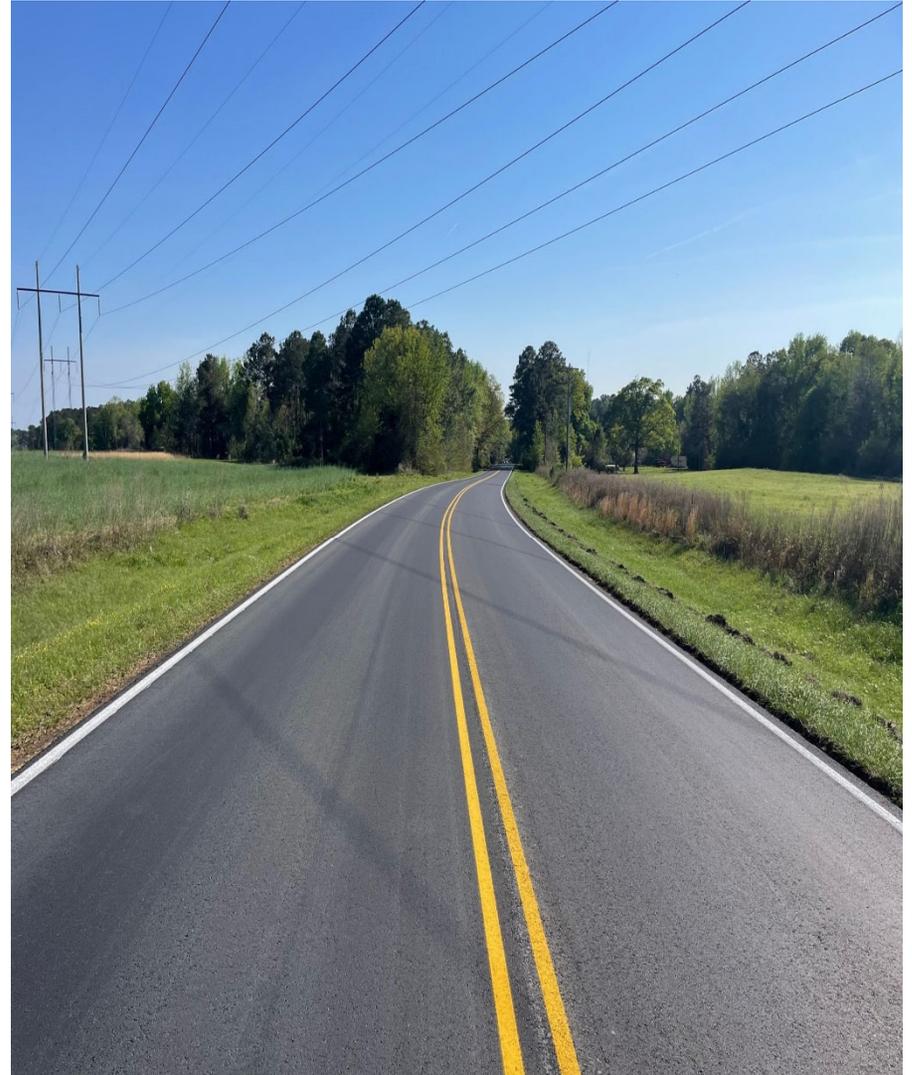


# Projects with Local Let Agreements

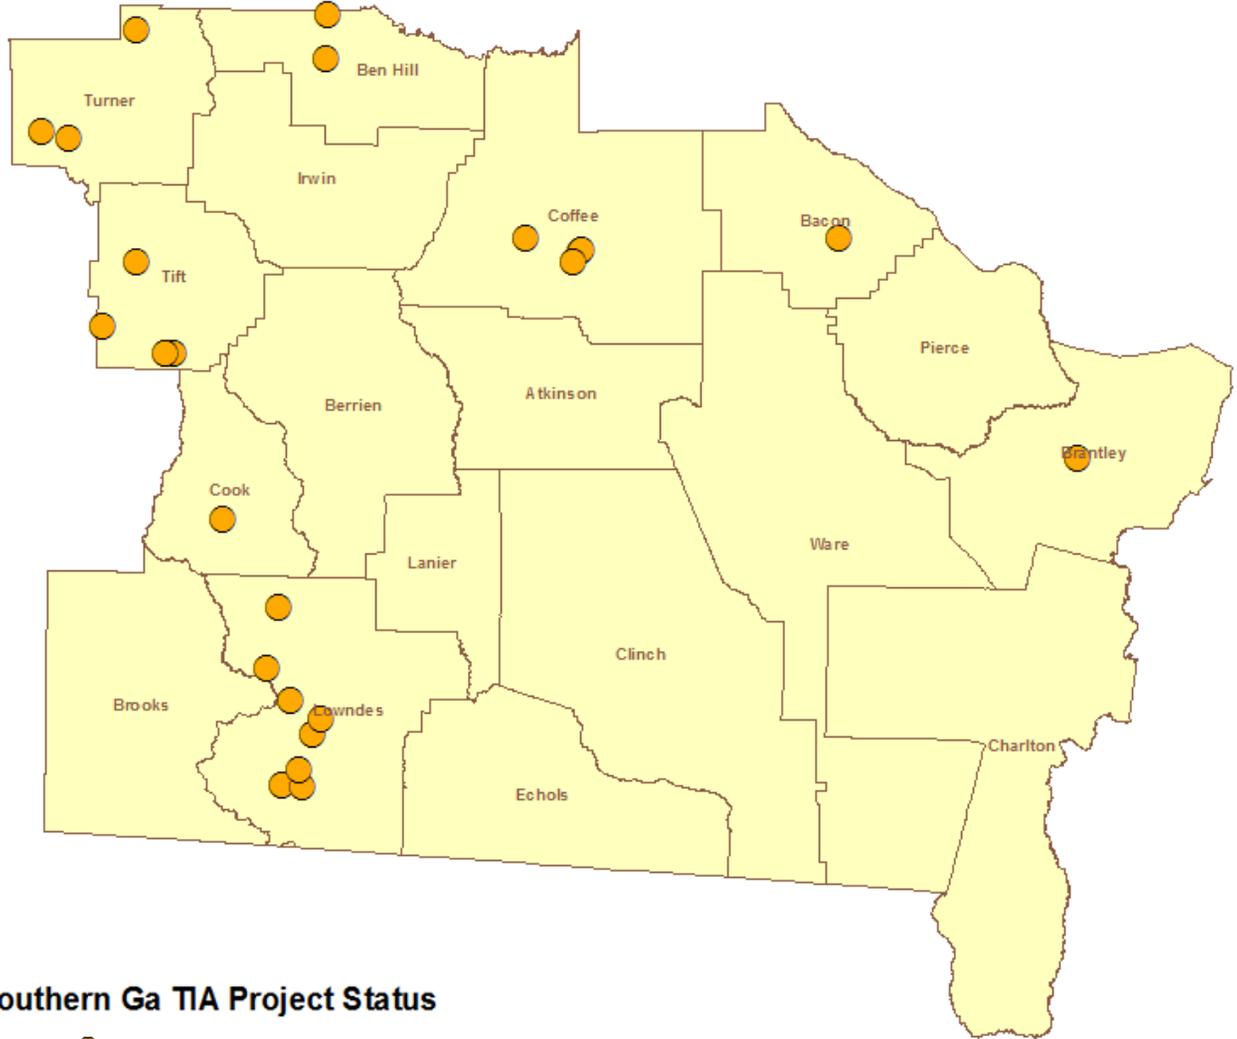

**Southern Ga TIA Project Status**

● PE-Local


# Projects under Construction

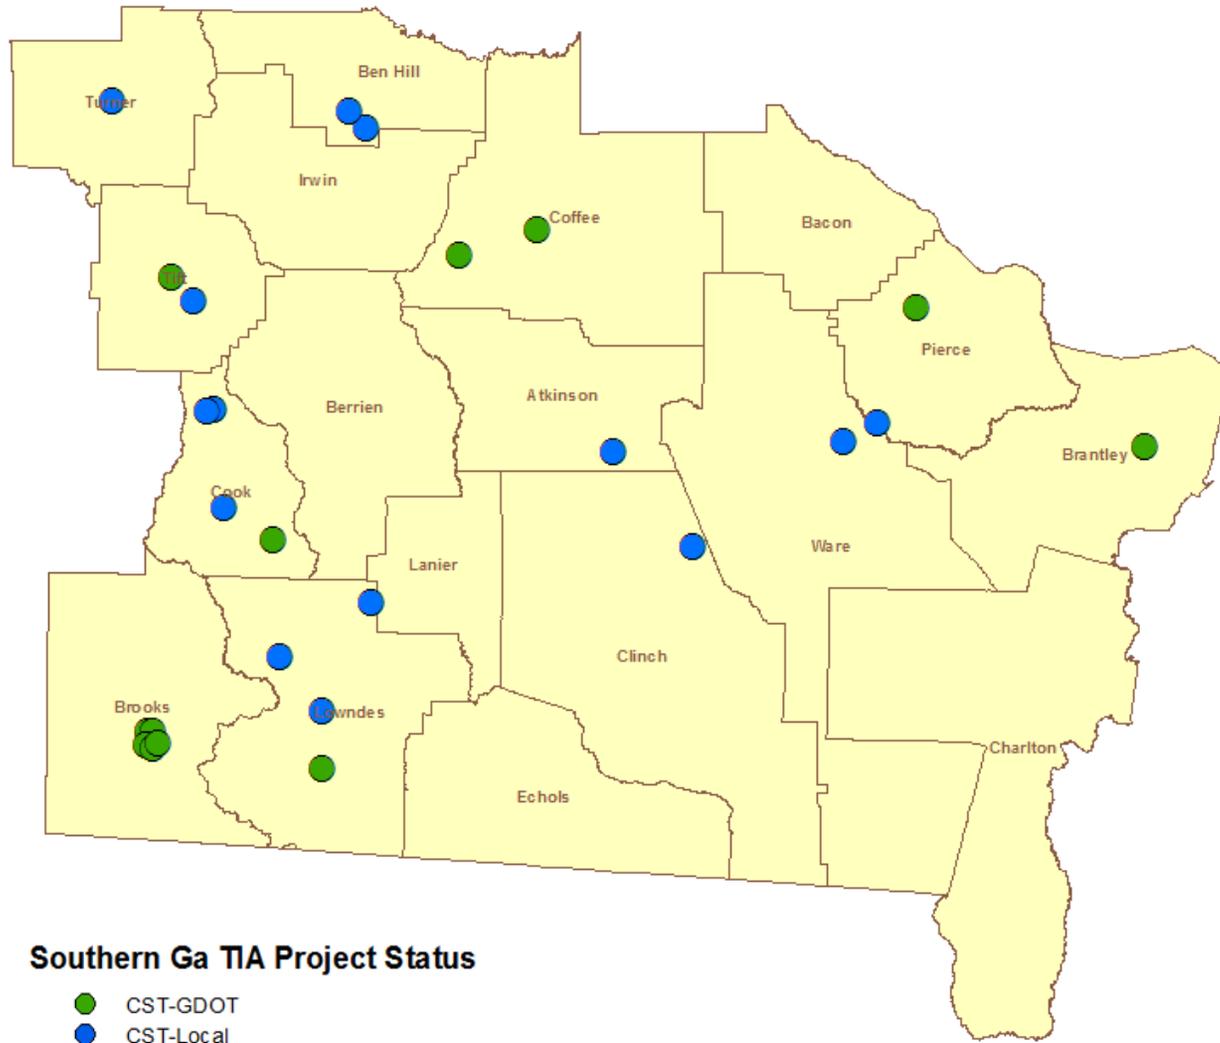

**Southern Ga TIA Project Status**

- CST-GDOT
- CST-Local

## Completed Projects

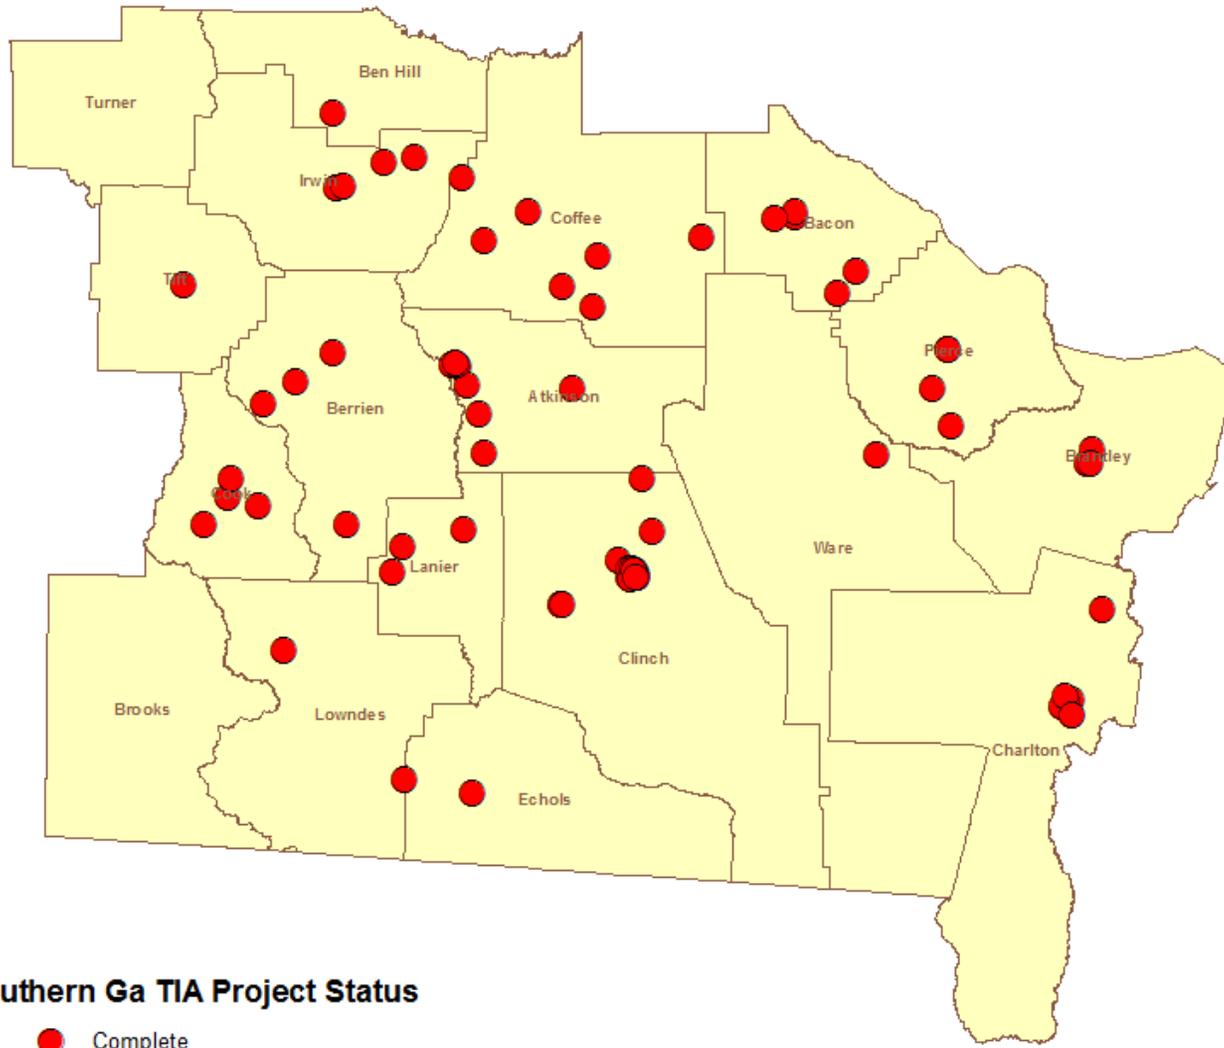

**Southern Ga TIA Project Status**

● Complete

# Questions?

**SOUTHERN GEORGIA**



**TRANSPORTATION  
INVESTMENT ACT**

*Your Penny, Your Progress*
