


*Lowndes County
Board of Commissioners*

Bill Slaughter, Chairman



Joyce E. Evans, District 1

Scott Crenstein, District 2

Mark Wisenbaker, District 3

Demarcus Marshall, Ph.D. District 4

Clay Griner, District 5

Post Office Box 1349 • Valdosta, GA 31603-1349 • Phone (229) 671-2400 • Fax (229) 245-5222

December 5, 2023

The Honorable Burt Jones
Office of the Lieutenant Governor
240 State Capitol
Atlanta, GA 30334

Dear Lt. Governor Jones,

As Chairman of the Southern Georgia Region Citizens Review Panel for the Transportation Act, I submit this report in pursuant to O.C.G.A. § 48-8-251.

Enclosed is the update from the Southern Georgia Region Citizens Review Panel consisting of a letter from Mr. Kenneth Franks, State TIA Administrator. Also included is a copy of the Annual Status Report and minutes of the meetings for calendar year 2023; all meetings were held in Nashville, Georgia.

The Transportation Act has been very beneficial to the Southern Georgia Region. We will be able to complete transportation projects for our region that may have never been completed.

We are very excited about revenue collections to date. The Southern Georgia Region has collected \$325,451,119.00 through September of calendar year 2023, that is 30.4% above the baseline projections; a positive sign that the economy in Georgia is doing very well. We have completed 86 projects in the Southern Georgia Region, 24 are currently under construction, and many are in preconstruction.


I would like to thank Mr. Kenneth Franks and his staff, for all of the information and support they have provided the Citizens Review Panel as we undertake our duties and responsibilities that our positions require of us.

Respectfully submitted,

Bill Slaughter, Chairman
Southern Georgia CRP

*Lowndes County
Board of Commissioners*

Bill Slaughter, Chairman



Joyce E. Evans, District 1

Scott Crenstein, District 2

Mark Wisenbaker, District 3

Demarcus Marshall, Ph.D. District 4

Clay Griner, District 5

Post Office Box 1349 • Valdosta, GA 31603-1349 • Phone (229) 671-2400 • Fax (229) 245-5222

December 5, 2023

The Honorable Jon Burns
Office of the Speaker of the House
332 State Capitol
Atlanta, GA 30334

Dear Speaker Jon Burns,

As Chairman of the Southern Georgia Region Citizens Review Panel for the Transportation Act, I submit this report in pursuant to O.C.G.A. § 48-8-251.

Enclosed is the update from the Southern Georgia Region Citizens Review Panel consisting of a letter from Mr. Kenneth Franks, State TIA Administrator. Also included is a copy of the Annual Status Report and minutes of the meetings for calendar year 2023; all meetings were held in Nashville, Georgia.

The Transportation Act has been very beneficial to the Southern Georgia Region. We will be able to complete transportation projects for our region that may have never been completed.

We are very excited about revenue collections to date. The Southern Georgia Region has collected \$325,451,119.00 through September of calendar year 2023, that is 30.4% above the baseline projections; a positive sign that the economy in Georgia is doing very well. We have completed 86 projects in the Southern Georgia Region, 24 are currently under construction, and many are in preconstruction.

I would like to thank Mr. Kenneth Franks and his staff, for all of the information and support they have provided the Citizens Review Panel as we undertake our duties and responsibilities that our positions require of us.

Respectfully submitted,

Bill Slaughter, Chairman
Southern Georgia CRP



Russell R. McMurtry, P.E., Commissioner
One Georgia Center
600 West Peachtree Street, NW
Atlanta, GA 30308
(404) 631-1000 Main Office

November 8, 2023

Citizens Review Panel (CRP) Members
Mr. Bill Slaughter, Chairman
Southern Georgia Special District

RE: Transportation Investment Act (TIA) of 2010

Dear Citizens Review Panel Members:

The Georgia Department of Transportation (Georgia DOT) presents the attached update through calendar year 2023 on the Transportation Investment Act of 2010 for the Southern Georgia Special District.

A summary of projects completed in 2023 is included. This summary can be utilized in the determination of benefits by the CRP for completed projects. As of this letter, 86 TIA projects have been completed in Southern Georgia with 12 completed in 2023. 24 are currently under construction and 39 are in preconstruction.

A calculation of revenue collection estimates versus actual receipts in Southern Georgia from program inception to date shows the total funds received are 30.4% higher than anticipated. TIA collections and construction activity in Southern Georgia have remained steady throughout 2023. Our Georgia DOT team's project management strategies and close coordination with local government partners have allowed us all to successfully continue planning, constructing, and completing TIA projects, and as a result, all TIA projects on the final investment list are still on track to be delivered. Georgia DOT remains committed to empowering the regions of our state in taking an active role in our transportation future.

Please let me know if you need further information.

Sincerely,

A handwritten signature in blue ink, appearing to read "K. Franks", is written over a light blue circular stamp.

Kenneth Franks
State TIA Administrator

Enclosure: Annual Report and CRP Meeting Minutes

cc: Diana Pope, Georgia State Finance and Investment Commission
Lisa Cribb, ATTN: Amy Martin, Southern Georgia Regional Commission

Southern Georgia
Annual Project Status Report
Status on October 30, 2023

Band	Project ID	County	GDOT ID	Description	Project Phase	Project Let By
01	SGRC-001	Atkinson	PI-0016170	US 441 Sidewalk Improvements	Complete	Local Let
01	SGRC-003	Atkinson	PI-0016172	Springhead Road Widen and Resurface Phase 1	Finance Closed	TIA Let
01	SGRC-004	Atkinson	PI-0016173	Springhead Road Widen and Resurface Phase 2	Finance Closed	TIA Let
01	SGRC-005	Atkinson	PI-0016174	Springhead Road Widen and Resurface Phase 3	Finance Closed	TIA Let
01	SGRC-006	Atkinson	PI-0016175	Bostwick Street Paving	Finance Closed	Local Let
01	SGRC-007	Atkinson	PI-0016176	McCranie Ave Paving	Finance Closed	Local Let
01	SGRC-008	Atkinson	PI-0016177	Florida Road Paving	Finance Closed	Local Let
01	SGRC-009	Atkinson	PI-0016178	School Road Paving	Finance Closed	Local Let
01	SGRC-010	Bacon	PI-0016179	Industrial Park Roads Resurfacing Bundle	Complete	TIA Let
01	SGRC-011	Bacon	PI-0016180	Douglas Street Resurfacing	Finance Closed	TIA Let
01	SGRC-014	Bacon	PI-0016183	Corinth Church Road Resurfacing	Complete	TIA Let
01	SGRC-015	Bacon	PI-0016184	Ten Mile Church Road Resurfacing	Complete	TIA Let
01	SGRC-016	Bacon	PI-0016185	Cumberland Road Resurfacing	Complete	TIA Let
01	SGRC-020	Ben Hill	PI-0016189	Evergreen Road Resurfacing - Ben Hill	Complete	Local Let
01	SGRC-022	Ben Hill	PI-0016191	Appomattox Road Resurfacing	Finance Closed	TIA Let
01	SGRC-023	Ben Hill	PI-0016192	Evergreen Road Resurfacing - Fitzgerald	Complete	Local Let
01	SGRC-024	Berrien	PI-0016193	West Lenox Road Widen and Resurface	Finance Closed	Local Let
01	SGRC-025	Berrien	PI-0016194	Lenox-Alapaha Highway Widen and Resurface	Complete	Local Let
01	SGRC-026	Berrien	PI-0016195	Coy Hancock Road Resurfacing	Finance Closed	Local Let
01	SGRC-027	Berrien	PI-0016196	Garner Road Widen and Resurface	Finance Closed	Local Let
01	SGRC-029	Brantley	PI-0016197	Roberson Street Widen and Resurface	Finance Closed	Local Let
01	SGRC-031	Brantley	PI-0016199	Velie Street Paving	Finance Closed	Local Let
01	SGRC-032	Brantley	PI-0016200	Cannon Street Resurfacing	Finance Closed	Local Let
01	SGRC-034	Brooks	PI-0016202	Webster Road Sidewalks and Drainage Improvements	Construction	TIA Let
01	SGRC-035	Brooks	PI-0016203	Barwick Road Sidewalks and Drainage Improvements	Construction	TIA Let
01	SGRC-036	Brooks	PI-0016204	N. Highland Street Sidewalks and Drainage Improvements	Construction	TIA Let
01	SGRC-037	Brooks	PI-0016205	N. MLK Street Sidewalks	Construction	TIA Let
01	SGRC-038	Brooks	PI-0016206	S. Court Street Sidewalk	Construction	TIA Let
01	SGRC-039	Charlton	PI-0016207	River Road Resurfacing	Finance Closed	Local Let
01	SGRC-041	Charlton	PI-0016208	Tower Street Resurfacing and Drainage Improvements	Finance Closed	Local Let
01	SGRC-042	Charlton	PI-0016209	Tower Street Paving and Drainage Improvements	Finance Closed	Local Let
01	SGRC-043	Charlton	PI-0016210	Homeland Park Road Bridge Replacement	Finance Closed	Local Let

**Southern Georgia
Annual Project Status Report**
Status on October 30, 2023

Band	Project ID	County	GDOT ID	Description	Project Phase	Project Let By
01	SGRC-044	Charlton	PI-0016211	Bowery Lane Widening and Resurfacing	Complete	TIA Let
01	SGRC-045	Charlton	PI-0016212	Broadway Resurfacing	Complete	TIA Let
01	SGRC-046	Charlton	PI-0016213	Paxton Road Resurfacing	Complete	TIA Let
01	SGRC-047	Clinch	PI-0016214	Oak Lane Resurfacing	Complete	Local Let
01	SGRC-050	Clinch	PI-0016216	Frank Sessoms Memorial Hwy/Cogdell Hwy Resurfacing	Complete	TIA Let
01	SGRC-051	Clinch	PI-0016217	Cogdell Hwy/Sandy Bottom Road Resurfacing	Finance Closed	TIA Let
01	SGRC-052	Clinch	PI-0016218	Lightsey Street Resurfacing	Finance Closed	TIA Let
01	SGRC-053	Clinch	PI-0016219	Mill Street Resurfacing	Finance Closed	TIA Let
01	SGRC-054	Clinch	PI-0016220	Peach Street Resurfacing	Finance Closed	Local Let
01	SGRC-055	Clinch	PI-0016221	Elna Street Resurfacing	Finance Closed	Local Let
01	SGRC-056	Clinch	PI-0016222	Wheeler Street Resurfacing	Finance Closed	Local Let
01	SGRC-057	Clinch	PI-0016223	Beacon Light Replacement at Homerville Airport	Finance Closed	Local Let
01	SGRC-058	Clinch	PI-0016224	Virginia Avenue Resurfacing	Finance Closed	Local Let
01	SGRC-059	Clinch	PI-0016225	Wiregrass Street Resurfacing	Finance Closed	Local Let
01	SGRC-060	Clinch	PI-0016226	Magnolia Street Resurfacing	Finance Closed	Local Let
01	SGRC-061	Clinch	PI-0016227	Orange Street Resurfacing	Finance Closed	Local Let
01	SGRC-062	Clinch	PI-0016228	Dovie Lane/Wiregrass Street Ext. Resurfacing	Finance Closed	Local Let
01	SGRC-063	Clinch	PI-0016229	Reddick Street Resurfacing	Finance Closed	Local Let
01	SGRC-064	Clinch	PI-0016230	Brown Street Resurfacing	Finance Closed	Local Let
01	SGRC-065	Clinch	PI-0016231	Tomlinson Street Resurfacing	Finance Closed	Local Let
01	SGRC-066	Clinch	PI-0016232	Old Pearson Road Resurfacing	Finance Closed	Local Let
01	SGRC-067	Clinch	PI-0016233	Battle Street Resurfacing	Finance Closed	Local Let
01	SGRC-070	Clinch	PI-0016234	Gaskins Street Resurfacing	Finance Closed	Local Let
01	SGRC-073	Coffee	PI-0016236	Harvey Vickers Road Widening and Resurface	Finance Closed	TIA Let
01	SGRC-074	Coffee	PI-0016237	Rebecca S Waldron Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-075	Coffee	PI-0016238	Wendell Sears Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-076	Coffee	PI-0016239	Wray Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-079	Coffee	PI-0016242	Sinkhole Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-080	Coffee	PI-0016243	Warren Carter Road/Hillcrest Road Widen and Resurface	Complete	TIA Let
01	SGRC-090	Coffee	PI-0016252	N. Liberty Street Resurfacing	Finance Closed	TIA Let
01	SGRC-072	Coffee	PI-421345-	SR 32 from west of CR 296 east to the West City Limits of Douglas	Complete	GDOT - OPD Let
01	SGRC-091	Cook	PI-0016253	Alabama Road Truck Route Improvements	Construction	Local Let

**Southern Georgia
Annual Project Status Report**
Status on October 30, 2023

Band	Project ID	County	GDOT ID	Description	Project Phase	Project Let By
01	SGRC-093	Cook	PI-0016255	Turn Lanes at New Recreation Facility on SR 37	Finance Closed	Local Let
01	SGRC-094	Cook	PI-0016256	Antioch Road Resurfacing	Finance Closed	TIA Let
01	SGRC-096	Cook	PI-0016258	Taylor Street Paving	Complete	Local Let
01	SGRC-097	Cook	PI-0016259	E. Revels Street Paving	Complete	Local Let
01	SGRC-098	Cook	PI-0016260	Lovett Street Sidewalks and Resurfacing	Finance Closed	Local Let
01	SGRC-099	Cook	PI-0016261	Elm Street Sidewalks and Resurfacing	Finance Closed	Local Let
01	SGRC-100	Echols	PI-0016262	John Hampton Road Paving	Complete	Local Let
01	SGRC-101	Irwin	PI-0016263	Osierfield Drive Widen and Resurface	Finance Closed	TIA Let
01	SGRC-102	Irwin	PI-0016264	Evergreen Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-103	Irwin	PI-0016265	Cherry Street Resurfacing and Drainage Improvements	Finance Closed	Local Let
01	SGRC-104	Irwin	PI-0016266	Fifth Street Ext. Paving	Finance Closed	Local Let
01	SGRC-105	Lanier	PI-0016267	River Road Widen and Resurface	Finance Closed	TIA Let
01	SGRC-106	Lanier	PI-0016268	Boyette Road Widen and Resurface	Complete	TIA Let
01	SGRC-107	Lanier	PI-0016269	Giddens Road/Royals Road Resurface	Complete	TIA Let
01	SGRC-109	Lowndes	PI-0010297	I-75 @ SR 31 - Phase II (Exit 11)	Construction	GDOT - OPD Let
01	SGRC-110	Lowndes	PI-0016271	Old 41 N. Widening	Complete	Local Let
01	SGRC-113	Lowndes	PI-0016274	Clyattstone Road/Simpson Lane Paving and Drainage Improvements	Finance Closed	Local Let
01	SGRC-115	Lowndes	PI-0016276	Hightower Road/Cooper Road NE Paving and Drainage Improvements	Construction	Local Let
01	SGRC-116	Lowndes	PI-0016277	Hickory Grove Road Bridge Replacement	Finance Closed	Local Let
01	SGRC-123	Lowndes	PI-0016284	New Air Traffic Control Tower at Valdosta Regional Airport	Construction	Local Let
01	SGRC-130	Pierce	PI-0016291	City of Patterson Resurfacing Bundle Phase 1	Complete	TIA Let
01	SGRC-131	Pierce	PI-0016292	City of Blackshear Session Hill Resurfacing Bundle	Complete	Local Let
01	SGRC-133	Pierce	PI-0016294	Ware Street Widen and Resurface	Finance Closed	TIA Let
01	SGRC-134	Pierce	PI-0016295	St. Johns Church Road Widen and Resurface	Complete	TIA Let
01	SGRC-135	Pierce	PI-0016296	Golf Course Road Alignment, Drainage and Resurfacing	Construction	Local Let
01	SGRC-142	Tift	PI-0016302	8th Street Widening for Turn Lane	Construction	TIA Let
01	SGRC-143	Tift	PI-0016303	2nd Street Resurfacing	Complete	TIA Let
01	SGRC-145	Tift	PI-0016305	Taxiway Improvements at Henry Tift Myers Airport	Complete	Local Let
01	SGRC-148	Turner	PI-0016308	City of Ashburn Resurfacing Bundle and Sidewalk Improvements	Finance Closed	Local Let
01	SGRC-153	Ware	PI-0016312	Albany Avenue Widen and Resurfacing	Finance Closed	Local Let
02	SGRC-002	Atkinson	PI-0016171	Cogdell Road Widen and Resurface	Construction	Local Let
02	SGRC-012	Bacon	PI-0016181	Johnson Lake Road Widening and Safety Improvements	Construction	Local Let

**Southern Georgia
Annual Project Status Report**
Status on October 30, 2023

Band	Project ID	County	GDOT ID	Description	Project Phase	Project Let By
02	SGRC-013	Bacon	PI-0016182	SR 32 Passing Lanes Between Alma to Douglas	Bidding	TIA Let
02	SGRC-017	Ben Hill	PI-0016186	Bethlehem Church Road Bridge at House Creek Bridge Replacement	Design	Local Let
02	SGRC-018	Ben Hill	PI-0016187	Bethlehem Church Road Bridge at Otter Creek Bridge Replacement	Design	Local Let
02	SGRC-019	Ben Hill	PI-0016188	Peachtree Road Corridor Realigning, Widening, and Intersection Improvements	Design	TIA Let
02	SGRC-021	Ben Hill	PI-0016190	Fitzgerald Perimeter Roads Improvements (Widen, Resurface, C/G)	Design	TIA Let
02	SGRC-030	Brantley	PI-0016198	Cherry Street Resurfacing	Construction	Local Let
02	SGRC-033	Brooks	PI-0016201	DeVane Road Bridge Replacement, Widen and Resurface	Construction	TIA Let
02	SGRC-049	Clinch	PI-422390-	SR 89/US441 from Orange St in Homerville to CR 101/Cowart Rd	Design	TIA Let
02	SGRC-071	Coffee	PI-0016235	Bud Hutcheson Road Paving	Design	Local Let
02	SGRC-078	Coffee	PI-0016241	Hwy 149/Youngie Fussell Road/Bridgetown Road Widen and Resurface	Complete	TIA Let
02	SGRC-082	Coffee	PI-0016245	S. Gaskin Avenue Sidewalk and Drainage Improvements	Construction	Local Let
02	SGRC-092	Cook	PI-0016254	Tillman Road Bypass Phase 3 Improvements	Design	Local Let
02	SGRC-095	Cook	PI-0016257	Valdel Road Resurfacing	Complete	TIA Let
02	SGRC-111	Lowndes	PI-0016272	Shiloh Road Resurfacing and Bridge Replacement	Design	Local Let
02	SGRC-114	Lowndes	PI-0016275	Briggston Road Paving and Drainage Improvements	Construction	Local Let
02	SGRC-124	Lowndes	PI-0016285	Old Clyattville Road Widening - Valdosta	Design	Local Let
02	SGRC-126	Lowndes	PI-0016287	S Patterson Street at Griffin Avenue Intersection and Drainage Improvements	Construction	Local Let
02	SGRC-127	Lowndes	PI-0016288	St Augustine Road at Gornto Road Intersection and Drainage Improvements	Design	TIA Let
02	SGRC-129	Lowndes	PI-0016290	Baytree Road at Gornto Road Intersection and Signal Improvements	Construction	Local Let
02	SGRC-132	Pierce	PI-0016293	Pierce County Horseshoe Road/Fletcher Road Area Resurfacing Bundle	Construction	TIA Let
02	SGRC-136	Pierce	PI-0016297	US 84 Intersection and Signal Improvements from County Farm Road to New School Road	Design	TIA Let
02	SGRC-137	Tift	PI-0016298	Upper Ty Ty Road Bridge Replacement over Little River	Design	Local Let
02	SGRC-139	Tift	PI-0016299	Scotterville Road Bridge Replacement over Little Creek	Construction	Local Let
02	SGRC-140	Tift	PI-0016300	Omega-Eldorado Road Bridge Replacement over Arnold Creek	Construction	Local Let
02	SGRC-141	Tift	PI-0016301	Omega-Eldorado Road Bridge Replacement over Little River	Design	Local Let
02	SGRC-146	Tift	PI-0016306	12th Street at Prince Avenue Intersection Improvements	Planning	Local Let
02	SGRC-149	Turner	PI-0016309	Hobby Road Paving	Design	Local Let
02	SGRC-150	Turner	PI-0016310	Glynn Cook Road Paving	Design	Local Let
02	SGRC-151	Turner	PI-0016311	Reid Road Paving	Design	Local Let
02	SGRC-152	Ware	PI-0013605	US 84 Bridge over Satilla River	Design	GDOT - OPD Let
02	SGRC-154	Ware	PI-0016313	Knight Avenue Resurfacing	Finance Closed	Local Let
03	SGRC-028	Brantley	PI-0015536	SR520/US82 @Satilla River Overflow 14 mi east of Hoboken	Construction	GDOT - OPD Let

Southern Georgia
Annual Project Status Report
 Status on October 30, 2023

Band	Project ID	County	GDOT ID	Description	Project Phase	Project Let By
03	SGRC-040	Charlton	PI-0000821	SR 40 from SR40 Conn to 0.36 mi east of May Bluff Rd	Design	GDOT - OPD Let
03	SGRC-048	Clinch	PI-0016215	Homerville Bypass Resurfacing, Bridge Replacement and Other Improvements	Design	TIA Let
03	SGRC-077	Coffee	PI-0016240	SR 158 Passing Lanes in Coffee County	Design	TIA Let
03	SGRC-081	Coffee	PI-0016244	McDonald Road Sidewalk and Drainage Improvements	Design	Local Let
03	SGRC-083	Coffee	PI-0016246	Chester Avenue Sidewalk and Drainage (Culvert) Improvements	Design	Local Let
03	SGRC-084	Coffee	PI-0016247	West Green Hwy (SR 135/US 221) Sidewalk Improvements	Design	Local Let
03	SGRC-086	Coffee	PI-0016248	Lupo Lane Sidewalk and Drainage Improvements	Design	Local Let
03	SGRC-087	Coffee	PI-0016249	Baker Hwy, East (SR 158) Sidewalk Improvements	Construction	Local Let
03	SGRC-088	Coffee	PI-0016250	West Walker Street Sidewalk Improvements	Design	Local Let
03	SGRC-089	Coffee	PI-0016251	Road Improvements at Douglas Municipal Airport	Design	Local Let
03	SGRC-108	Lowndes	PI-0016270	Old Clyattville Road Widening - Lowndes	Design	Local Let
03	SGRC-112	Lowndes	PI-0016273	Orr Road Extension	Inactive	TIA Let
03	SGRC-117	Lowndes	PI-0016278	Kinderlou Clyattville Road Paving and Drainage Improvements	Design	Local Let
03	SGRC-118	Lowndes	PI-0016279	Coleman Road NW Paving and Drainage Improvements	Design	Local Let
03	SGRC-119	Lowndes	PI-0016280	Twin Lakes Road Paving and Drainage Improvements	Design	Local Let
03	SGRC-120	Lowndes	PI-0016281	Hall Road Paving, Drainage and Other Improvements	Inactive	TIA Let
03	SGRC-121	Lowndes	PI-0016282	Country Club Drive Widening	Design	TIA Let
03	SGRC-122	Lowndes	PI-0016283	St. Augustine Road RR Grade Separation	Design	TIA Let
03	SGRC-125	Lowndes	PI-0016286	St Augustine Road at Norman Drive Intersection, Drainage and Signal Improvements	Design	TIA Let
03	SGRC-128	Lowndes	PI-0016289	Forrest Street Widening	Design	TIA Let
03	SGRC-138	Tift	PI-0010318	I-75 @ CR421/Chula Brookfield Rd - Phase II (Exit 69)	Design	TIA Let
03	SGRC-144	Tift	PI-0016304	McCormick Drive Widening and Realignment	Planning	Local Let
03	SGRC-147	Tift	PI-0016307	18th Street Ditch Bridge Replacements (5 Culverts)	Planning	Local Let
Multiple		Regional	PI-A000835	Program Administration		

10/31/2023

9:02:32 AM

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-001	Atkinson	01	PI-0016170	US 441 Sidewalk Improvements	\$1,188,000	\$645,502	\$645,502	\$0	No	N/A
SGRC-003	Atkinson	01	PI-0016172	Springhead Road Widen and Resurface Phase 1	\$1,085,000	\$664,413	\$664,413	\$0	No	N/A
SGRC-004	Atkinson	01	PI-0016173	Springhead Road Widen and Resurface Phase 2	\$1,253,000	\$1,295,702	\$1,295,702	\$0	Yes	Project exceeded original estimated cost. GDOT managed costs to keep overruns at a minimum.
SGRC-005	Atkinson	01	PI-0016174	Springhead Road Widen and Resurface Phase 3	\$885,000	\$354,037	\$354,037	\$0	No	N/A
SGRC-006	Atkinson	01	PI-0016175	Bostwick Street Paving	\$103,000	\$64,529	\$64,529	\$0	No	N/A
SGRC-007	Atkinson	01	PI-0016176	McCranie Ave Paving	\$77,000	\$50,303	\$50,303	\$0	No	N/A
SGRC-008	Atkinson	01	PI-0016177	Florida Road Paving	\$200,000	\$120,930	\$120,930	\$0	No	N/A
SGRC-009	Atkinson	01	PI-0016178	School Road Paving	\$72,000	\$46,110	\$46,110	\$0	No	N/A
SGRC-010	Bacon	01	PI-0016179	Industrial Park Roads Resurfacing Bundle	\$722,000	\$535,395	\$535,395	\$0	No	N/A
SGRC-011	Bacon	01	PI-0016180	Douglas Street Resurfacing	\$292,800	\$215,671	\$215,671	\$0	No	N/A
SGRC-014	Bacon	01	PI-0016183	Corinth Church Road Resurfacing	\$620,100	\$504,092	\$504,092	\$0	No	N/A
SGRC-015	Bacon	01	PI-0016184	Ten Mile Church Road Resurfacing	\$534,000	\$424,267	\$424,267	\$0	No	N/A
SGRC-016	Bacon	01	PI-0016185	Cumberland Road Resurfacing	\$389,687	\$241,340	\$238,435	\$2,905	No	N/A
SGRC-020	Ben Hill	01	PI-0016189	Evergreen Road Resurfacing - Ben Hill	\$688,300	\$949,608	\$0	\$834,745	Yes	Project exceeded original estimated cost. GDOT managed costs to keep overruns at a minimum.
SGRC-022	Ben Hill	01	PI-0016191	Appomattox Road Resurfacing	\$415,400	\$338,762	\$338,762	\$0	No	N/A
SGRC-023	Ben Hill	01	PI-0016192	Evergreen Road Resurfacing - Fitzgerald	\$523,500	\$523,500	\$0	\$470,134	No	N/A
SGRC-024	Berrien	01	PI-0016193	West Lenox Road Widen and Resurface	\$1,645,000	\$1,479,670	\$1,479,670	\$0	No	N/A
SGRC-025	Berrien	01	PI-0016194	Lenox-Alapaha Highway Widen and Resurface	\$1,610,000	\$1,352,752	\$1,352,752	\$0	No	N/A
SGRC-026	Berrien	01	PI-0016195	Coy Hancock Road Resurfacing	\$686,300	\$685,080	\$685,080	\$0	No	N/A
SGRC-027	Berrien	01	PI-0016196	Garner Road Widen and Resurface	\$2,513,000	\$2,447,539	\$2,447,539	\$0	No	N/A
SGRC-029	Brantley	01	PI-0016197	Roberson Street Widen and Resurface	\$87,900	\$87,523	\$87,523	\$0	No	N/A
SGRC-031	Brantley	01	PI-0016199	Velie Street Paving	\$200,000	\$171,207	\$171,207	\$0	No	N/A
SGRC-032	Brantley	01	PI-0016200	Cannon Street Resurfacing	\$52,000	\$46,487	\$46,487	\$0	No	N/A
SGRC-034	Brooks	01	PI-0016202	Webster Road Sidewalks and Drainage Improvements	\$2,281,900	\$2,628,667	\$358,762	\$354,601	No	Inflation applied to Original Estimated Cost; updated Project Budget \$2,628,667

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-035	Brooks	01	PI-0016203	Barwick Road Sidewalks and Drainage Improvements	\$399,800	\$719,137	\$115,120	\$234,339	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-036	Brooks	01	PI-0016204	N. Highland Street Sidewalks and Drainage Improvements	\$644,500	\$873,593	\$156,660	\$624,128	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-037	Brooks	01	PI-0016205	N. MLK Street Sidewalks	\$1,040,000	\$1,195,962	\$278,912	\$439,871	No	Inflation applied to Original Estimated Cost; updated Project Budget \$1,195,962
SGRC-038	Brooks	01	PI-0016206	S. Court Street Sidewalk	\$556,400	\$632,220	\$122,884	\$288,806	No	Inflation applied to Original Estimated Cost; updated Project Budget \$632,220
SGRC-039	Charlton	01	PI-0016207	River Road Resurfacing	\$1,947,200	\$1,910,542	\$1,910,542	\$0	No	N/A
SGRC-041	Charlton	01	PI-0016208	Tower Street Resurfacing and Drainage Improvements	\$250,000	\$249,524	\$249,524	\$0	No	N/A
SGRC-042	Charlton	01	PI-0016209	Tower Street Paving and Drainage Improvements	\$273,467	\$229,258	\$229,258	\$0	No	N/A
SGRC-043	Charlton	01	PI-0016210	Homeland Park Road Bridge Replacement	\$500,000	\$500,000	\$500,000	\$0	No	N/A
SGRC-044	Charlton	01	PI-0016211	Bowery Lane Widening and Resurfacing	\$150,000	\$162,439	\$162,439	\$0	No	Inflation applied to Original Estimated Cost; updated Project Budget \$162,439
SGRC-045	Charlton	01	PI-0016212	Broadway Resurfacing	\$161,000	\$169,577	\$169,577	\$0	No	Inflation applied to Original Estimated Cost; updated Project Budget \$169,577
SGRC-046	Charlton	01	PI-0016213	Paxton Road Resurfacing	\$120,600	\$100,560	\$100,560	\$0	No	N/A
SGRC-047	Clinch	01	PI-0016214	Oak Lane Resurfacing	\$300,000	\$260,009	\$30,449	\$229,560	No	N/A
SGRC-050	Clinch	01	PI-0016216	Frank Sessoms Memorial Hwy/Cogdell Hwy Resurfacing	\$2,161,000	\$1,511,126	\$1,511,126	\$0	No	N/A
SGRC-051	Clinch	01	PI-0016217	Cogdell Hwy/Sandy Bottom Road Resurfacing	\$319,100	\$391,054	\$391,054	\$0	Yes	Project exceeded original estimated cost. GDOT managed costs to keep overruns at a minimum.
SGRC-052	Clinch	01	PI-0016218	Lightsey Street Resurfacing	\$53,700	\$49,463	\$49,463	\$0	No	N/A
SGRC-053	Clinch	01	PI-0016219	Mill Street Resurfacing	\$65,400	\$56,330	\$56,330	\$0	No	N/A
SGRC-054	Clinch	01	PI-0016220	Peach Street Resurfacing	\$20,541	\$15,718	\$15,718	\$0	No	N/A
SGRC-055	Clinch	01	PI-0016221	Elna Street Resurfacing	\$94,900	\$82,678	\$82,678	\$0	No	N/A
SGRC-056	Clinch	01	PI-0016222	Wheeler Street Resurfacing	\$21,000	\$15,451	\$15,451	\$0	No	N/A
SGRC-057	Clinch	01	PI-0016223	Beacon Light Replacement at Homerville Airport	\$18,000	\$19,319	\$19,319	\$0	No	Inflation applied to Original Estimated Cost; updated Project Budget \$19,319
SGRC-058	Clinch	01	PI-0016224	Virginia Avenue Resurfacing	\$70,600	\$58,555	\$58,555	\$0	No	N/A
SGRC-059	Clinch	01	PI-0016225	Wiregrass Street Resurfacing	\$60,000	\$59,997	\$59,997	\$0	No	N/A
SGRC-060	Clinch	01	PI-0016226	Magnolia Street Resurfacing	\$58,800	\$51,593	\$51,593	\$0	No	N/A

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-061	Clinch	01	PI-0016227	Orange Street Resurfacing	\$19,257	\$17,500	\$17,500	\$0	No	N/A
SGRC-062	Clinch	01	PI-0016228	Dovie Lane/Wiregrass Street Ext. Resurfacing	\$32,700	\$5,514	\$5,514	\$0	No	N/A
SGRC-063	Clinch	01	PI-0016229	Reddick Street Resurfacing	\$100,900	\$60,580	\$60,580	\$0	No	N/A
SGRC-064	Clinch	01	PI-0016230	Brown Street Resurfacing	\$68,900	\$45,250	\$45,250	\$0	No	N/A
SGRC-065	Clinch	01	PI-0016231	Tomlinson Street Resurfacing	\$57,700	\$39,191	\$39,191	\$0	No	N/A
SGRC-066	Clinch	01	PI-0016232	Old Pearson Road Resurfacing	\$76,000	\$75,919	\$75,919	\$0	No	N/A
SGRC-067	Clinch	01	PI-0016233	Battle Street Resurfacing	\$18,100	\$17,903	\$17,903	\$0	No	N/A
SGRC-070	Clinch	01	PI-0016234	Gaskins Street Resurfacing	\$18,100	\$11,095	\$11,095	\$0	No	N/A
SGRC-073	Coffee	01	PI-0016236	Harvey Vickers Road Widening and Resurface	\$900,000	\$488,796	\$488,796	\$0	No	N/A
SGRC-074	Coffee	01	PI-0016237	Rebecca S Waldron Road Widen and Resurface	\$1,687,000	\$1,288,007	\$1,288,007	\$0	No	N/A
SGRC-075	Coffee	01	PI-0016238	Wendell Sears Road Widen and Resurface	\$350,000	\$334,274	\$334,274	\$0	No	N/A
SGRC-076	Coffee	01	PI-0016239	Wray Road Widen and Resurface	\$615,313	\$531,303	\$531,303	\$0	No	N/A
SGRC-079	Coffee	01	PI-0016242	Sinkhole Road Widen and Resurface	\$1,456,000	\$1,038,251	\$1,038,251	\$0	No	N/A
SGRC-080	Coffee	01	PI-0016243	Warren Carter Road/Hillcrest Road Widen and Resurface	\$950,000	\$605,188	\$605,188	\$0	No	N/A
SGRC-090	Coffee	01	PI-0016252	N. Liberty Street Resurfacing	\$231,500	\$268,417	\$268,417	\$0	Yes	Project exceeded original estimated cost. GDOT managed costs to keep overruns at a minimum. Inflation also applied to Original Estimated Cost.
SGRC-072	Coffee	01	PI-421345-	SR 32 from west of CR 296 east to the West City Limits of Douglas	\$9,780,000	\$27,003,849	\$16,108,984	\$5,627,739	No	Blended Project - Total Project Cost \$36,854,657. TIA and HB170 funds adjusted to accommodate band change request. Inflation also applied to Original Estimated Cost.
SGRC-091	Cook	01	PI-0016253	Alabama Road Truck Route Improvements	\$3,312,000	\$4,460,043	\$173,687	(\$0)	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-093	Cook	01	PI-0016255	Turn Lanes at New Recreation Facility on SR 37	\$250,000	\$129,269	\$129,269	\$0	No	Blended Project (State Funds) - Total Project Cost \$379,269
SGRC-094	Cook	01	PI-0016256	Antioch Road Resurfacing	\$1,949,300	\$1,621,329	\$1,621,329	\$0	No	N/A
SGRC-096	Cook	01	PI-0016258	Taylor Street Paving	\$276,900	\$107,033	\$19,383	\$87,650	No	N/A
SGRC-097	Cook	01	PI-0016259	E. Revels Street Paving	\$450,000	\$179,008	\$34,500	\$144,508	No	N/A
SGRC-098	Cook	01	PI-0016260	Lovett Street Sidewalks and Resurfacing	\$588,000	\$234,434	\$234,434	\$0	No	N/A
SGRC-099	Cook	01	PI-0016261	Elm Street Sidewalks and Resurfacing	\$715,000	\$496,582	\$496,582	\$0	No	N/A

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-100	Echols	01	PI-0016262	John Hampton Road Paving	\$400,000	\$364,140	\$364,140	\$0	No	N/A
SGRC-101	Irwin	01	PI-0016263	Osierfield Drive Widen and Resurface	\$1,967,000	\$1,347,562	\$1,347,562	\$0	No	N/A
SGRC-102	Irwin	01	PI-0016264	Evergreen Road Widen and Resurface	\$1,596,000	\$1,067,955	\$1,067,955	\$0	No	N/A
SGRC-103	Irwin	01	PI-0016265	Cherry Street Resurfacing and Drainage Improvements	\$500,000	\$341,121	\$341,121	\$0	No	N/A
SGRC-104	Irwin	01	PI-0016266	Fifth Street Ext. Paving	\$500,000	\$542,099	\$375,363	\$166,736	No	Inflation applied to Original Estimated Cost; updated Project Budget \$542,099
SGRC-105	Lanier	01	PI-0016267	River Road Widen and Resurface	\$3,250,000	\$1,603,059	\$1,603,059	\$0	No	N/A
SGRC-106	Lanier	01	PI-0016268	Boyette Road Widen and Resurface	\$1,700,000	\$976,944	\$976,944	\$0	No	N/A
SGRC-107	Lanier	01	PI-0016269	Giddens Road/Royals Road Resurface	\$770,000	\$606,378	\$606,378	\$0	No	N/A
SGRC-109	Lowndes	01	PI-0010297	I-75 @ SR 31 - Phase II (Exit 11)	\$19,445,000	\$19,445,000	\$4,661,689	\$12,151,943	No	Blended Project - Total Project Cost \$53,200,024
SGRC-110	Lowndes	01	PI-0016271	Old 41 N. Widening	\$6,516,800	\$6,516,800	\$4,264,451	\$1,718,220	No	N/A
SGRC-113	Lowndes	01	PI-0016274	Clyattstone Road/Simpson Lane Paving and Drainage Improvements	\$2,300,000	\$2,400,000	\$2,400,000	\$0	No	Inflation applied to Original Estimated Cost; updated Project Budget \$2,400,000
SGRC-115	Lowndes	01	PI-0016276	Hightower Road/Cooper Road NE Paving and Drainage Improvements	\$3,750,000	\$3,750,000	\$1,552,682	\$1,036,682	No	N/A
SGRC-116	Lowndes	01	PI-0016277	Hickory Grove Road Bridge Replacement	\$2,700,000	\$2,699,434	\$2,699,434	\$0	No	N/A
SGRC-123	Lowndes	01	PI-0016284	New Air Traffic Control Tower at Valdosta Regional Airport	\$2,705,000	\$2,705,000	\$411,425	\$171,116	No	N/A
SGRC-130	Pierce	01	PI-0016291	City of Patterson Resurfacing Bundle Phase 1	\$2,750,000	\$1,097,754	\$1,097,754	\$0	No	N/A
SGRC-131	Pierce	01	PI-0016292	City of Blackshear Session Hill Resurfacing Bundle	\$1,500,324	\$1,200,330	\$1,200,330	\$0	No	N/A
SGRC-133	Pierce	01	PI-0016294	Ware Street Widen and Resurface	\$2,600,000	\$1,853,438	\$1,853,438	\$0	No	N/A
SGRC-134	Pierce	01	PI-0016295	St. Johns Church Road Widen and Resurface	\$2,440,300	\$1,422,578	\$1,422,578	\$0	No	N/A
SGRC-135	Pierce	01	PI-0016296	Golf Course Road Alignment, Drainage and Resurfacing	\$3,408,000	\$3,408,000	\$46,800	\$199,415	No	N/A
SGRC-142	Tift	01	PI-0016302	8th Street Widening for Turn Lane	\$941,600	\$1,512,063	\$267,477	\$983,107	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-143	Tift	01	PI-0016303	2nd Street Resurfacing	\$1,081,600	\$847,786	\$847,786	\$0	No	N/A
SGRC-145	Tift	01	PI-0016305	Taxiway Improvements at Henry Tift Myers Airport	\$5,600,000	\$5,600,000	\$3,085,325	\$1,743,090	No	N/A
SGRC-148	Turner	01	PI-0016308	City of Ashburn Resurfacing Bundle and Sidewalk Improvements	\$1,000,000	\$940,431	\$50,084	\$890,347	No	N/A
SGRC-153	Ware	01	PI-0016312	Albany Avenue Widen and Resurfacing	\$1,600,000	\$1,843,143	\$1,131,784	\$711,359	No	Inflation applied to Original Estimated Cost; updated Project Budget \$1,843,143

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-002	Atkinson	02	PI-0016171	Cogdell Road Widen and Resurface	\$2,359,000	\$2,359,000	\$57,789	\$0	No	N/A
SGRC-012	Bacon	02	PI-0016181	Johnson Lake Road Widening and Safety Improvements	\$3,000,000	\$3,000,000	\$41,567	\$103,474	No	N/A
SGRC-013	Bacon	02	PI-0016182	SR 32 Passing Lanes Between Alma to Douglas	\$536,000	\$1,093,745	\$784,573	\$225,619	Yes	Blended Project (State Funds) - Total Project Cost \$8,242,107. GDOT is actively managing the design phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-017	Ben Hill	02	PI-0016186	Bethlehem Church Road Bridge at House Creek Bridge Replacement	\$1,500,000	\$1,500,000	\$0	\$0	No	N/A
SGRC-018	Ben Hill	02	PI-0016187	Bethlehem Church Road Bridge at Otter Creek Bridge Replacement	\$1,000,000	\$1,000,000	\$0	\$0	No	N/A
SGRC-019	Ben Hill	02	PI-0016188	Peachtree Road Corridor Realigning, Widening, and Intersection Improvements	\$913,200	\$1,202,777	\$555,749	\$271,644	No	Blended Project (State Funds) - Total Project Cost \$6,202,777. Inflation applied to Original Estimated Cost; updated Project Budget \$1,202,777.
SGRC-021	Ben Hill	02	PI-0016190	Fitzgerald Perimeter Roads Improvements (Widen, Resurface, C/G)	\$5,165,192	\$5,165,192	\$0	\$45,418	No	N/A
SGRC-030	Brantley	02	PI-0016198	Cherry Street Resurfacing	\$367,317	\$367,317	\$6,083	\$128,901	No	N/A
SGRC-033	Brooks	02	PI-0016201	DeVane Road Bridge Replacement, Widen and Resurface	\$4,000,000	\$4,128,843	\$546,698	\$216,012	No	Inflation applied to Original Estimated Cost; updated Project Budget \$4,128,843
SGRC-049	Clinch	02	PI-422390-	SR 89/US441 from Orange St in Homerville to CR 101/Cowart Rd	\$6,625,000	\$1,625,000	\$615,906	\$175,854	No	Blended Project - Total Project Cost \$38,206,454. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-071	Coffee	02	PI-0016235	Bud Hutcheson Road Paving	\$2,798,000	\$2,798,000	\$110,380	\$83,823	No	N/A
SGRC-078	Coffee	02	PI-0016241	Hwy 149/Youngie Fussell Road/Bridgetown Road Widen and Resurface	\$850,000	\$1,740,174	\$291	\$1,564,662	Yes	Blended Project - Total Project Cost \$5,140,174. Project exceeded original estimated cost. GDOT managed costs to keep overruns at a minimum. Inflation also applied to Original Estimated Cost.
SGRC-082	Coffee	02	PI-0016245	S. Gaskin Avenue Sidewalk and Drainage Improvements	\$657,100	\$957,396	\$32,473	\$222,502	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-092	Cook	02	PI-0016254	Tillman Road Bypass Phase 3 Improvements	\$4,900,000	\$4,900,000	\$0	\$0	No	N/A
SGRC-095	Cook	02	PI-0016257	Valdel Road Resurfacing	\$2,007,500	\$2,581,522	\$0	\$2,401,234	Yes	GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-111	Lowndes	02	PI-0016272	Shiloh Road Resurfacing and Bridge Replacement	\$5,600,000	\$5,602,002	\$341,182	\$13,647	No	Inflation applied to Original Estimated Cost; updated Project Budget \$5,602,002
SGRC-114	Lowndes	02	PI-0016275	Briggston Road Paving and Drainage Improvements	\$2,525,000	\$2,525,000	\$146,209	\$244,771	No	N/A
SGRC-124	Lowndes	02	PI-0016285	Old Clyattville Road Widening - Valdosta	\$6,217,514	\$6,230,827	\$457,510	\$27,001	No	Inflation applied to Original Estimated Cost; updated Project Budget \$6,230,827
SGRC-126	Lowndes	02	PI-0016287	S Patterson Street at Griffin Avenue Intersection and Drainage Improvements	\$1,258,000	\$1,258,000	\$56,573	\$319,067	No	N/A
SGRC-127	Lowndes	02	PI-0016288	St Augustine Road at Gornto Road Intersection and Drainage Improvements	\$2,510,100	\$2,510,100	\$189,904	\$224,475	No	N/A

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-129	Lowndes	02	PI-0016290	Baytree Road at Gornito Road Intersection and Signal Improvements	\$2,734,000	\$2,734,000	\$145,020	\$10,260	No	N/A
SGRC-132	Pierce	02	PI-0016293	Pierce County Horseshoe Road/Fletcher Road Area Resurfacing Bundle	\$681,890	\$1,207,896	\$0	\$790,508	Yes	Blended Project - Total Project Cost \$2,207,896. GDOT is actively managing the construction phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-136	Pierce	02	PI-0016297	US 84 Intersection and Signal Improvements from County Farm Road to	\$3,500,000	\$3,500,000	\$626,244	\$171,627	No	Blended Project (State Funds) - Total Project Cost \$8,500,000
SGRC-137	Tift	02	PI-0016298	Upper Ty Ty Road Bridge Replacement over Little River	\$2,710,000	\$2,710,000	\$29,499	\$70,650	No	N/A
SGRC-139	Tift	02	PI-0016299	Scotterville Road Bridge Replacement over Little Creek	\$1,410,000	\$1,410,000	\$102,650	\$1,005,485	No	N/A
SGRC-140	Tift	02	PI-0016300	Omega-Eldorado Road Bridge Replacement over Arnold Creek	\$1,911,000	\$1,911,000	\$143,918	\$705,607	No	N/A
SGRC-141	Tift	02	PI-0016301	Omega-Eldorado Road Bridge Replacement over Little River	\$2,582,250	\$2,582,250	\$30,308	\$72,588	No	N/A
SGRC-146	Tift	02	PI-0016306	12th Street at Prince Avenue Intersection Improvements	\$2,285,500	\$2,285,500	\$0	\$0	No	N/A
SGRC-149	Turner	02	PI-0016309	Hobby Road Paving	\$1,400,000	\$1,400,000	\$33,694	\$26,194	No	N/A
SGRC-150	Turner	02	PI-0016310	Glynn Cook Road Paving	\$620,000	\$620,000	\$5,149	\$0	No	N/A
SGRC-151	Turner	02	PI-0016311	Reid Road Paving	\$2,400,000	\$2,400,000	\$16,892	\$35,339	No	N/A
SGRC-152	Ware	02	PI-0013605	US 84 Bridge over Satilla River	\$3,650,000	\$3,650,000	\$309,861	\$349,373	No	Blended Project - Total Project Cost \$37,771,579
SGRC-154	Ware	02	PI-0016313	Knight Avenue Resurfacing	\$650,000	\$591,061	\$591,061	\$0	No	N/A
SGRC-028	Brantley	03	PI-0015536	SR520/US82 @Satilla River Overflow 14 mi east of Hoboken	\$900,000	\$200,000	\$0	\$200,000	No	Blended Project - Total Project Cost \$9,745,450. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-040	Charlton	03	PI-0000821	SR 40 from SR40 Conn to 0.36 mi east of May Bluff Rd	\$2,635,000	\$2,100,000	\$476,503	\$52,290	No	Blended Project - Total Project Cost \$14,850,399. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-048	Clinch	03	PI-0016215	Homerville Bypass Resurfacing, Bridge Replacement and Other Improvements	\$3,000,000	\$3,000,000	\$2,310	\$208,231	No	N/A
SGRC-077	Coffee	03	PI-0016240	SR 158 Passing Lanes in Coffee County	\$3,428,000	\$1,428,000	\$372,335	\$549,081	No	Blended Project (State Funds) - Total Project Cost \$8,428,000. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-081	Coffee	03	PI-0016244	McDonald Road Sidewalk and Drainage Improvements	\$1,341,800	\$1,341,800	\$0	\$0	No	N/A
SGRC-083	Coffee	03	PI-0016246	Chester Avenue Sidewalk and Drainage (Culvert) Improvements	\$2,846,200	\$2,846,200	\$0	\$0	No	N/A
SGRC-084	Coffee	03	PI-0016247	West Green Hwy (SR 135/US 221) Sidewalk Improvements	\$560,200	\$560,200	\$0	\$0	No	N/A
SGRC-086	Coffee	03	PI-0016248	Lupo Lane Sidewalk and Drainage Improvements	\$674,400	\$674,400	\$37,588	\$5,196	No	N/A

Southern Georgia
Annual Report - TIA Funds Only
Report covers: November 8, 2022 - October 30, 2023

Project ID	County	Band	GDOT ID	Description	Original Estimated Cost	Current Estimated Cost	Prior Years	Current Year	Corrective Action Required?	Comments
SGRC-087	Coffee	03	PI-0016249	Baker Hwy, East (SR 158) Sidewalk Improvements	\$694,600	\$694,600	\$28,180	\$8,555	No	N/A
SGRC-088	Coffee	03	PI-0016250	West Walker Street Sidewalk Improvements	\$433,900	\$433,900	\$0	\$0	No	N/A
SGRC-089	Coffee	03	PI-0016251	Road Improvements at Douglas Municipal Airport	\$150,000	\$150,000	\$0	\$0	No	N/A
SGRC-108	Lowndes	03	PI-0016270	Old Clyattville Road Widening - Lowndes	\$21,200,000	\$21,200,000	\$0	\$543,850	No	N/A
SGRC-112	Lowndes	03	PI-0016273	Orr Road Extension	\$1,175,000	\$1,175,000	\$0	\$0	No	N/A
SGRC-117	Lowndes	03	PI-0016278	Kinderlou Clyattville Road Paving and Drainage Improvements	\$3,450,000	\$3,450,000	\$54,000	\$99,206	No	N/A
SGRC-118	Lowndes	03	PI-0016279	Coleman Road NW Paving and Drainage Improvements	\$2,300,000	\$2,300,000	\$0	\$37,393	No	N/A
SGRC-119	Lowndes	03	PI-0016280	Twin Lakes Road Paving and Drainage Improvements	\$2,100,000	\$2,100,000	\$0	\$25,500	No	N/A
SGRC-120	Lowndes	03	PI-0016281	Hall Road Paving, Drainage and Other Improvements	\$3,700,000	\$3,700,000	\$0	\$0	No	N/A
SGRC-121	Lowndes	03	PI-0016282	Country Club Drive Widening	\$800,800	\$1,536,660	\$310,274	\$223,755	Yes	Blended Project (State Funds) - Total Project Cost \$8,000,000. GDOT is actively managing the design phase of this project to reduce costs and control cost variance. Inflation also applied to Original Estimated Cost.
SGRC-122	Lowndes	03	PI-0016283	St. Augustine Road RR Grade Separation	\$8,900,000	\$3,162,536	\$54,101	\$367,976	No	Blended Project (State Funds) - Total Project Cost \$18,900,000. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-125	Lowndes	03	PI-0016286	St Augustine Road at Norman Drive Intersection, Drainage and Signal	\$3,988,700	\$3,988,700	\$296,133	\$249,848	No	N/A
SGRC-128	Lowndes	03	PI-0016289	Forrest Street Widening	\$20,301,700	\$20,301,700	\$511,307	\$362,365	No	N/A
SGRC-138	Tift	03	PI-0010318	I-75 @ CR421/Chula Brookfield Rd - Phase II (Exit 69)	\$3,155,000	\$1,800,000	\$491,611	\$551,412	No	Blended Project (State Funds) - Total Project Cost \$20,905,000. TIA and HB170 funds adjusted to accommodate band change request for PI-421345-
SGRC-144	Tift	03	PI-0016304	McCormick Drive Widening and Realignment	\$3,500,000	\$3,500,000	\$0	\$0	No	N/A
SGRC-147	Tift	03	PI-0016307	18th Street Ditch Bridge Replacements (5 Culverts)	\$1,869,400	\$1,869,400	\$0	\$0	No	N/A
	Regional	Multiple	PI-A000835	Program Administration	\$18,491,374	\$18,491,374	\$5,074,470	\$983,121	No	N/A
Total					\$315,254,826	\$309,888,013	\$89,471,287	\$43,084,512		

Nov 7, 2023

9:24:03 AM

Southern Georgia - 2023 Completed Project & Benefit Report

All projects listed within this report have met the stated public benefit as detailed in the Southern Georgia TIA Final Investment List (2018).

Ben Hill County

Summary of Work: 5.4 miles of plant mix resurfacing on sections of Evergreen Road in Ben Hill County and the City of Fitzgerald.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-020	PI-0016189	Evergreen Road Resurfacing – Ben Hill	\$688,300	\$949,608	Local Let
SGRC-023	PI-0016192	Evergreen Road Resurfacing - Fitzgerald	\$523,500	\$523,500	Local Let

Clinch County

Summary of Work: 0.34 miles of grade, drain, base and paving on Oak Lane in the City of Argyle.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-047	PI-0016214	Oak Lane Resurfacing	\$300,000	\$260,009	Local Let

Coffee County

Summary of Work: 11 miles of shoulder widening and plant mix resurfacing on Youngie Fussell Road/ Bridgetown Road and 4.4 miles of SR 32 widened from two to five lanes just west of the City of Douglas.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-078	PI-0016241	Youngie Fussell Road/ Bridgetown Road Resurfacing*	\$850,000	\$1,740,174	TIA Let
SGRC-072	PI-421345-	SR 32 Widening from just West of Troy Carter Road to the Westside Douglas City Limits*	\$9,780,000	\$27,003,849	GDOT-OPD Let

* Featured project. See attached sheet for additional details.

Southern Georgia - 2023 Completed Project & Benefit Report, Continued

Cook County

Summary of Work: 9.2 miles of plant mix resurfacing on Val Del Road from US 41 to the Lowndes County line, and .22 miles of grade, drain, base and paving of Taylor Street and East Revels Street in the City of Lenox.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-095	PI-0016257	Val Del Road Resurfacing*	\$2,007,500	\$2,581,522	TIA Let
SGRC-096	PI-0016258	Taylor Street Paving	\$276,900	\$107,033	Local Let
SGRC-097	PI-0016259	East Revels Street Paving	\$450,000	\$179,008	Local Let

* Featured project. See attached sheet for additional details.

Lowndes County

Summary of Work: 2.8 miles of Old US 41 North widened to include sections of either three lanes or five lanes from SR 7 to Union Road, northwest of the City of Valdosta.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-110	PI-0016271	Old US 41 North Widening from SR 7 to Union Road*	\$6,516,800	\$6,516,800	Local Let

* Featured project. See attached sheet for additional details.

Tift County

Summary of Work:

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-145	PI-0016305	Taxiway Improvements at Henry Tift Myers Airport*	\$5,600,000	\$5,600,000	Local Let

* Featured project. See attached sheet for additional details.

Southern Georgia - 2023 Completed Project & Benefit Report, Continued

Turner County

Summary of Work: 4.2 miles of plant mix resurfacing and sidewalk construction on several streets in the City of Ashburn.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-148	PI-0016308	City of Ashburn Resurfacing Bundle and Sidewalk Improvements	\$1,000,000	\$940,431	Local Let

Ware County

Summary of Work: 1.35 miles of improvements to drainage, city water and sewer on Albany Avenue. Project also included reconstruction of portions of sidewalk, curb and gutter as well as plant mix resurfacing.

Project ID	GDOT ID	Project Name	Original Estimated Cost	Final Projected Cost	Project Let By
SGRC-153	PI-0016312	Albany Avenue Widening and Resurfacing*	\$1,600,000	\$1,843,143	Local Let

* Featured project. See attached sheet for additional details.

Completed Project & Benefits Review Report

Southern Georgia



Project: Youngie Fussell Road/Bridgetown Road Widening and Resurfacing
County: Coffee
Project ID: SGRC-078
GDOT ID: PI-0016241

Project Description

This project included 11 miles of asphalt patching, shoulder widening, leveling and resurfacing on Youngie Fussell Road/Bridgetown Road from SR 32 to the Atkinson County line.

Project Benefit

This project has benefited the public by enhancing safety by providing drivers with a wider driving space with accessible shoulders, as well as a smoother, durable surface. It also reduced the county's road maintenance costs.

Schedule Information

NTP Date: 07.25.22

Completion Date: 08.18.23

Budget / Cost Information

Original Budget: \$850,000

Projected Final Cost: \$1,740,174

Project Delivery

TIA Let


Project construction managed by Georgia DOT

Project Photos

Pre-Construction



Completed

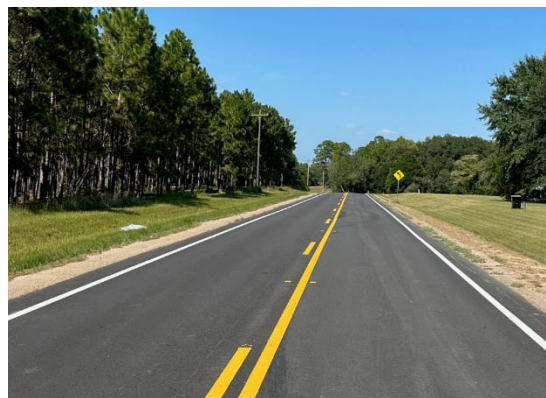

Completed Project & Benefits Review Report

Southern Georgia



Project: SR 32 Widening from just West of Troy Carter Road to the Westside Douglas City Limits
County: Coffee
Project ID: SGRC-072
GDOT ID: PI-421345-

Project Description

This project involved the widening and reconstruction of 4.4 miles of SR 32 from two to five lanes including a 14-foot flushed median and 10-foot shoulders with roadside ditches, from the CSX Railroad bridge west of Troy Carter Road to the westside Douglas city limits.

Project Benefit

This project has benefited the public by anticipating traffic growth in the county, particularly commercial trucks. In addition to providing a wider, more efficient corridor that allows for vehicles to safely pass and potentially reduce crash frequency, the project also supported future industrial development by enhancing access to modal facilities.

Schedule Information

NTP Date: 06.23.20

Completion Date: 12.28.23

Budget / Cost Information

Original Budget: \$9,780,000

Projected Final Cost: \$27,003,849

NOTE: Project budget adjusted to accommodate band change request

Project Delivery

GDOT-OPD Let

Project construction managed by Georgia DOT

Project Photos

Pre-Construction



Completed



Completed Project & Benefits Review Report

Southern Georgia



Project: Val Del Road Resurfacing from US 41 to Lowndes County Line
County: Cook
Project ID: SGRC-095
GDOT ID: PI-0016257

Project Description

This project consisted of 9.2 miles of asphalt patching, leveling and resurfacing on Val Del Road, starting at US 41 and ending at the Lowndes County line.

Project Benefit

This project has benefited the public by enhancing safety by providing motorists with a smooth, durable traveling surface. It also reduced the county's road maintenance costs, as well as the vehicle maintenance costs of local and commercial drivers.

Schedule Information

NTP Date: 07.22.22

Completion Date: 04.14.23

Budget / Cost Information

Original Budget: \$2,007,500

Projected Final Cost: \$2,581,522

Project Delivery

TIA Let

Project construction managed by Georgia DOT

Project Photos

Pre-Construction



Completed



Completed Project & Benefits Review Report

Southern Georgia



Project: Old US 41 North Widening from SR 7 to Union Road
County: Lowndes
Project ID: SGRC-110
GDOT ID: PI-0016271

Project Description

This project consisted of the widening of 2.8 miles of Old US 41 North to include sections of either three lanes or five lanes from SR 7 to Union Road, northwest of the City of Valdosta.

Project Benefit

This project has benefited the public by anticipating traffic growth in the county, particularly commercial trucks. In addition to providing a wider, more efficient corridor that allows for vehicles to safely pass and potentially reduce crash frequency, the project also supported future industrial development by enhancing access to modal facilities.

Schedule Information

NTP Date: 05.17.21

Completion Date: 07.14.23

Budget / Cost Information

Original Budget: \$6,516,800

Projected Final Cost: \$6,516,800

Project Delivery

Local Let

Project construction managed by Lowndes County

Project Photos

Pre-Construction



Completed



Completed Project & Benefits Review Report

Southern Georgia



Project: Taxiway Improvements at Henry Tift Myers Airport
County: Tift
Project ID: SGRC-145
GDOT ID: PI-0016305

Project Description

This project resurfaced the regional airport's existing runway and taxiways and restriped them with durable high-visibility paints.

Project Benefit

This project has benefited the public by making the necessary upgrades to bring Henry Tift Myers Airport into compliance with federal standards.

Schedule Information

NTP Date: 07.01.2021
Completion Date: 08.25.2023

Budget / Cost Information

Original Budget: \$5,600,000
Projected Final Cost: \$5,600,000

Project Delivery

Local Let
Project construction managed by Tift County Airport Authority

Project Photos

Pre-Construction



Completed



Completed Project & Benefits Review Report

Southern Georgia



Project: Albany Avenue Widening and Resurfacing
County: Ware
Project ID: SGRC-153
GDOT ID: PI-0016312

Project Description

This project consisted of 1.35 miles of improvements to drainage, city water and sewer on Albany Avenue. It also included reconstruction of portions of sidewalk, curb and gutter as well as plant mix resurfacing.

Project Benefit

This project improved the city's drainage, water and sewer system throughout the project length, benefitting the community with new, upgraded facilities that will reduce city maintenance expenses and extend the life of the overall infrastructure. The resurfacing provides an added benefit of safety to drivers with a smooth, durable roadway.

Schedule Information

NTP Date: 04.05.21
Completion Date: 07.14.23

Budget / Cost Information


Original Budget: \$1,600,000
Projected Final Cost: \$1,843,143

Project Delivery


Local Let
Project construction managed by City of Waycross

Project Photos

Pre-Construction

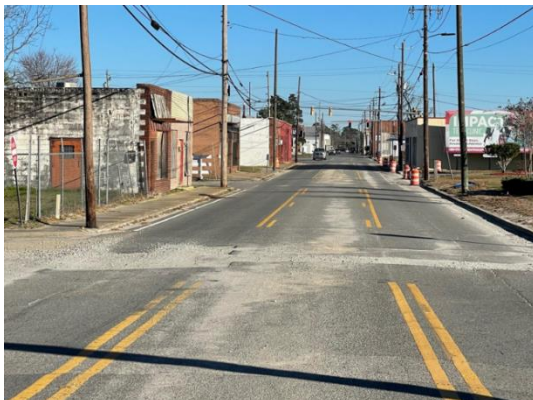

Completed

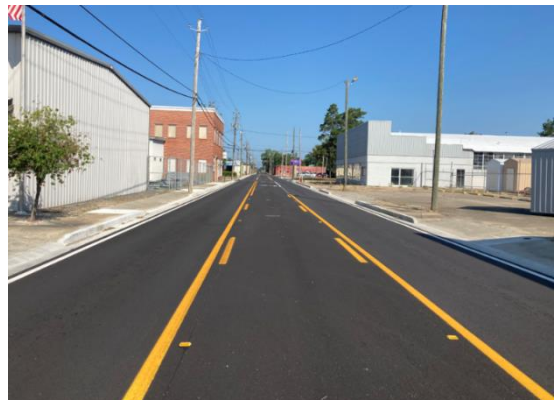

TIA Citizens Review Panel Agenda
Thursday, July 20, 2023; 2:00 p.m.
Berrien County Administrative Building
201 North Davis Street
Nashville, GA 31639

I. Call to Order	Chair
II. Introductions/Roll Call	Chair
III. Approval of Minutes – March 21, 2023	Chair
IV. Public Comment	Chair
V. New Business	Chair
A. TIA 2 Update	SGRC Staff
B. TIA Update	Kenneth Franks
VI. SGRC Staff Update	SGRC Staff
VII. Privilege of the Floor	Chair
VIII. Next Meeting Date, Place, Time	Chair
IX. Adjournment	Chair

Minutes
TIA Citizens Review Panel
Berrien County Administrative Building
March 21, 2023
2:00 PM

Members Present	Organization
Bill Slaughter	Lowndes County
Walter Hudson	Irwin County
Robert Griner	Berrien County
Patrick Jones	Pierce County
D.W. Harper	Irwin County
Others Present	
Kenneth Franks	GDOT TIA Office
Erik Wilkinson	GDOT TIA Office
Brent Moseley	GDOT TIA Office
Penny Brooks	GDOT TIA Office
Elizabeth Backe	SGRC
Kimberly Hobbs	SGRC

CRP Item #1 - Call to Order

Mr. Slaughter called the meeting to order at 2:01 pm.

CRP Item #2 - Introductions/Roll Call

Mr. Slaughter asked those present to introduce themselves and state their affiliation with the committee.

CRP Item #3 – Approval of Minutes – March 21, 2023

Mr. Slaughter gave the committee time to review the minutes. Mr. Hudson made a motion to approve the minutes. Mr. Griner made a motion in the second. The vote was unanimous; the motion carried.

CRP Item #4 – Public Comment

Mr. Slaughter opened the floor for public comments. There were no comments.

CRP Item #5 – New Business

A. TIA Timeline, SPLOST/ELOST Dates Discussion

Ms. Backe passed out a spreadsheet for both the SPLOST and ELOST for the 18 counties in the Southern Georgia Region. She explained that these were the upcoming expiration dates for the SPLOST / ELOST so that the committee could have a better idea of what other sales taxes would have an upcoming reimposition referendum around the same time as the TSPLOST referendum. Mr. Slaughter asked if she would also email the spreadsheet to the TIA CRP members. Ms. Backe responded that she would send it out as soon as she was back in the office. A discussion about the project submission process ensued.

CRP Item # 6 – TIA Update

Mr. Franks provided the panel with an update on the status of the TIA program. Mr. Franks stated that the Southern Georgia Region continues to be in a good place with TIA revenue as the monies collected has been above the projected revenue and currently cover the entire cost of projects in the first four years. Mr. Franks continued that based on the most recent projections, the current TIA is still on track to end in FY2026. Mr. Franks also stated that the State Economist predicts a potential drop in collections. Mr. Franks continued that the GDOT TIA office have held back funds to account for inflation. Mr. Moseley presented the status of current projects and upcoming projects that will be let in the next 6 months.

Mr. Franks stated for the upcoming TIA, the State Economist is projecting TIA II revenues to be about \$800 million. Mr. Slaughter stated that during the last TIA process, there was a spreadsheet with population and LARC formula calculations to enable decision making. Ms. Backe stated that the spreadsheet was being created and would be sent out in the next few months as the next Regional Transportation Roundtable meeting will be held on May 17, 2023.

CRP Item # 7 – Privilege of the Floor

There were no comments

CRP Item # 8– Next Meeting Date, Place, Time

Mr. Slaughter asked the committee what would be a good day and time for the next meeting. The committee agreed that the next meeting will be held on Thursday, July 20, 2022 @ 2:00

p.m. at the Berrien County Courthouse. Mr. Slaughter made a motion to adjourn the meeting. The meeting was adjourned.

TIA Citizens Review Panel Agenda
Wednesday, November 8, 2023; 9:00 am
Berrien County Administrative Building
201 North Davis Street
Nashville, GA 31639

- | | |
|---|-----------------------|
| I. Call to Order | Chair |
| II. Introductions/Roll Call | Chair |
| III. Approval of Minutes – July 20, 2023 | Chair |
| IV. Public Comment | Chair |
| V. New Business | Chair |
| A. Band Change Requests – Lowndes County | Chair |
| B. TIA 2 Update | SGRC Staff |
| C. TIA Update | Kenneth Franks |
| VI. Privilege of the Floor | Chair |
| VII. Next Meeting Date, Place, Time | Chair |
| VIII. Adjournment | Chair |

Minutes
TIA Citizens Review Panel
Berrien County Administrative Building
July 20, 2023
2:00 PM

Members Present	Organization
Bill Slaughter	Lowndes County
Walter Hudson	Irwin County
Robert Griner	Berrien County
D.W. Harper	Irwin County
Patrick Jones	Pierce County
Others Present	
Kenneth Franks	GDOT TIA Office
Brent Moseley	GDOT TIA Office
Penny Brooks	GDOT TIA Office
Amy Martin	SGRC

CRP Item #1 - Call to Order

Mr. Slaughter called the meeting to order at 2:00 pm.

CRP Item #2 - Introductions/Roll Call

Mr. Slaughter asked those present to introduce themselves and state their affiliation with the committee.

CRP Item #3 – Approval of Minutes – July 20, 2023

Mr. Slaughter gave the committee time to review the minutes. Mr. Harper made a motion to approve the minutes. Mr. Griner made a motion in the second. The vote was unanimous; the motion carried.

CRP Item #4 – Public Comment

Mr. Slaughter opened the floor for public comments. There were no comments.

CRP Item #5 – New Business

A. TIA 2 Update

Ms. Martin explained to the committee that the TIA 2 process was moving along and the submission portal was open and would be closing soon. She continued that once the submission portal closes, all of the projects will be moved over to a spreadsheet for GDOT TIA office staff to review.

B. TIA Update

Mr. Franks provided the panel with an update on the status of the TIA program. Mr. Franks stated that they are almost a year into Band 2 projects and it would not be much longer before we start looking at Band 3 projects. Mr. Moseley gave a brief update on the status of current and upcoming GDOT and Local let TIA projects. He stated that 26 projects are in the construction, 81 projects are complete and 120.8 million has gone to the projects.

CRP Item # 7 – Privilege of the Floor

There were no comments.

CRP Item # 8– Next Meeting Date, Place, Time

Mr. Slaughter asked the committee what would be a good day and time for the next meeting. The committee agreed that the next meeting will be held on Wednesday, November 8th @ 2:00 p.m. at the Berrien County Administrative Building. The meeting was adjourned by acclamation.

Lowndes County
Board of Commissioners
Bill Slaughter, Chairman



Joyce E. Evans, District 1
Scott Crenstein, District 2
Mark Wisenbaker, District 3
Demarcus Marshall, Ph.D. District 4
Clay Griner, District 5

Post Office Box 1349 • Valdosta, GA 31603-1349 • Phone (229) 671-2400 • Fax (229) 245-5222

October 4, 2023

Ms. Amy Martin
1937 Carlton Adams Drive
Valdosta, GA 31601

Amy,

Per my discussions with Brent Mosley with the GDOT TIA office regarding the timing and need for a change in band year for the Coleman Road Paving project (0016279), Mr. Mosley advised me of the process for change in priority and band year. Mr. Mosley stated that collections were up by greater than 10% over the projected amounts and that there should be ample revenue in band 2 projects for this project.

Therefore, Lowndes County is requesting that TIA Project Number 0016279 known as the Coleman Road Project be moved from Band 3 into Band 2 due to the need regarding increased traffic and safety in this area. The estimated cost for this project is \$2,300,000. Lowndes County anticipates that it will take approximately 18-24 months from approval for the band change until we would be ready to let the project for construction. Therefore, we would anticipate a summer 2024 letting.

We look forward to hearing from you regarding the presentation of our request to the local roundtable at the meeting in November.

Respectfully Submitted,

Michael Fletcher, P.E.
Lowndes County Engineer

Cc: Bill Slaughter, Chairman
Brent Moseley, GDOT TIA Regional Coordinator

Lowndes County
Board of Commissioners
Bill Haughter, Chairman



Joyce E. Evans, District 1
Scott Orenstein, District 2
Mark Wisenbaker, District 3
Demarcus Marshall, Ph.D. District 4
Clay Griner, District 5

Post Office Box 1349 • Valdosta, GA 31603-1349 • Phone (229) 671-2400 • Fax (229) 245-5222

October 4, 2023

Ms. Amy Martin
1937 Carlton Adams Drive
Valdosta, GA 31601

Amy,

Per my discussions with Brent Mosley with the GDOT TIA office regarding the timing and need for a change in band year for the Kinderlou-Clyattville Road Paving project (0016278), Mr. Mosley advised me of the process for change in priority and band year. Mr. Mosley stated that collections were up by greater than 10% over the projected amounts and that there should be ample revenue in band 2 projects for this project.

Therefore, Lowndes County is requesting that TIA Project Number 0016278 known as the Kinderlou-Clyattville Road Project be moved from Band 3 into Band 2 due to the need regarding increased traffic and safety in this area. The estimated cost for this project is \$3,450,000. Lowndes County anticipates that it will take approximately 18-24 months from approval for the band change until we would be ready to let the project for construction. Therefore, we would anticipate a summer 2024 letting.

We look forward to hearing from you regarding the presentation of our request to the local roundtable at the meeting in November.

Respectfully Submitted,



Michael Fletcher, P.E.
Lowndes County Engineer

Cc: Brent Moseley, GDOT TIA Regional Coordinator
