



Georgia Department of Transportation


Transportation Investment Act

Southern Georgia

March 18, 2025 CRP Update



TIA Regions




TIA Collections thru January 2025

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
CSRA	\$224,328,204*	\$168,246,153*	\$56,082,051*
River Valley	\$144,764,809*	\$108,573,607*	\$36,191,202*
Heart of Georgia	\$102,967,427*	\$77,225,570*	\$25,741,857*
Southern Georgia	\$432,551,392*	\$324,413,544*	\$108,137,848*
Totals (*rounded amounts)	\$904,611,832	\$678,458,874	\$226,152,958

TIA Collections thru January 2025


Region	Original Revenue Forecast	Actual Revenue Collected	% Ahead of Forecast
CSRA	\$174,752,614*	\$224,328,204*	28.4%
River Valley	\$124,317,975*	\$144,764,809*	16.4%
Heart of Georgia	\$75,390,897*	\$102,967,427*	36.6%
Southern Georgia	\$318,849,519*	\$432,551,392*	35.7%
Totals (*rounded amounts)	\$693,311,005	\$904,611,832	30.5%

Southern Georgia Timeline

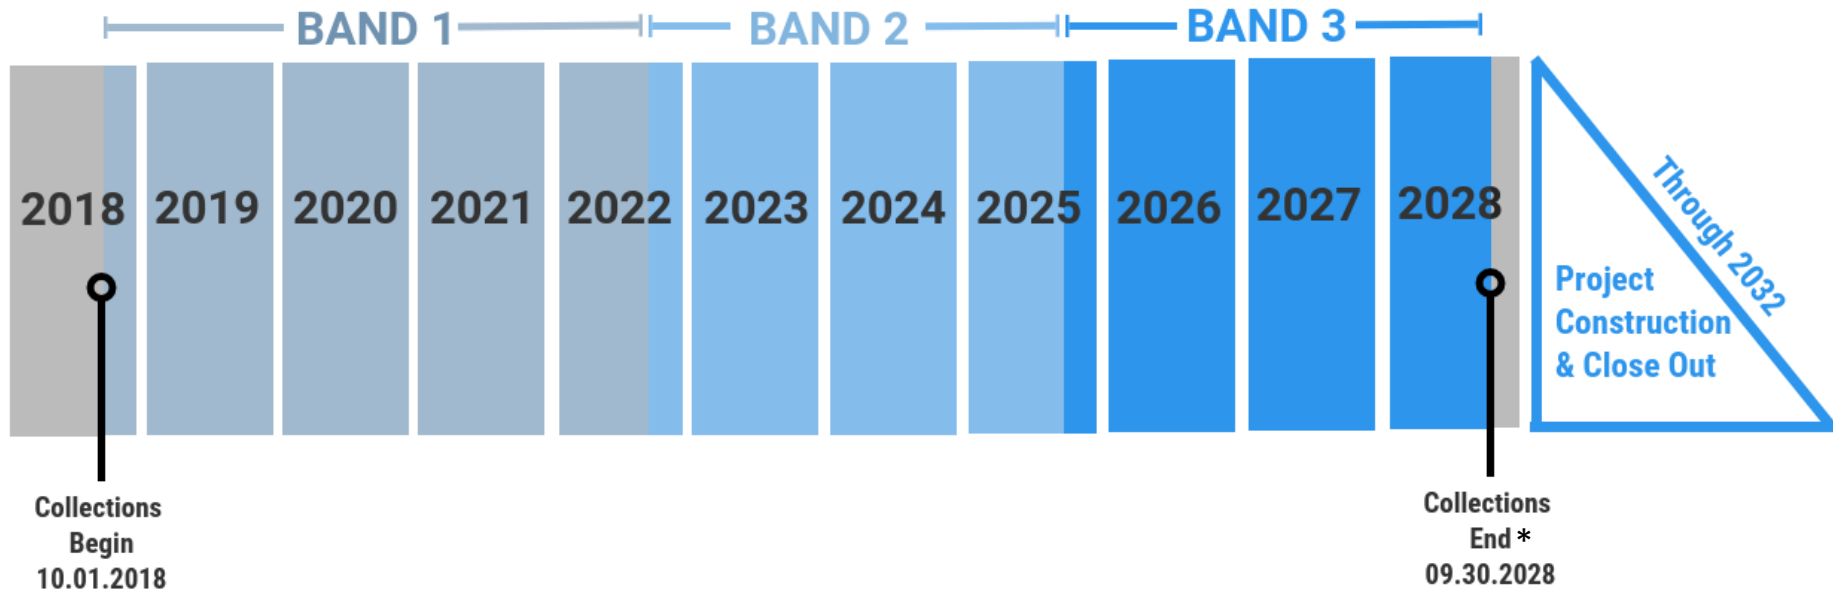

* Should revenue meet the projected max prior to the legislated end date, collections will end early.

Southern GA Project Overview



151

Total Projects

\$408,763,452

Final Investment List
Project Total

15

In Construction

106


Projects Completed

\$174,746,907

Total TIA Expenditure to Date
(as of 3/14/25)

Projects Let since December


PI Number	Project Name	County	Let Date	Project Type	Original Total Budget	Bid Amount
0016307	18th Street Ditch Bridge Replacements (5 Culverts)	Tift / Tifton	Feb 2025	Bridge / Culvert	\$1,869,400	\$2,099,265.69

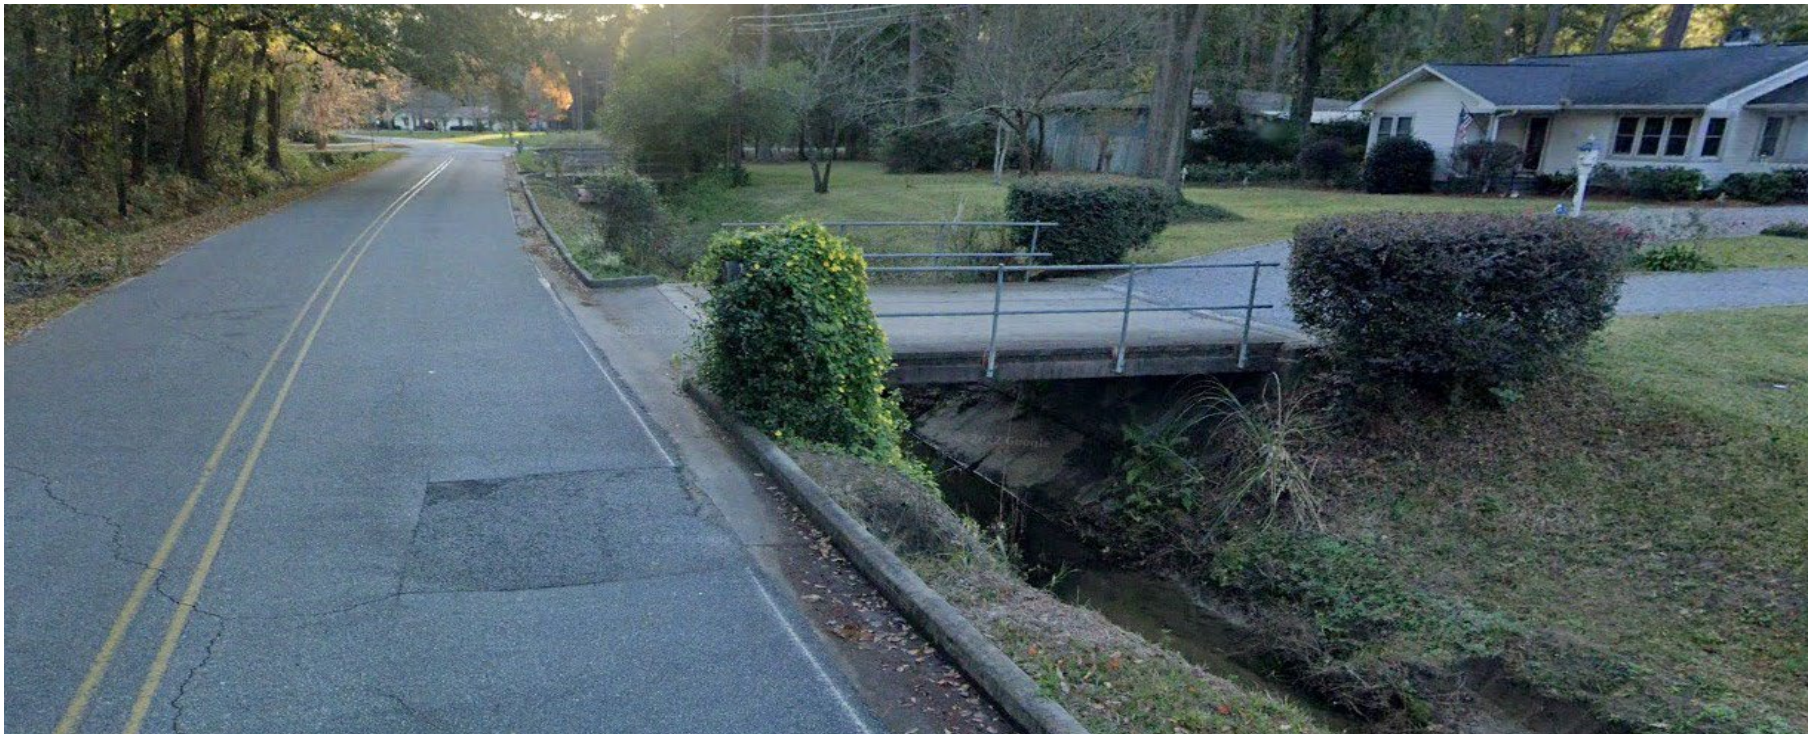

TIA Letting Forecast

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0016272	Shiloh Road Resurfacing and Bridge Replacement	Lowndes	Apr 2025	Bridge	\$5,600,000
0016301	Omega-Eldorado Road Bridge Replacement over Little River	Tift	Apr 2025	Bridge	\$2,582,250
0016250	West Walker Street Sidewalk Improvements	Coffee / Douglas	May 2025	Sidewalks	\$433,900
0016235	Bud Hutcheson Road Paving	Coffee	Jun 2025	Grd Drn Bs Pv	\$2,798,000
422390-	SR 89/US441 from Orange St in Homerville to SR 122	Clinch	Jul 2025	Widening	\$26,625,000
0016280	Twin Lakes Road Paving and Drainage Improvements	Lowndes	Aug 2025	Grd Drn Bs Pv	\$2,100,000

Bud Hutcheson Rd, Coffee County

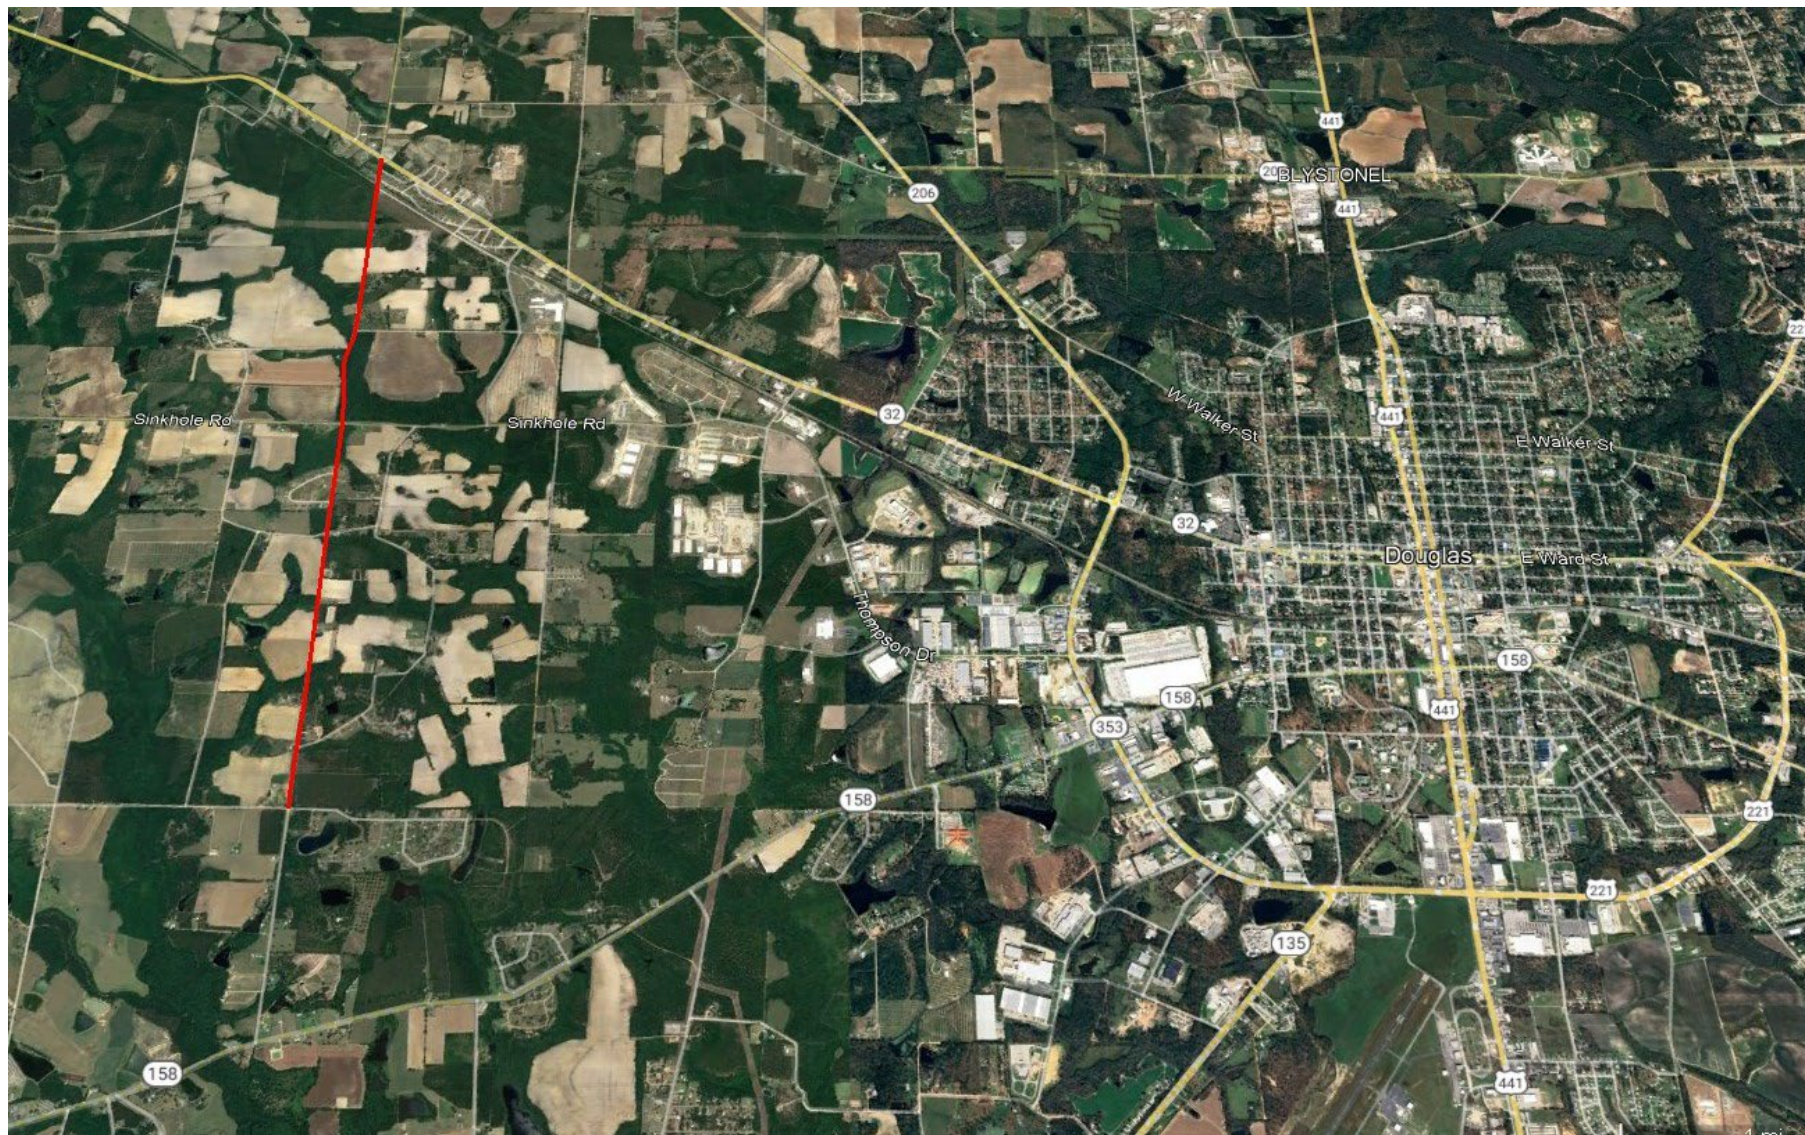

Projects under Construction

PI Number	Project Name	County	Project Type
0016248	Lupo Lane Sidewalk and Drainage Improvements	Coffee / Douglas	Sidewalks
0013605	US 84 Bridge over Satilla River & Overflow	Ware	Bridge
0016285	Old Clyattville Road Widening - Valdosta	Lowndes / Valdosta	Widening
0016251	Road Improvements at Douglas Municipal Airport	Coffee / Douglas	Grd Drn Bs Pv
0016286 & 0016288	St Augustine Road at Norman Drive & Gornto Rd	Lowndes / Valdosta	Intsct Imp
0016297	US 84 Intersection and Signal Improvements from County Farm Road to New School Road	Pierce	Intsct Imp
0016278	Kinderlou Clyattville Road Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv

I-75 at SR 31 (Exit 11), Lowndes County



Air Traffic Control Tower, Valdosta



Briggston Rd, Lowndes County



Golf Course Rd, Pierce County



SR 32 Passing Lanes, Bacon & Coffee County



Coleman Rd, Lowndes County




Band 2 Projects Remaining

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0016272	Shiloh Road Bridge Replacement	Lowndes	Apr 2025	Bridge	\$5,600,000
0016301	Omega-Eldorado Road Bridge Replacement over Little River	Tift	Apr 2025	Bridge	\$2,582,250
0016235	Bud Hutcheson Road Paving	Coffee	Jun 2025	Grd Drn Bs Pv	\$2,798,000
422390-	SR 89/US441 Widening	Clinch	Jul 2025	Widening	\$26,625,000
0016190	Fitzgerald Perimeter Roads Improvements (Widen, Resurface, C/G)	Ben Hill	Jul 2025	Minor Widen	\$5,165,192
0016298	Upper Ty Ty Road Bridge Replacement over Little River	Tift	Aug 2025	Bridge	\$2,710,000
0016254	Tillman Road Bypass Phase 3 Improvements	Cook	Dec 2025	Grd Drn Bs Pv	\$4,900,000
0016188	Peachtree Road Corridor Realigning, Widening, and Intersection Improvements	Ben Hill	Dec 2025	Realignment	\$5,913,200
0016186	Bethlehem Church Road Bridge at House Creek Bridge Replacement	Ben Hill	Dec 2025	Bridge	\$1,500,000
0016187	Bethlehem Church Road Bridge at Otter Creek Bridge Replacement	Ben Hill	Dec 2025	Bridge	\$1,000,000
0016311	Reid Road Paving	Turner	Dec 2025	Grd Drn Bs Pv	\$2,400,000
0016309	Hobby Road Paving	Turner	Apr 2026	Grd Drn Bs Pv	\$1,400,000
0016310	Glynn Cook Road Paving	Turner	Apr 2026	Grd Drn Bs Pv	\$620,000
0016306	12th Street at Prince Avenue Intersection Improvements	Tift	Jun 2026	Intsct Imp	\$2,285,500
0000821	SR 40 from SR40 Conn to 0.36 mi east of May Bluff Rd	Charlton	Dec 2027	Widening	\$8,635,000


Band 3 Projects Advanced

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0015536	SR520/US82 @Satilla River Overflow	Brantley	Jul 2022	Bridge	\$5,900,000
0016249	Baker Hwy, East (SR 158) Sidewalk Improvements	Coffee	May 2023	Sidewalks	\$694,600
0016248	Lupo Lane Sidewalk and Drainage Improvements	Coffee	Jan 2024	Sidewalks	\$674,400
0016251	Road Improvements at Douglas Municipal Airport	Coffee	Apr 2024	Grd Drn Bs Pv	\$150,000
0016286	St Augustine Road at Norman Drive Intersection, Drainage and Signal Improvements	Lowndes	May 2024	Intsct Imp	\$3,988,700
0016307	18th Street Ditch Bridge Replacements (5 Culverts)	Tift	Feb 2025	Bridge	\$1,869,400
0016250	West Walker Street Sidewalk Improvements	Coffee	May 2025	Sidewalks	\$433,900
0016280	Twin Lakes Road Paving and Drainage Improvements	Lowndes	Aug 2025	Grd Drn Bs Pv	\$2,100,000
0016215	Homerville Bypass Resurfacing, Bridge Replacement and Other Improvements	Clinch	Oct 2025	Bridge	\$3,000,000

Projects with Local Let Agreements

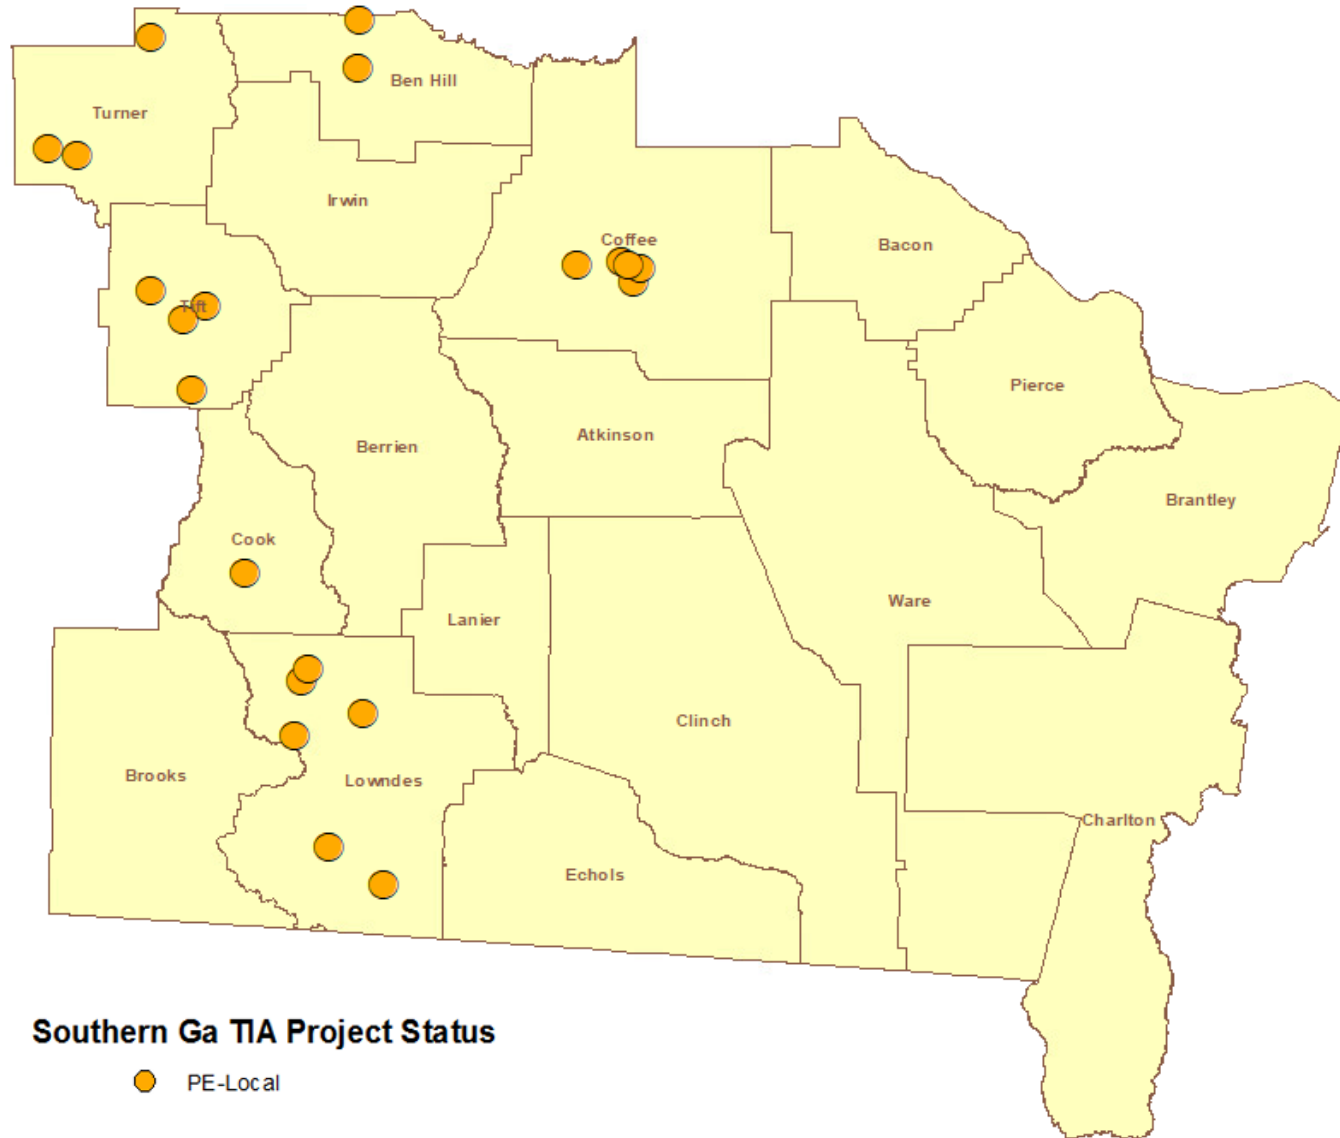


Projects Under Construction

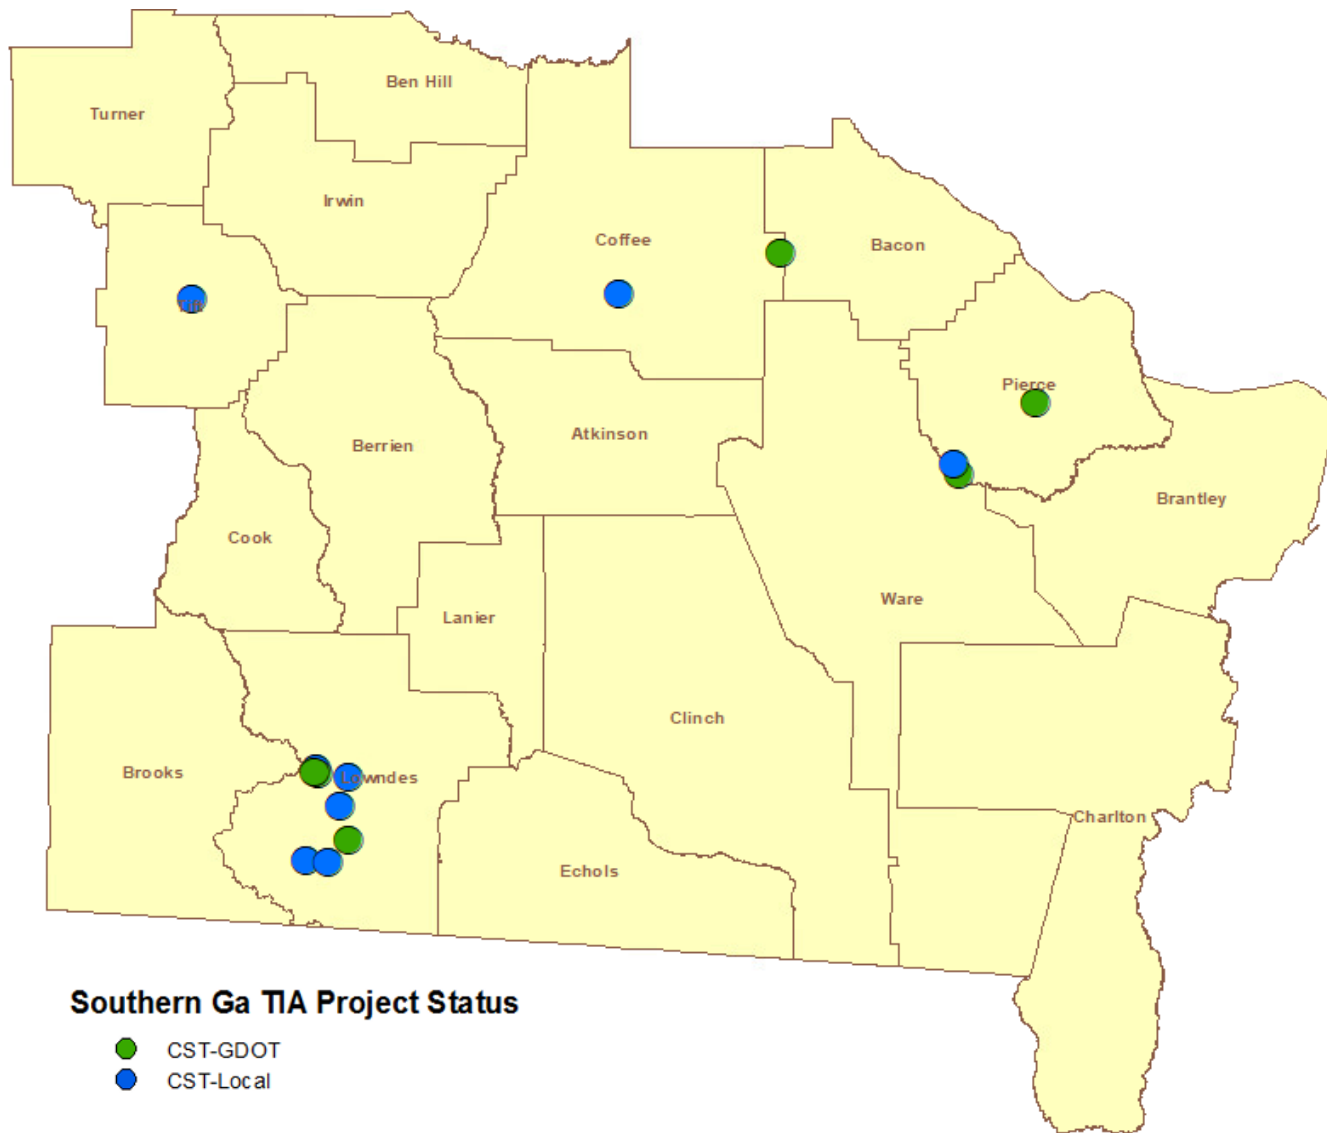

Southern Ga TIA Project Status

- CST-GDOT
- CST-Local

Completed Projects

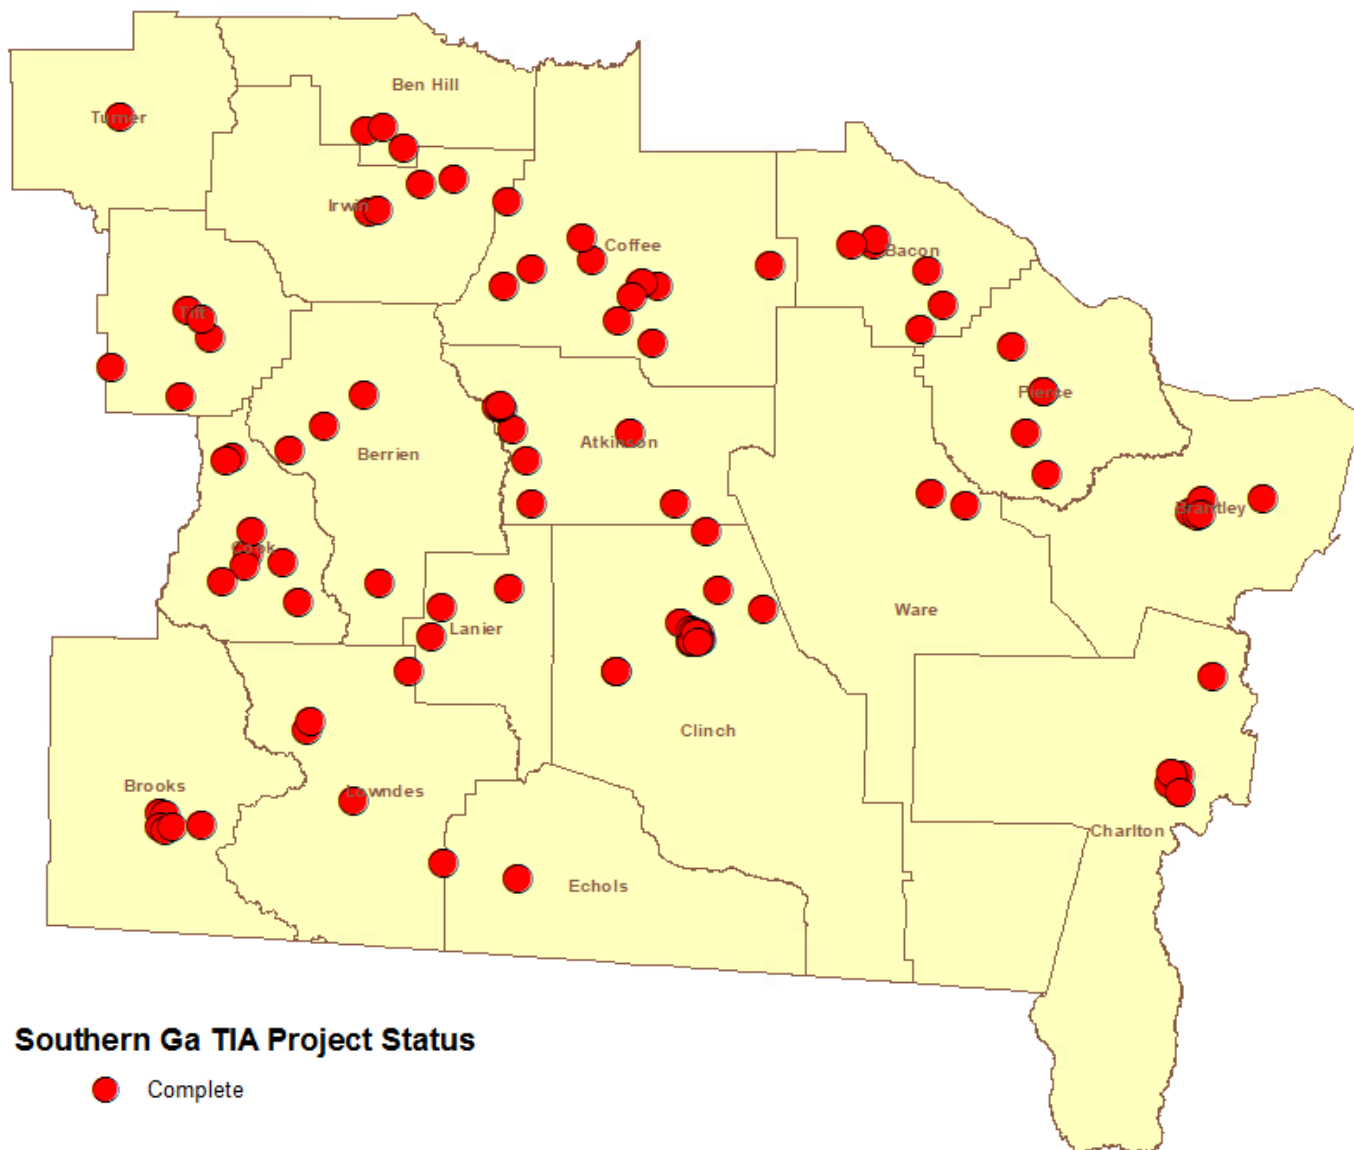

Questions?

SOUTHERN GEORGIA



**TRANSPORTATION
INVESTMENT ACT**

Your Penny, Your Progress
