




Transportation Investment Act

Southern Georgia

July 26, 2022 CRP Update



TIA Regions

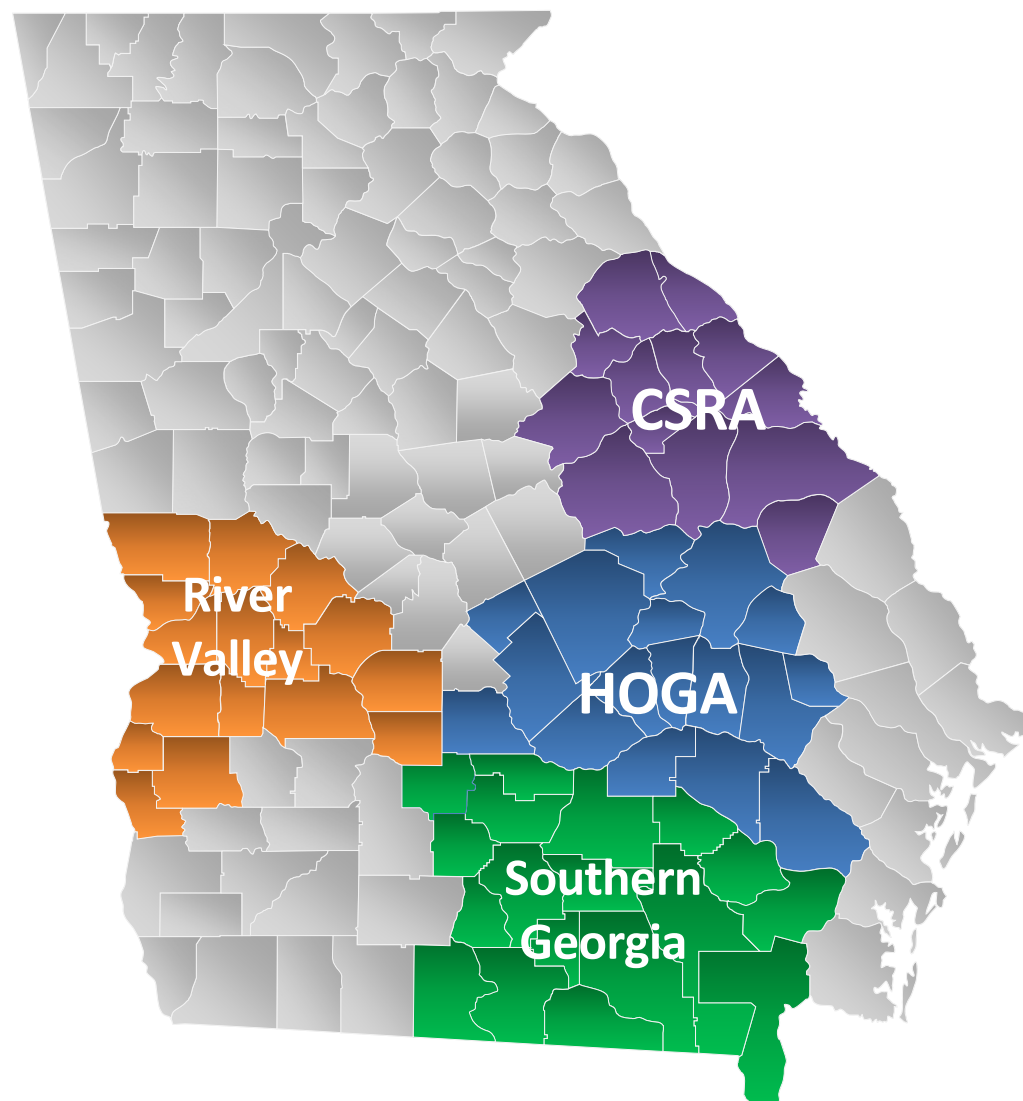


TIA Collections thru May 2022

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
CSRA	\$689,543,512*	\$517,157,634*	\$172,385,878*
River Valley	\$472,724,320*	\$354,543,240*	\$118,181,080*
Heart of Georgia	\$308,085,817*	\$231,064,363*	\$77,021,454*
Southern Georgia	\$225,502,782*	\$169,127,086*	\$56,375,696*
Totals (*rounded amounts)	\$1,695,856,431	\$1,271,892,323	\$423,964,108

TIA Collections thru May 2022


Region	Original Revenue Forecast	Actual Revenue Collected	% Behind Forecast
CSRA	\$787,604,858*	\$689,543,512*	-12.5%
River Valley	\$556,457,825*	\$472,724,320*	-15.0%
Heart of Georgia	\$373,438,210*	\$308,085,817*	-17.5%
Southern Georgia	\$180,953,632*	\$225,502,782*	24.6%
Totals (*rounded amounts)	\$1,898,454,525	\$1,695,856,431	-10.7%

Southern Georgia Timeline

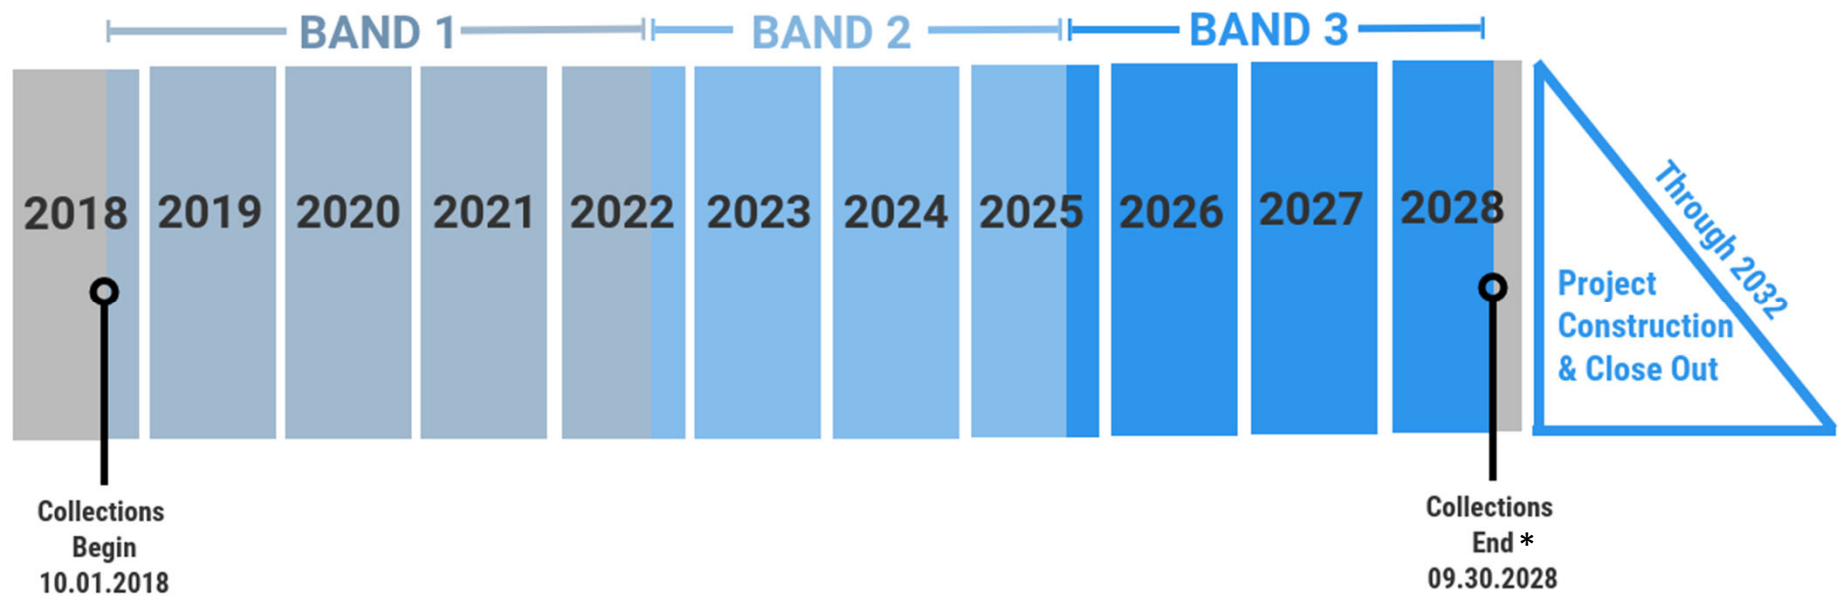

* Should revenue meet the projected max prior to the legislated end date, collections will end early.

Southern GA Project Overview

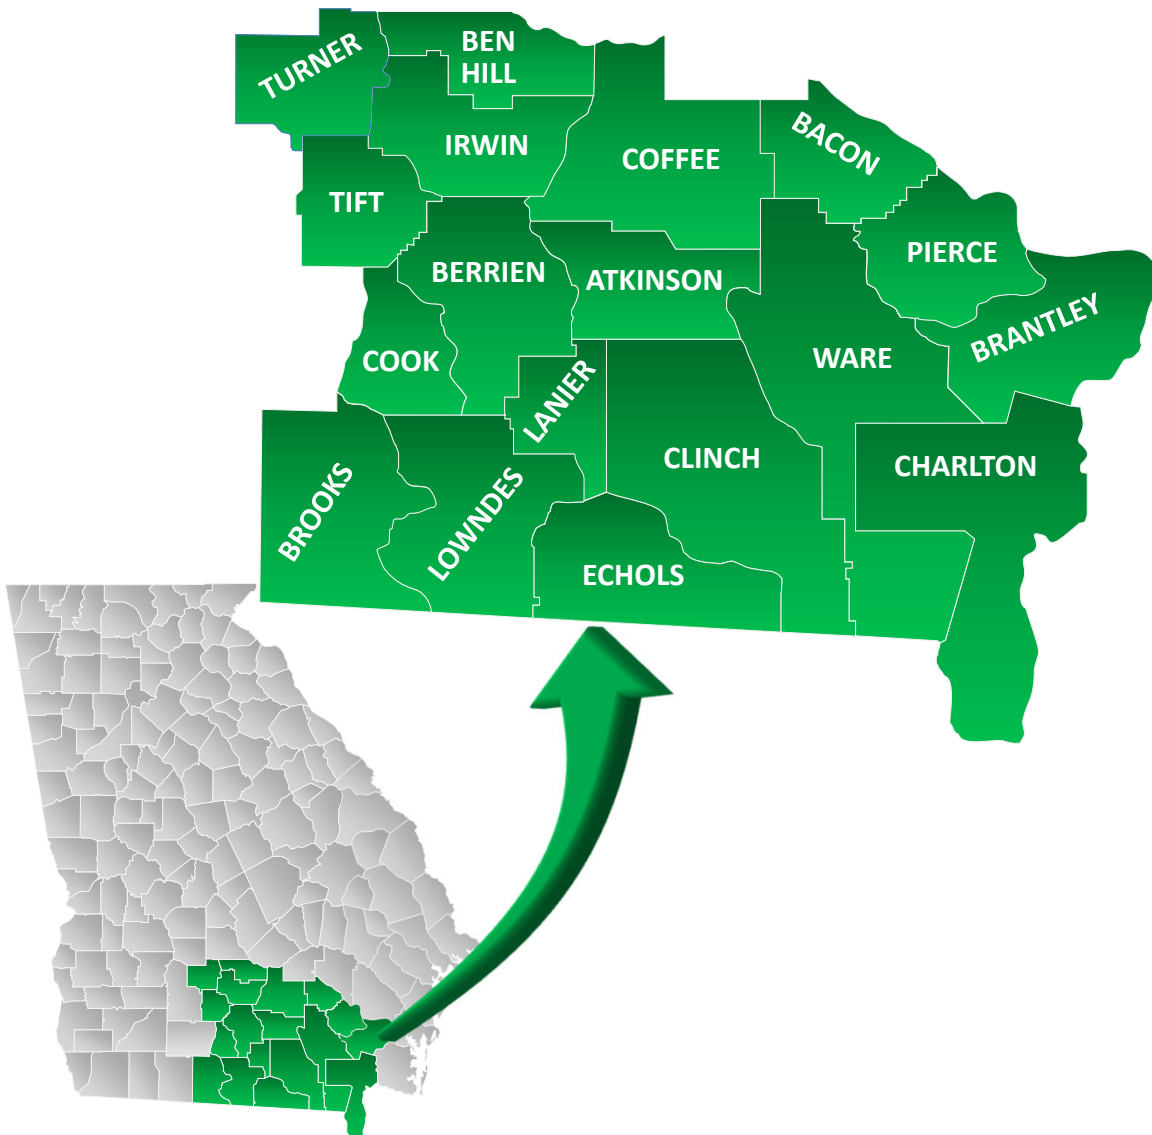

151

Total Projects

\$408,763,452

Final Investment List
Project Total

17

In Construction

69

Projects Completed

\$77,956,522

Total Expenditure to Date
(as of 7/21/22)

Projects Let since March

PI #	Project Name	County	Let Date	Project Type	Original Budget	Low Bid
0016308	City of Ashburn Resurfacing Bundle and Sidewalk Improvements	Turner / Ashburn	April 2022	Resurfacing / Sidewalk	\$1,000,000	\$248,890
0016241	Hwy 149/Youngie Fussell Road/Bridgetown Road Widen and Resurface	Coffee	May 2022	Minor Widen	\$3,850,000	\$4,572,884
0016257	Valdel Road Resurfacing	Cook	May 2022	Resurfacing	\$2,007,500	\$2,448,522
0016293	Pierce County Horseshoe Road/Fletcher Road Area Resurfacing Bundle	Pierce	May 2022	Resurfacing	\$1,681,890	\$1,731,990

Total Budget = \$8,539,390
4 Total Projects

Horseshoe Rd / Fletcher Rd Pierce County



TIA Letting Forecast

PI #	Project Name	County	Let Date	Project Type	TIA Budget
0015536	SR520/US82 @ Satilla River Overflow	Brantley	Jul 2022	Bridge	\$200,000
0016253	Alabama Road Truck Route Improvements	Cook / Adel	Aug 2022	Grd Drn Bs Pv	\$3,312,000
0016296	Golf Course Road Alignment, Drainage and Resurfacing	Pierce	Aug 2022	Resurfacing	\$3,408,000
0016258 +	Taylor Street, E Revels Street Paving	Cook / Lenox	Aug 2022	Grd Drn Bs Pv	\$726,900
0016302	8th Street Widening for Turn Lane	Tift / Tifton	Aug 2022	Turn Lanes	\$941,600
0016202 +	City of Quitman Sidewalks and Drainage Improvements (5 projects)	Brooks / Quitman	Sep 2022	Sidewalks	\$4,922,600
0016171	Cogdell Road Widen and Resurface	Atkinson	Oct 2022	Minor Widen	\$2,359,000
0016299 +	Scooterville & Omega-Eldorado Road Bridge Replacements (2 projects)	Tift	Nov 2022	Bridge	\$3,321,000
0016285	Old Clyattville Road Widening - Valdosta	Lowndes / Valdosta	Nov 2022	Widening	\$6,217,514
0016287	S Patterson Street at Griffin Avenue Intersection and Drainage Improvements	Lowndes / Valdosta	Nov 2022	Intsct Imp	\$1,258,000
0016290	Baytree Road at Gornto Road Intersection and Signal Improvements	Lowndes / Valdosta	Nov 2022	Intsct Imp	\$2,734,000

17 Projects

Total TIA Budget = \$29,400,614

Alabama Rd, City of Adel



Projects under Construction

PI #	Project Name	County	Project Type	Original Total Budget
0016265	Cherry Street Resurfacing and Drainage Improvements	Irwin / Ocilla	Resurfacing	\$500,000
0016214	Oak Lane Resurfacing	Clinch / Argyle	Grd Drn Bs Pv	\$300,000
0016312	Albany Avenue Widen and Resurfacing	Ware / Waycross	Resurfacing	\$1,600,000
0016271	Old 41 N. Widening	Lowndes	Widening	\$6,516,800
0016305	Taxiway Improvements at Henry Tift Myers Airport	Tift	Airport	\$5,600,000
0016262	John Hampton Road Paving	Echols	Grd Drn Bs Pv	\$400,000
0016276	Hightower Road/Cooper Road NE Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv	\$3,750,000
0016266	Fifth Street Ext. Paving	Irwin / Ocilla	Grd Drn Bs Pv	\$500,000
0010297	I-75 @ SR 31 - Phase II (Exit 11)	Lowndes	Interchange	\$21,445,000

Albany Ave, City of Waycross



Old 41 North, Lowndes County



Old 41 North, Lowndes County



Taxiway Improvements Henry Tift Myers Airport



John Hampton Rd, Echols County




Fifth Street Ext, City of Ocilla



I-75 at Exit 11, Lowndes County




Projects with Local Let Agreements

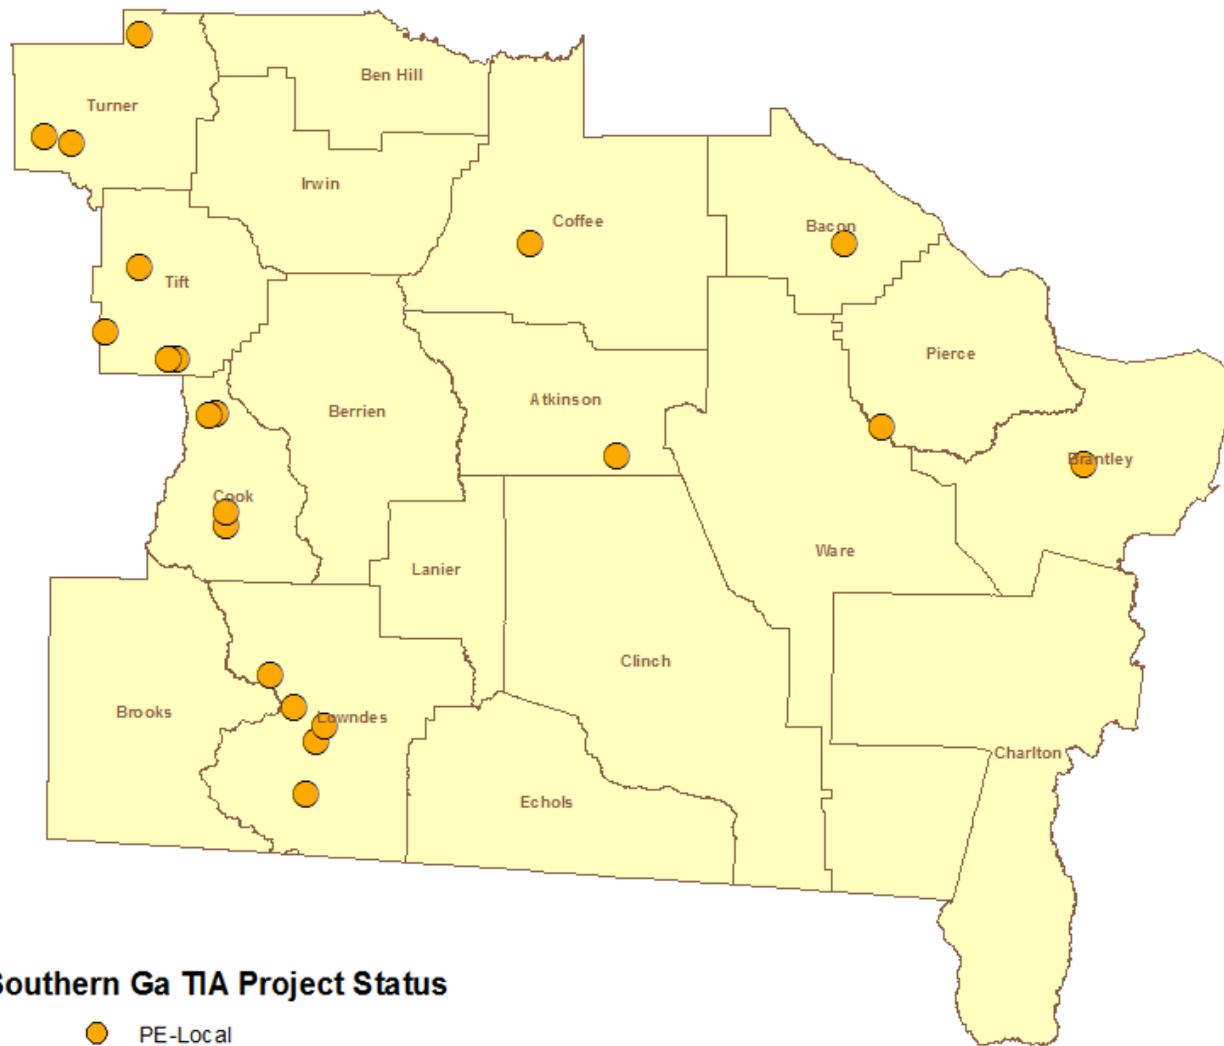

Southern Ga TIA Project Status

● PE-Local


Projects under Construction

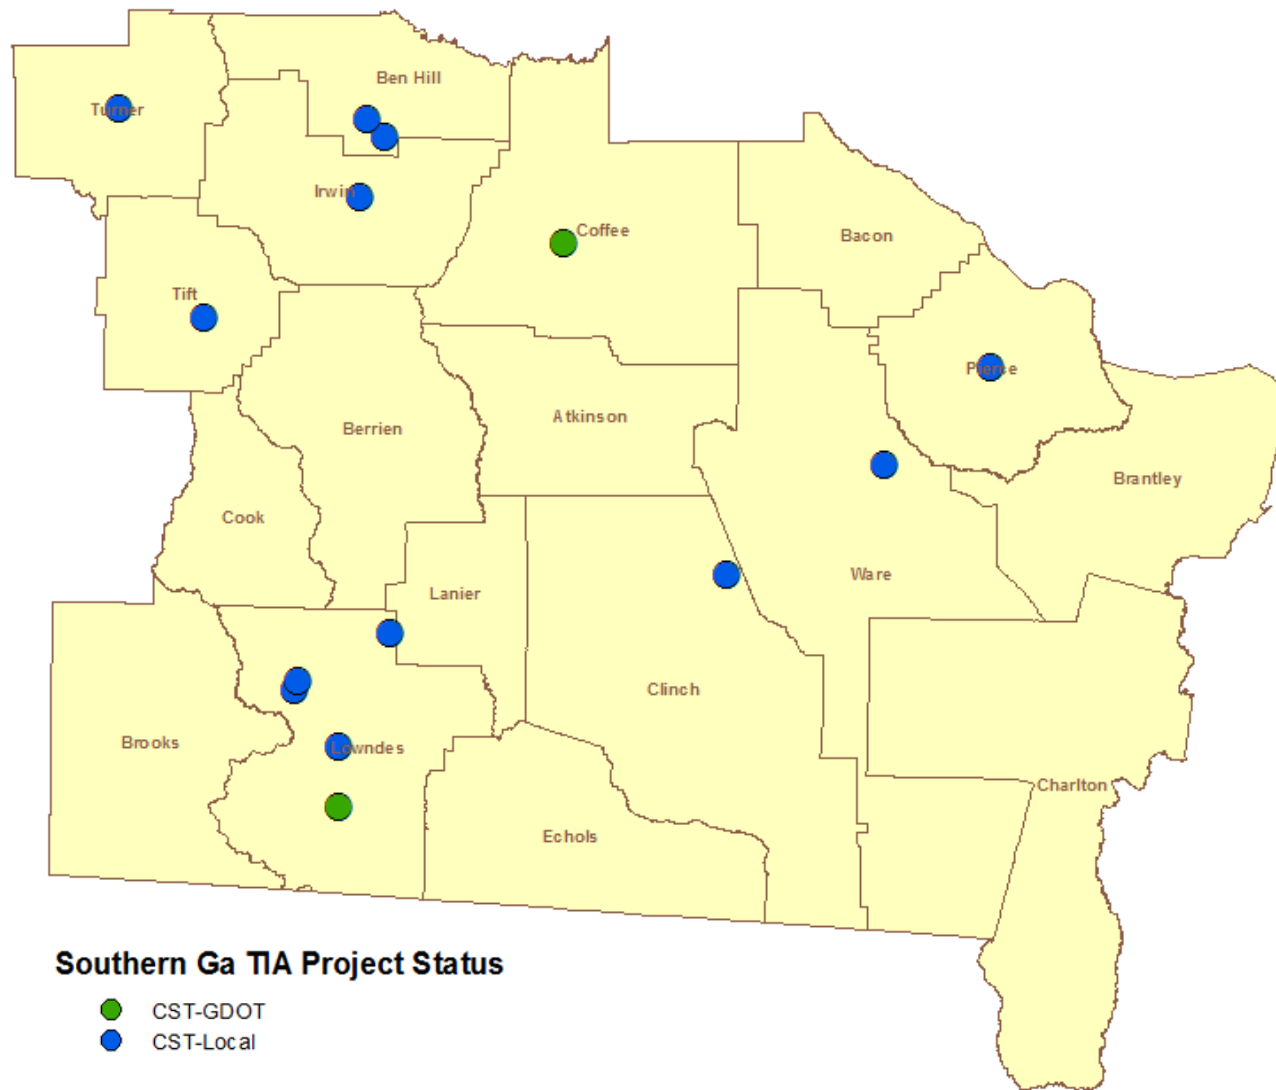

Southern Ga TIA Project Status

- CST-GDOT
- CST-Local

Completed Projects

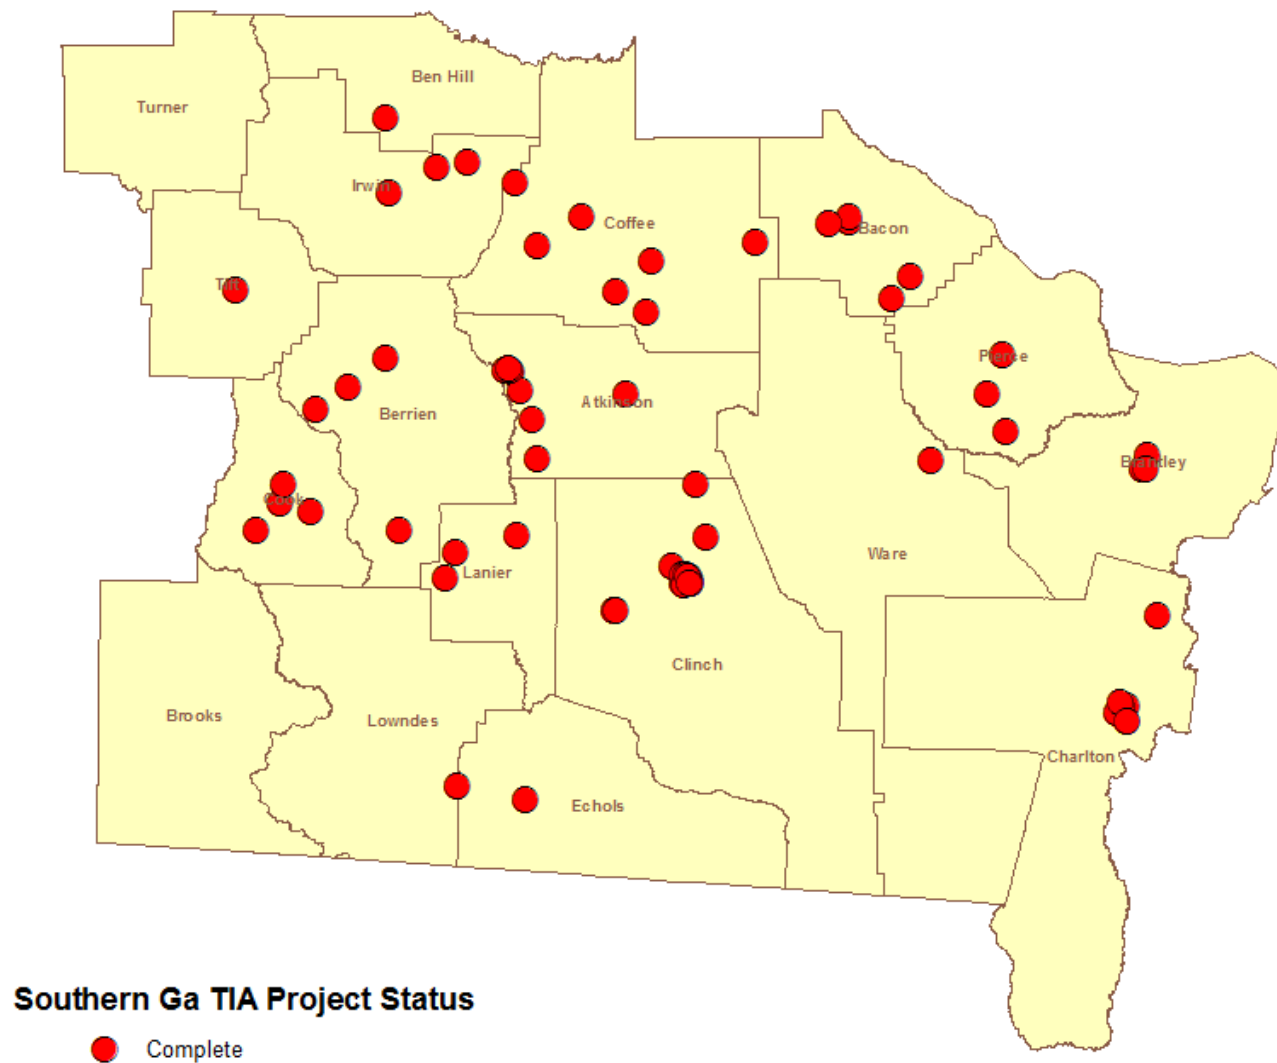

Questions?

SOUTHERN GEORGIA



**TRANSPORTATION
INVESTMENT ACT**

Your Penny, Your Progress
