



Georgia Department of Transportation


Transportation Investment Act

Southern Georgia

August 27, 2025 CRP Update



TIA Regions

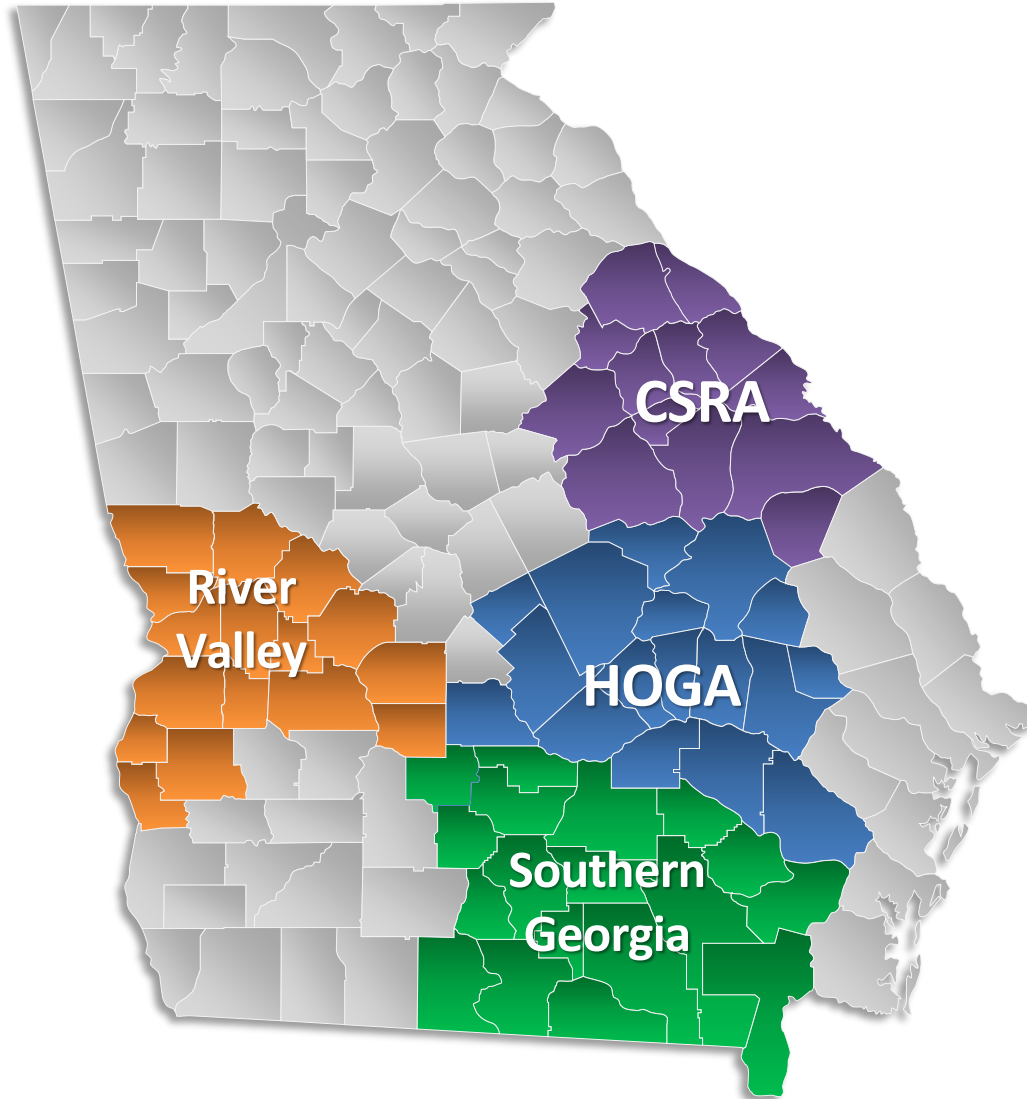


TIA Collections thru June 2025

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
CSRA 2	\$273,085,389*	\$204,814,042*	\$68,271,347*
River Valley 2	\$174,192,486*	\$130,644,365*	\$43,548,121*
Heart of Georgia 2	\$125,442,780*	\$94,082,085*	\$31,360,695*
Southern Georgia	\$468,160,860*	\$351,120,645*	\$117,040,215*
Totals (*rounded amounts)	\$1,040,881,515	\$780,661,137	\$260,220,378

TIA Collections thru June 2025


Region	Original Revenue Forecast	Actual Revenue Collected	% Ahead of Forecast
CSRA 2	\$211,745,584*	\$273,085,389*	29.0%
River Valley 2	\$149,331,689*	\$174,192,486*	16.6%
Heart of Georgia 2	\$89,898,074*	\$125,442,780*	39.5%
Southern Georgia	\$340,561,841*	\$468,160,860*	37.5%
Totals (*rounded amounts)	\$791,537,188	\$1,040,881,515	31.5%

Southern Georgia Timeline

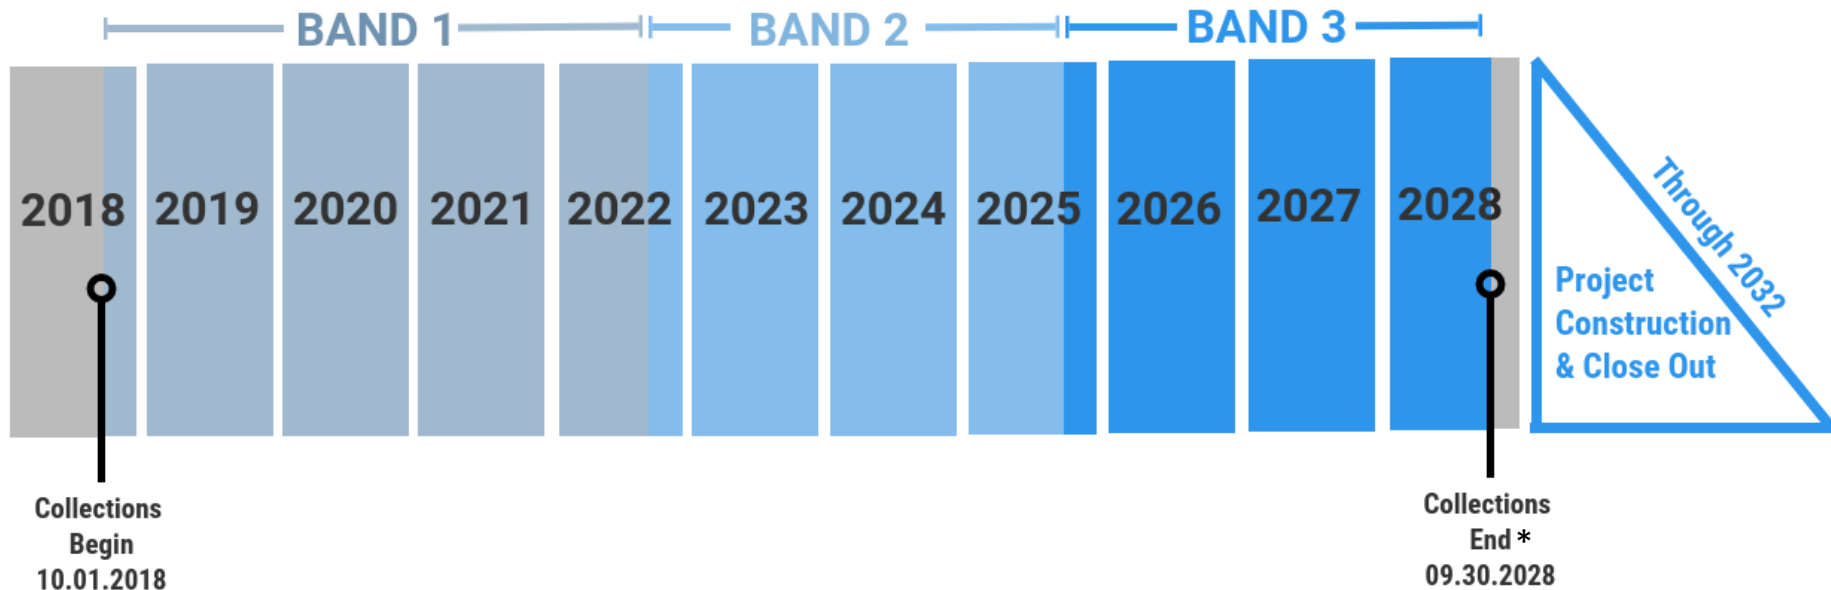

* Should revenue meet the projected max prior to the legislated end date, collections will end early.

Southern GA Project Overview

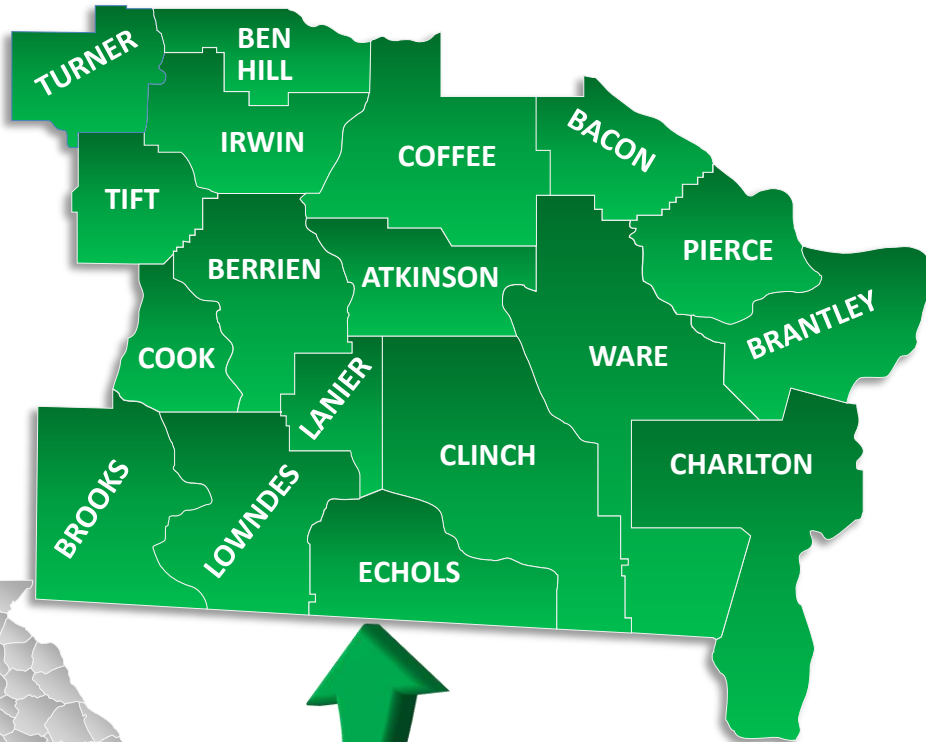

151

Total Projects

\$408,763,452

Final Investment List
Project Total

17

In Construction

108

Projects Completed

\$184,553,225

Total TIA Expenditure to Date
(as of 8/18/25)

Projects Let since March

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget	Low Bid
0016250	West Walker Street Sidewalk Improvements	Coffee / Douglas	May 2025	Sidewalks	\$433,900	\$725,195.12
0016235	Bud Hutcheson Road Paving	Coffee	Jun 2025	Grd Drn Bs Pv	\$2,798,000	\$4,242,398.63
422390-	SR 89/US441 Widening	Clinch	Jul 2025	Widening	\$26,625,000	\$45,589,665.20
0016272	Shiloh Road Resurfacing and Bridge Replacement	Lowndes	Jul 2025	Bridge	\$5,600,000	\$6,400,444.98

TIA Letting Forecast

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0016301	Omega-Eldorado Road Bridge Replacement over Little River	Tift	Aug 2025	Bridge	\$2,582,250
0016246	Chester Avenue Sidewalk and Drainage (Culvert) Improvements	Coffee / Douglas	Oct 2025	Sidewalk / Resurfacing	\$2,846,200
0016280	Twin Lakes Road Paving and Drainage Improvements	Lowndes	Oct 2025	Grd Drn Bs Pv	\$2,100,000
0016215	Homerville Bypass Resurfacing, Bridge Replacement and Other Improvements	Clinch	Oct 2025	Bridge	\$3,000,000
0016244	McDonald Road Sidewalk and Drainage Improvements	Coffee / Douglas	Nov 2025	Sidewalk / Resurfacing	\$1,341,800
0016247	West Green Hwy (SR 135/US 221) Sidewalk Improvements	Coffee / Douglas	Nov 2025	Sidewalks	\$560,200
0016311	Reid Road Paving	Turner	Dec 2025	Grd Drn Bs Pv	\$2,400,000

Homerville Bypass, Clinch County



Projects under Construction

PI Number	Project Name	County	Project Type
0016284	New Air Traffic Control Tower at Valdosta Regional Airport	Lowndes / Valdosta	Airport
0016182	SR 32 Passing Lanes Between Alma to Douglas	Bacon	Passing Lanes
0013605	US 84 Bridge over Satilla River	Ware	Bridge
0016285	Old Clyattville Road Widening - Valdosta	Lowndes / Valdosta	Widening
0016297	US 84 Intersection and Signal Improvements from County Farm Road to New School Road.	Pierce	Intsct Imp
0016278	Kinderlou Clyattville Road Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv
0016279	Coleman Road NW Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv

County Farm Rd, Pierce County



Kinderlou Clyattville Rd, Lowndes County



SR 32 Passing Lanes, Bacon & Coffee County




Band 2 Projects Needing a Band Change

PI Number	Project Name	County	Current Band	Let Date	Original Total Budget
0016311	Reid Road Paving	Turner	2	Dec 2025	\$2,400,000
0016309	Hobby Road Paving	Turner	2	Apr 2026	\$1,400,000
0016310	Glynn Cook Road Paving	Turner	2	Apr 2026	\$620,000
0016254	Tillman Road Bypass Phase 3 Improvements	Cook / Adel	2	Jun 2026	\$4,900,000
0016186	Bethlehem Church Road Bridge at House Creek Bridge Replacement	Ben Hill	2	Jun 2026	\$1,500,000
0016187	Bethlehem Church Road Bridge at Otter Creek Bridge Replacement	Ben Hill	2	Jun 2026	\$1,000,000
0016188	Peachtree Road Corridor Realigning, Widening, and Intersection Improvements	Ben Hill	2	Jun 2026	\$5,913,200
0016306	12th Street at Prince Avenue Intersection Improvements	Tift / Tifton	2	Jun 2026	\$2,285,500
0016298	Upper Ty Ty Road Bridge Replacement over Little River	Tift	2	Jun 2026	\$2,710,000
0016190	Fitzgerald Perimeter Roads Improvements (Widen, Resurface, C/G)	Ben Hill / Fitzgerald	2	Dec 2026	\$5,165,192
0000821	SR 40 from SR40 Conn to 0.36 mi east of May Bluff Rd	Charlton	2	Oct 2027	\$8,635,000


Band 3 Projects Advanced

PI Number	Project Name	County	Current Band	Let Date	Project Stage
0015536	SR520/US82 @Satilla River Overflow 14 mi east of Hoboken	Brantley	3	Jul 2022	Complete
0016249	Baker Hwy, East (SR 158) Sidewalk Improvements	Coffee / Douglas	3	May 2023	Complete
0016248	Lupo Lane Sidewalk and Drainage Improvements	Coffee / Douglas	3	Nov 2024	Complete
0016251	Road Improvements at Douglas Municipal Airport	Coffee / Douglas	3	Apr 2024	Construction
0016286	St Augustine Road at Norman Drive Intersection, Drainage and Signal Improvements	Lowndes / Valdosta	3	May 2024	Construction
0016307	18th Street Ditch Bridge Replacements (5 Culverts)	Tift / Tifton	3	Feb 2025	Construction


Projects with Local Let Agreements

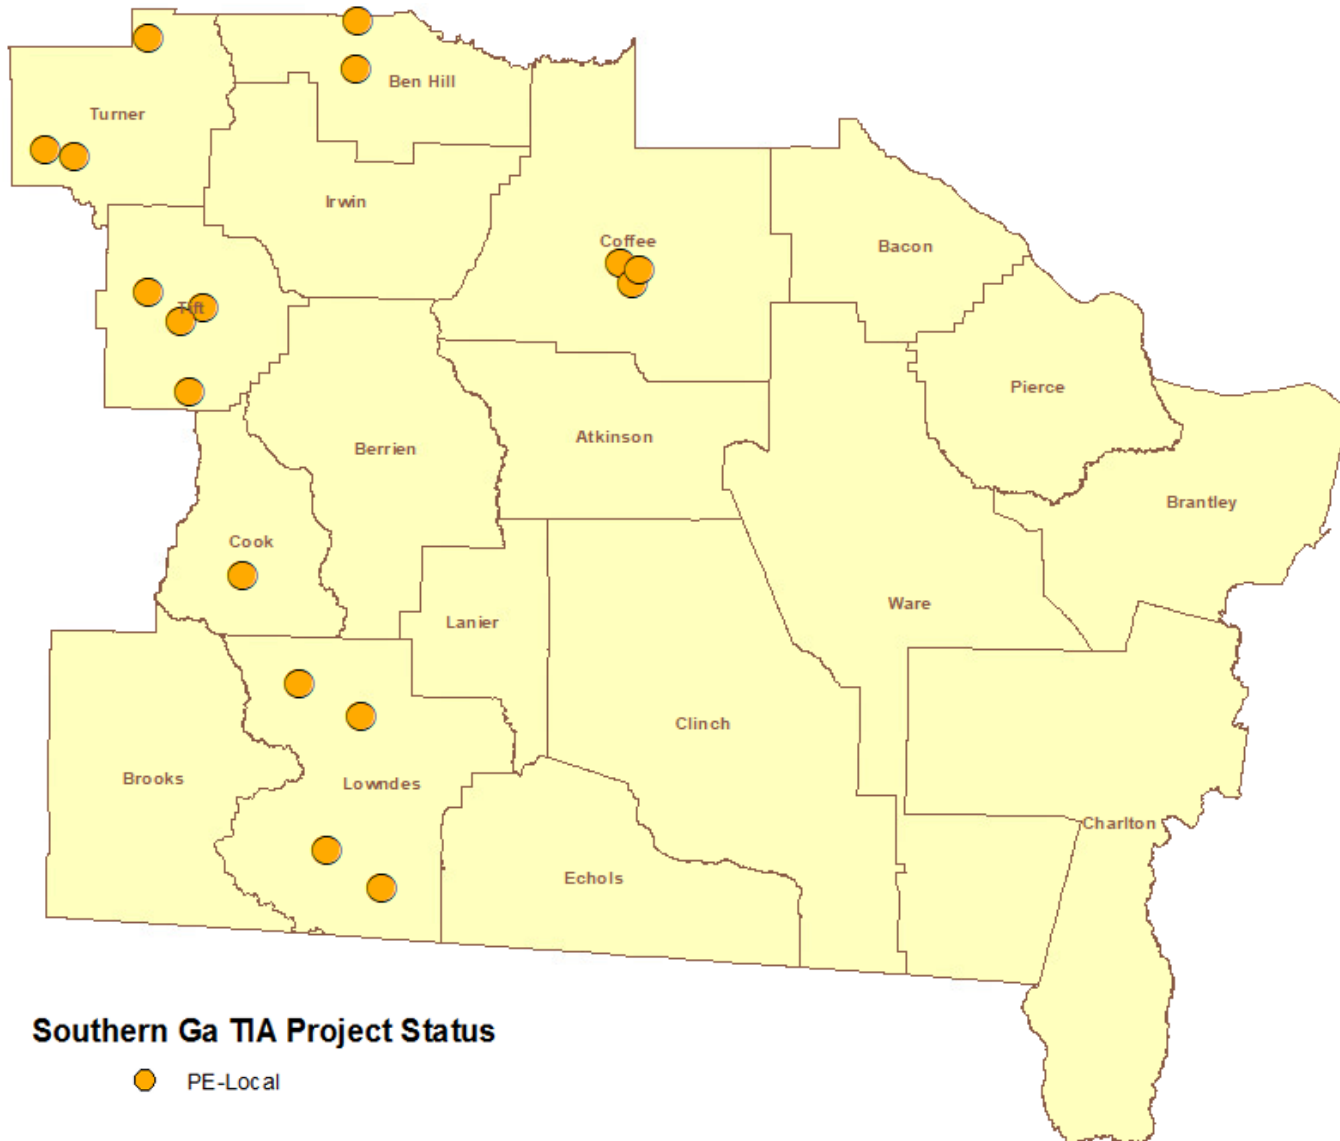

Projects Under Construction

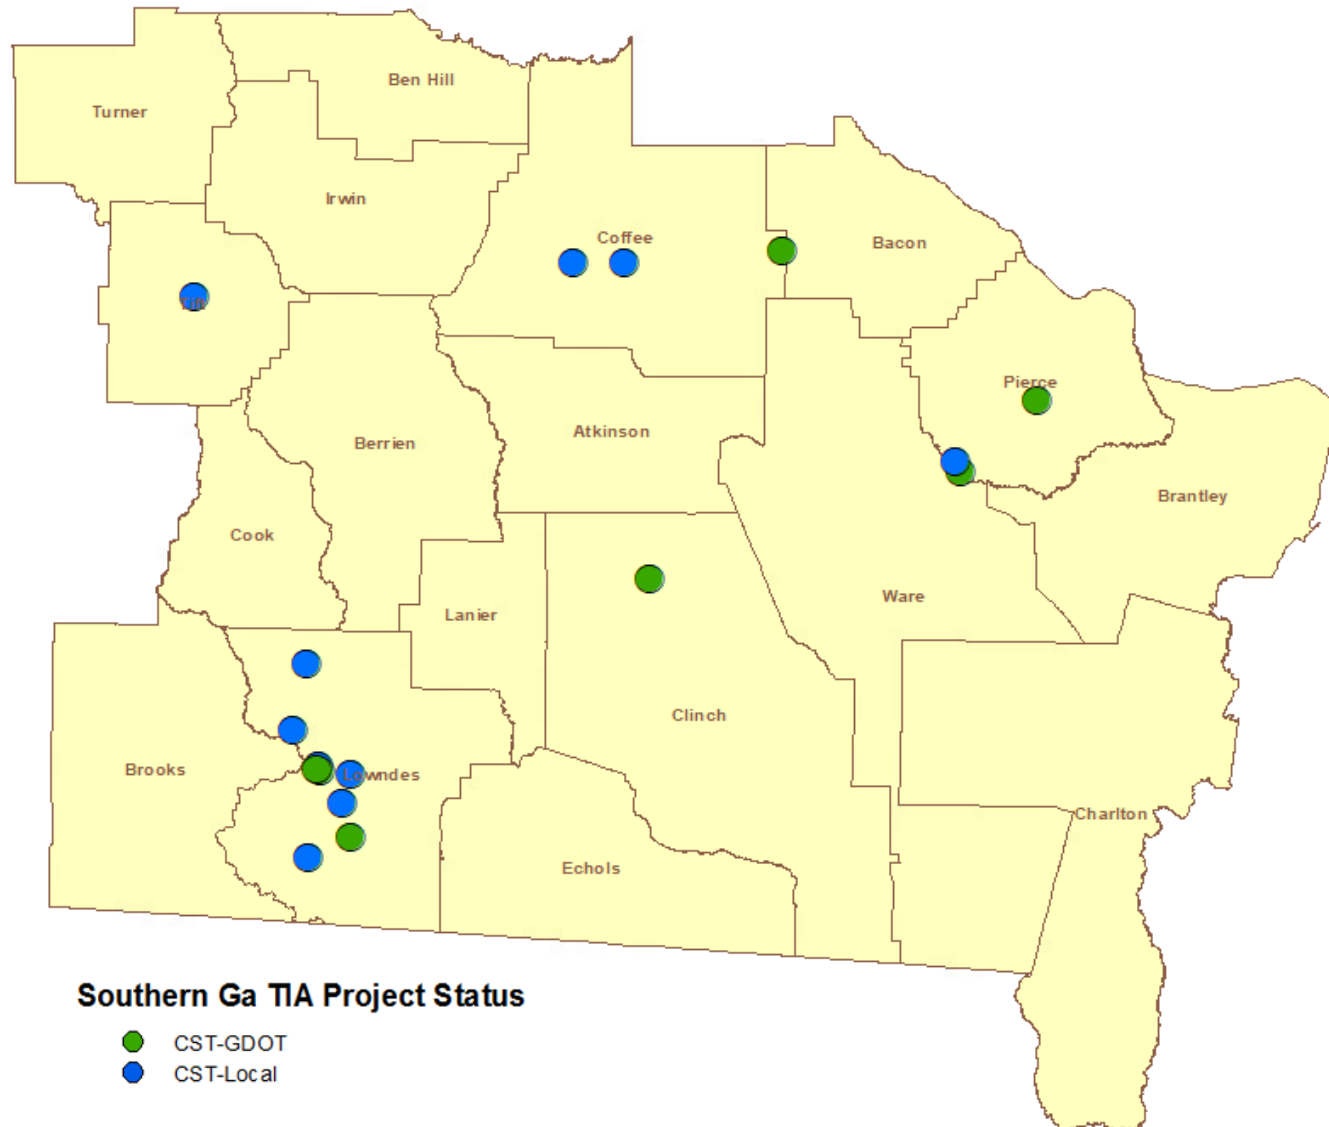

Completed Projects

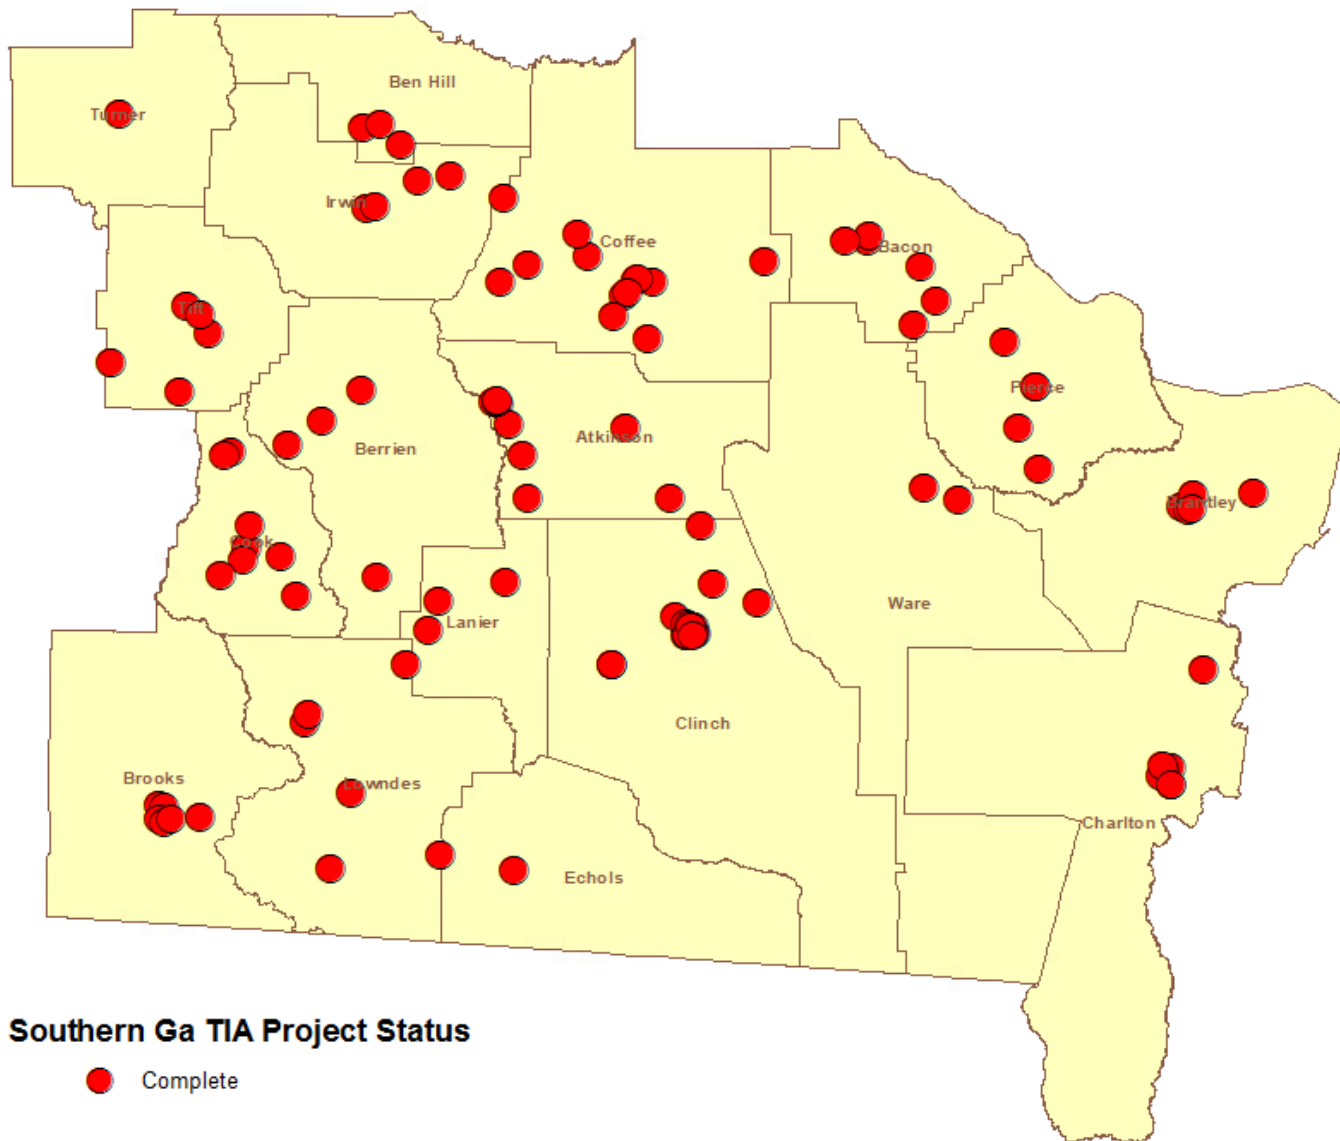

Questions?

SOUTHERN GEORGIA



**TRANSPORTATION
INVESTMENT ACT**

Your Penny, Your Progress
