




# Transportation Investment Act

Southern Georgia

November 8, 2023 CRP Update



# TIA Regions

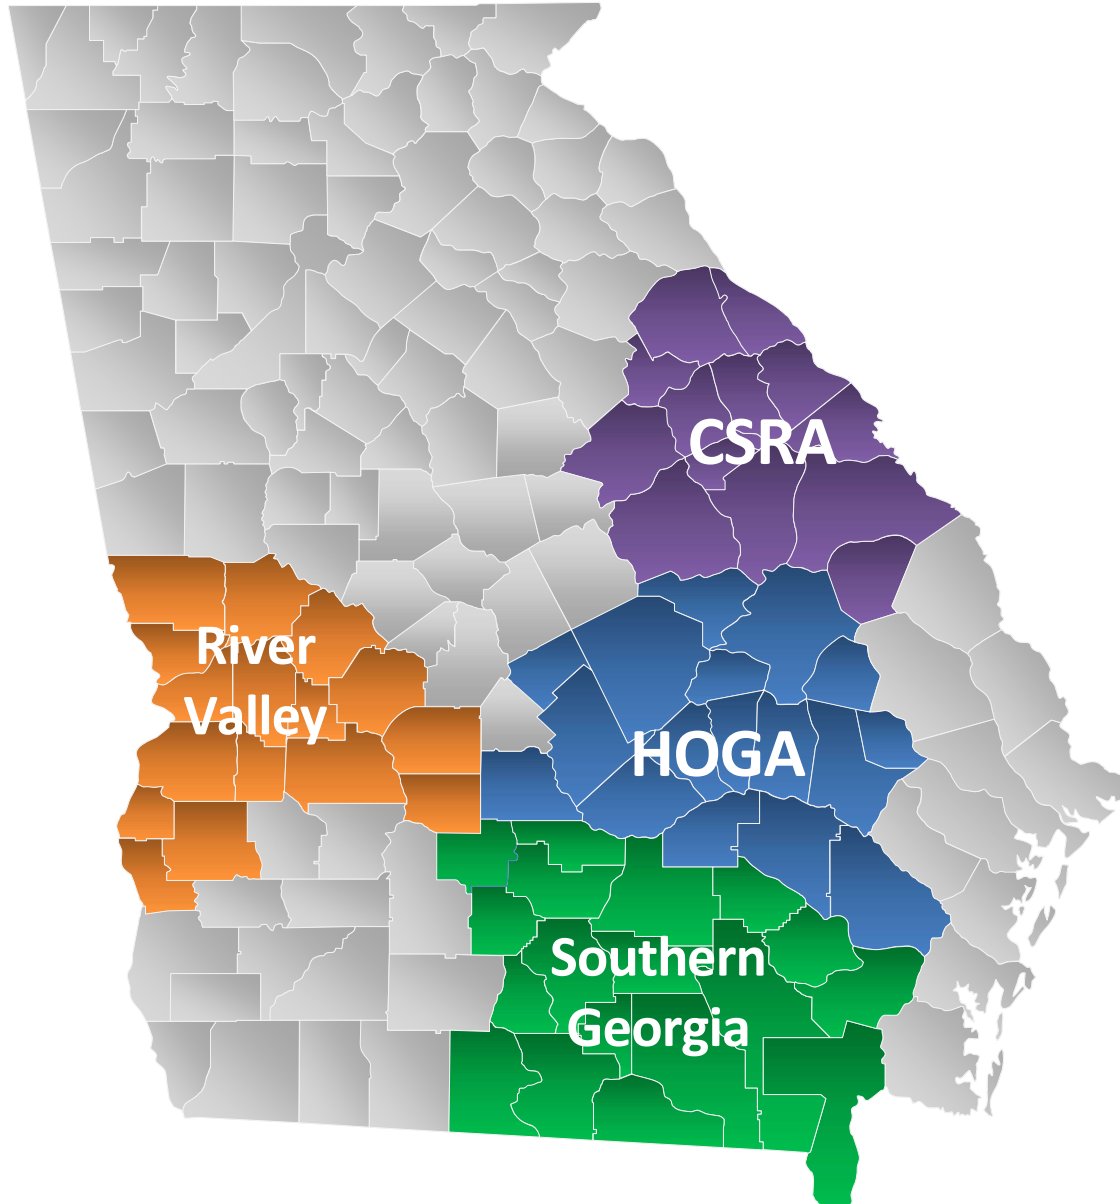


## TIA Collections thru September 2023

Region	Total	Approved Investment List (75%)	Local Discretionary (25%)
CSRA	\$79,181,791*	\$59,386,343*	\$19,795,448*
River Valley	\$51,055,475*	\$38,291,606*	\$12,763,869*
Heart of Georgia	\$34,354,616*	\$25,765,962*	\$8,588,654*
<b>Southern Georgia</b>	<b>\$325,451,119*</b>	<b>\$244,088,339*</b>	<b>\$81,362,780*</b>
Totals (*rounded amounts)	\$490,043,001	\$367,532,250	\$122,510,751

## TIA Collections thru September 2023


Region	Original Revenue Forecast	Actual Revenue Collected	% Behind Forecast
CSRA	\$62,645,179*	\$79,181,791*	26.4%
River Valley	\$43,154,211*	\$51,055,475*	18.3%
Heart of Georgia	\$25,334,247*	\$34,354,616*	35.6%
<b>Southern Georgia</b>	<b>\$249,541,613*</b>	<b>\$325,451,119*</b>	<b>30.4%</b>
Totals (*rounded amounts)	\$380,675,250	\$490,043,001	28.7%

# Southern Georgia Timeline

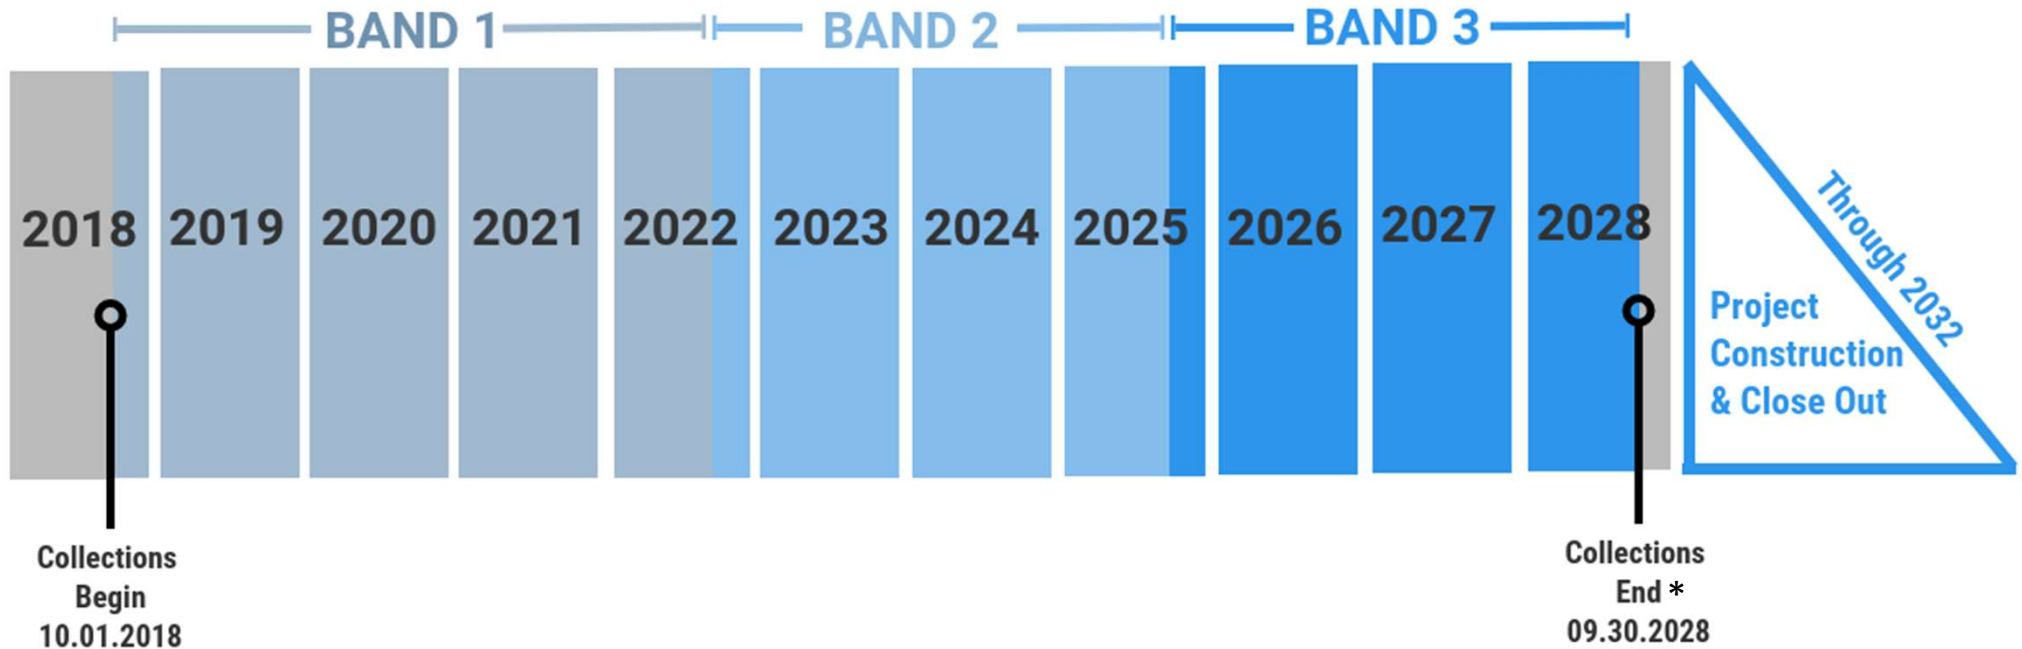

\* Should revenue meet the projected max prior to the legislated end date, collections will end early.

## Southern GA Project Overview

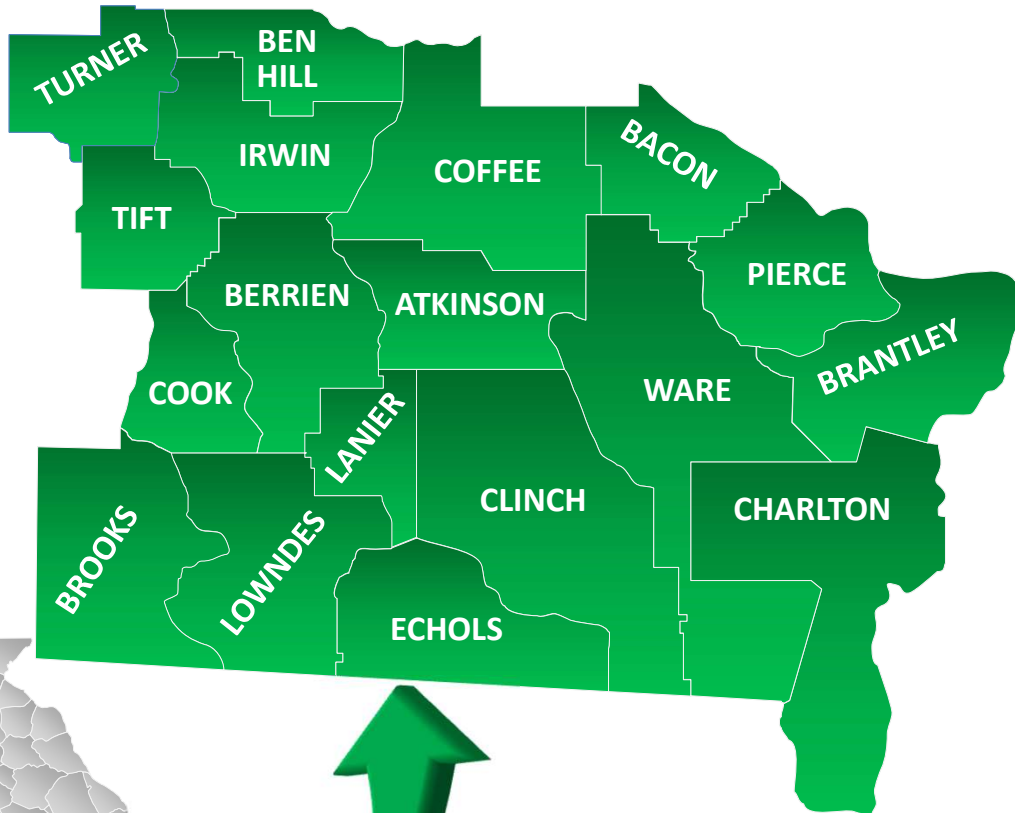

**151**

Total Projects

**\$408,763,452**

Final Investment List  
Project Total

**24**

In Construction

**86**

Projects Completed

**\$132,555,799**

Total Expenditure to Date  
(as of 10/31/23)

## Projects Let since July

PI Number	Project Name	County	Let Date	Project Type	Original Budget	Bid Amount
0016275	Briggston Road Paving and Drainage Improvements	Lowndes	Sept 2023	Grd Drn Bs Pv	\$2,525,000	\$2,611,309

# TIA Letting Forecast

PI Number	Project Name	County	Let Date	Project Type	Original Total Budget
0016182	SR 32 Passing Lanes Between Alma to Douglas	Bacon / Coffee	Nov 2023	Passing Lanes	\$4,536,000
0016285	Old Clyattville Road Widening - Valdosta	Lowndes / Valdosta	Dec 2023	Widening	\$6,217,514
0016248	Lupo Lane Sidewalk and Drainage Improvements	Coffee / Douglas	Dec 2023	Sidewalks	\$674,400
0013605	US 84 Bridge over Satilla River	Ware	Feb 2024	Bridge	\$8,650,000
0016272	Shiloh Road Resurfacing and Bridge Replacement	Lowndes	Apr 2024	Bridge	\$5,600,000
0016297	US 84 Intersection and Signal Improvements from County Farm Road to New School Road	Pierce	Apr 2024	Intsct Imp	\$8,500,000

**6 Projects**  
**Total TIA Budget = \$34,177,914**



# Old Clyattville Rd, City of Valdosta



# Projects under Construction

PI Number	Project Name	County	Project Type
0016276	Hightower Road/Cooper Road NE Paving and Drainage Improvements	Lowndes	Grd Drn Bs Pv
0016302	8th Street Widening for Turn Lane	Tift / Tifton	Turn Lanes
0016202	Webster Road Sidewalks and Drainage Improvements	Brooks / Quitman	Sidewalks
0016296	Golf Course Road Alignment, Drainage and Resurfacing	Pierce	Resurfacing / Realignment
0016171	Cogdell Road Widen and Resurface	Atkinson	Shoulder Widen
0016287	S Patterson Street at Griffin Avenue Intersection and Drainage Improvements	Lowndes / Valdosta	Intsct Imp
0016198	Cherry Street Resurfacing	Brantley / Nahunta	Grd Drn Bs Pv
0016181	Johnson Lake Road Widening and Safety Improvements	Bacon	Shoulder Widen
0016201	DeVane Road Bridge Replacement, Widen and Resurface	Brooks	Bridge



# Hightower Rd, Lowndes County





# Johnson Lake Rd, Bacon County





# Golf Course Rd, Pierce County






# 8<sup>th</sup> Street, City of Tifton





# Youngie Fussell Rd, Coffee County

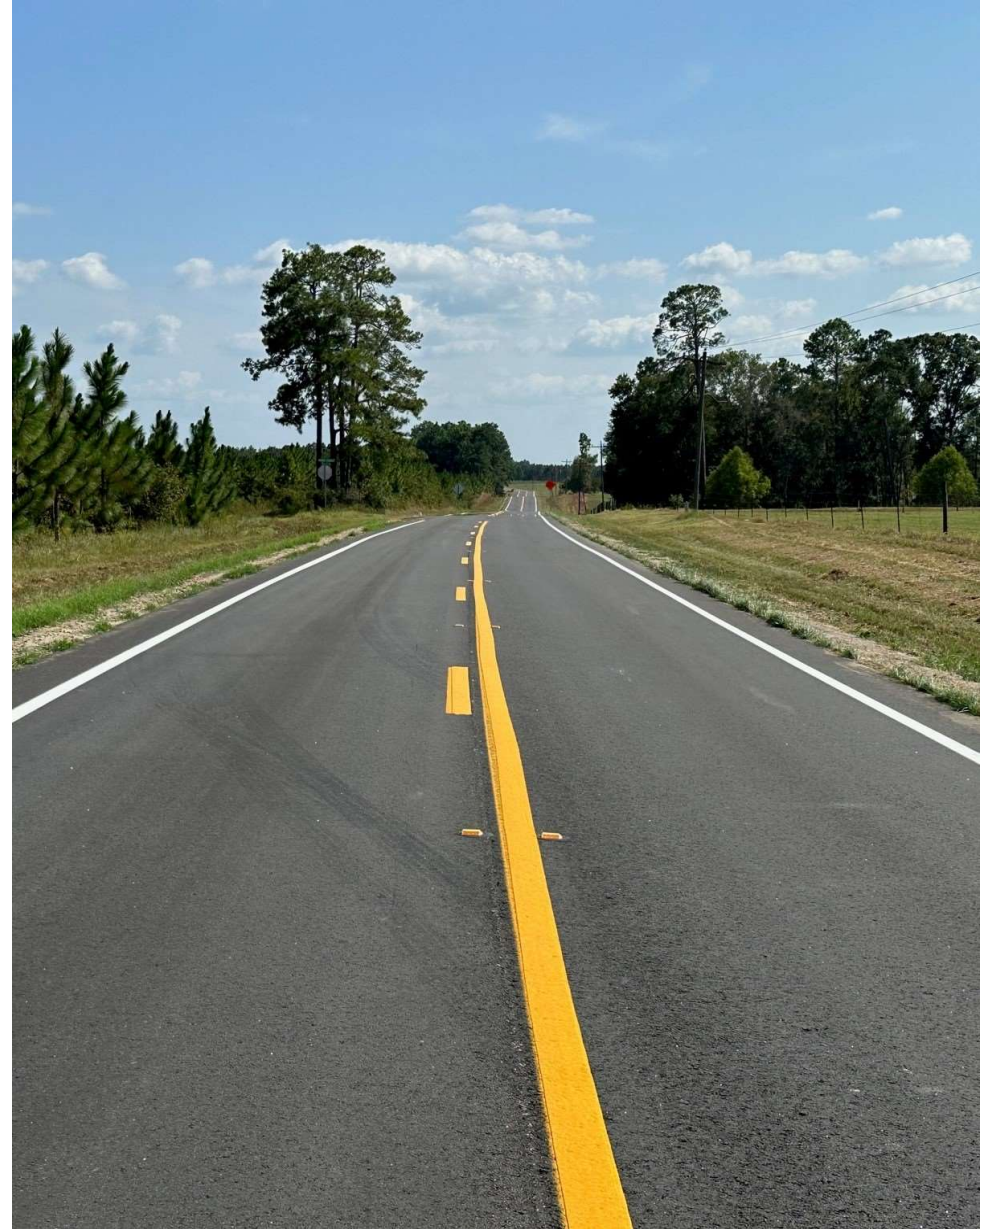




# US 41 @ Griffin Ave, City of Valdosta






# Projects with Local Let Agreements

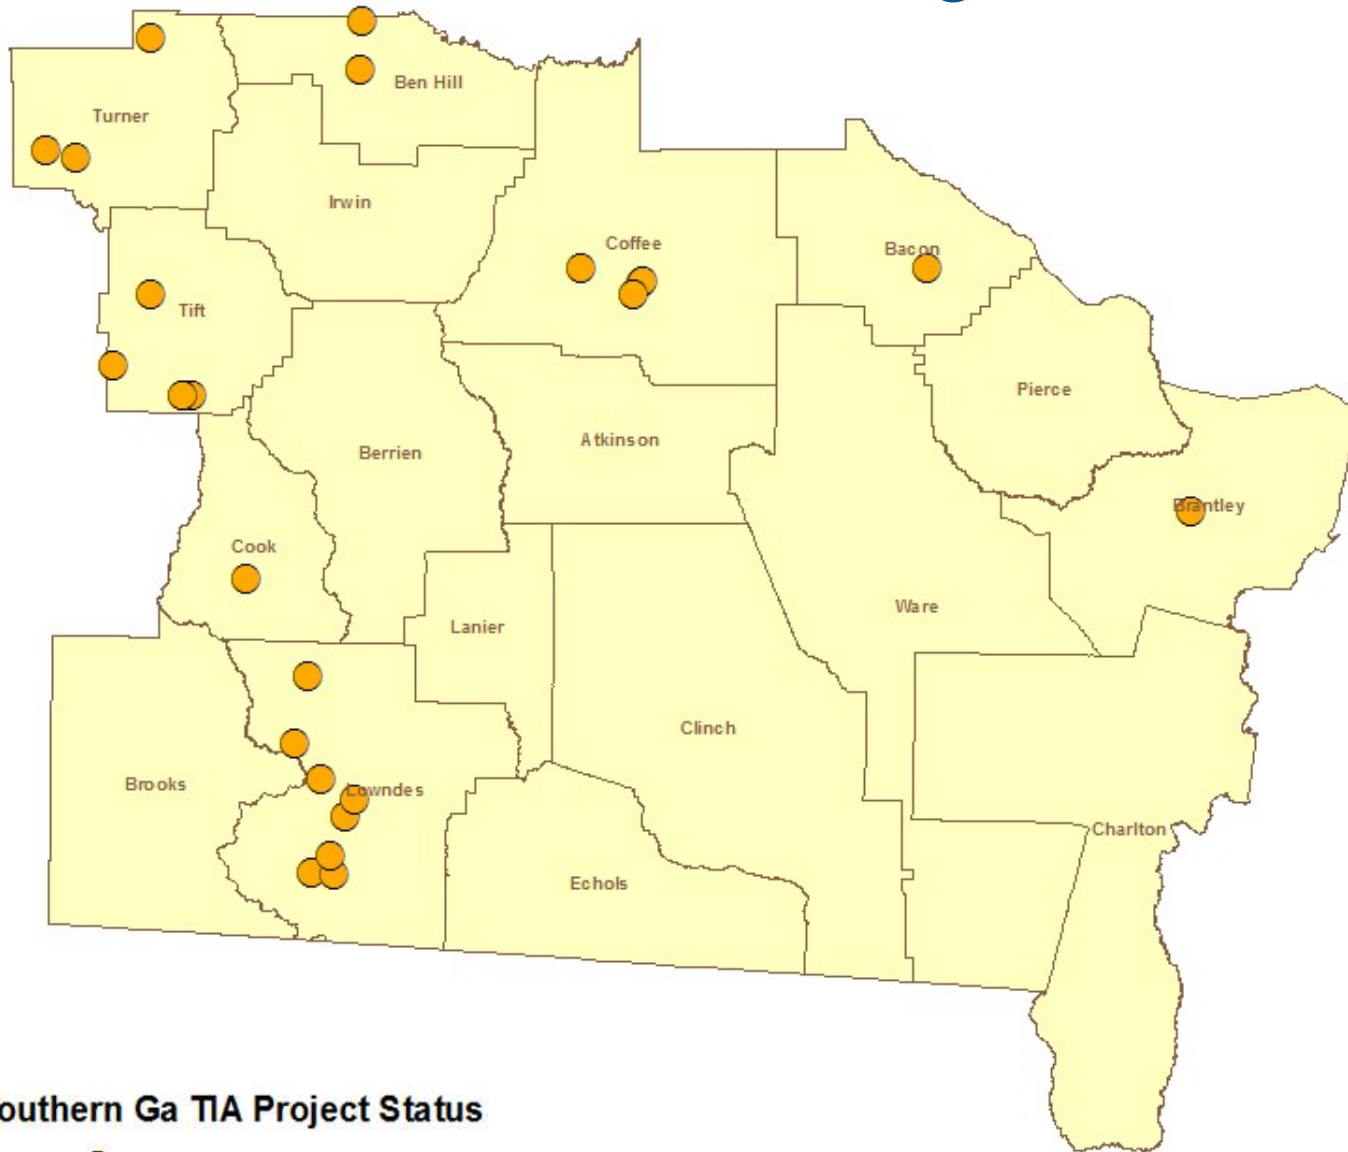

**Southern Ga TIA Project Status**

● PE-Local


# Projects under Construction

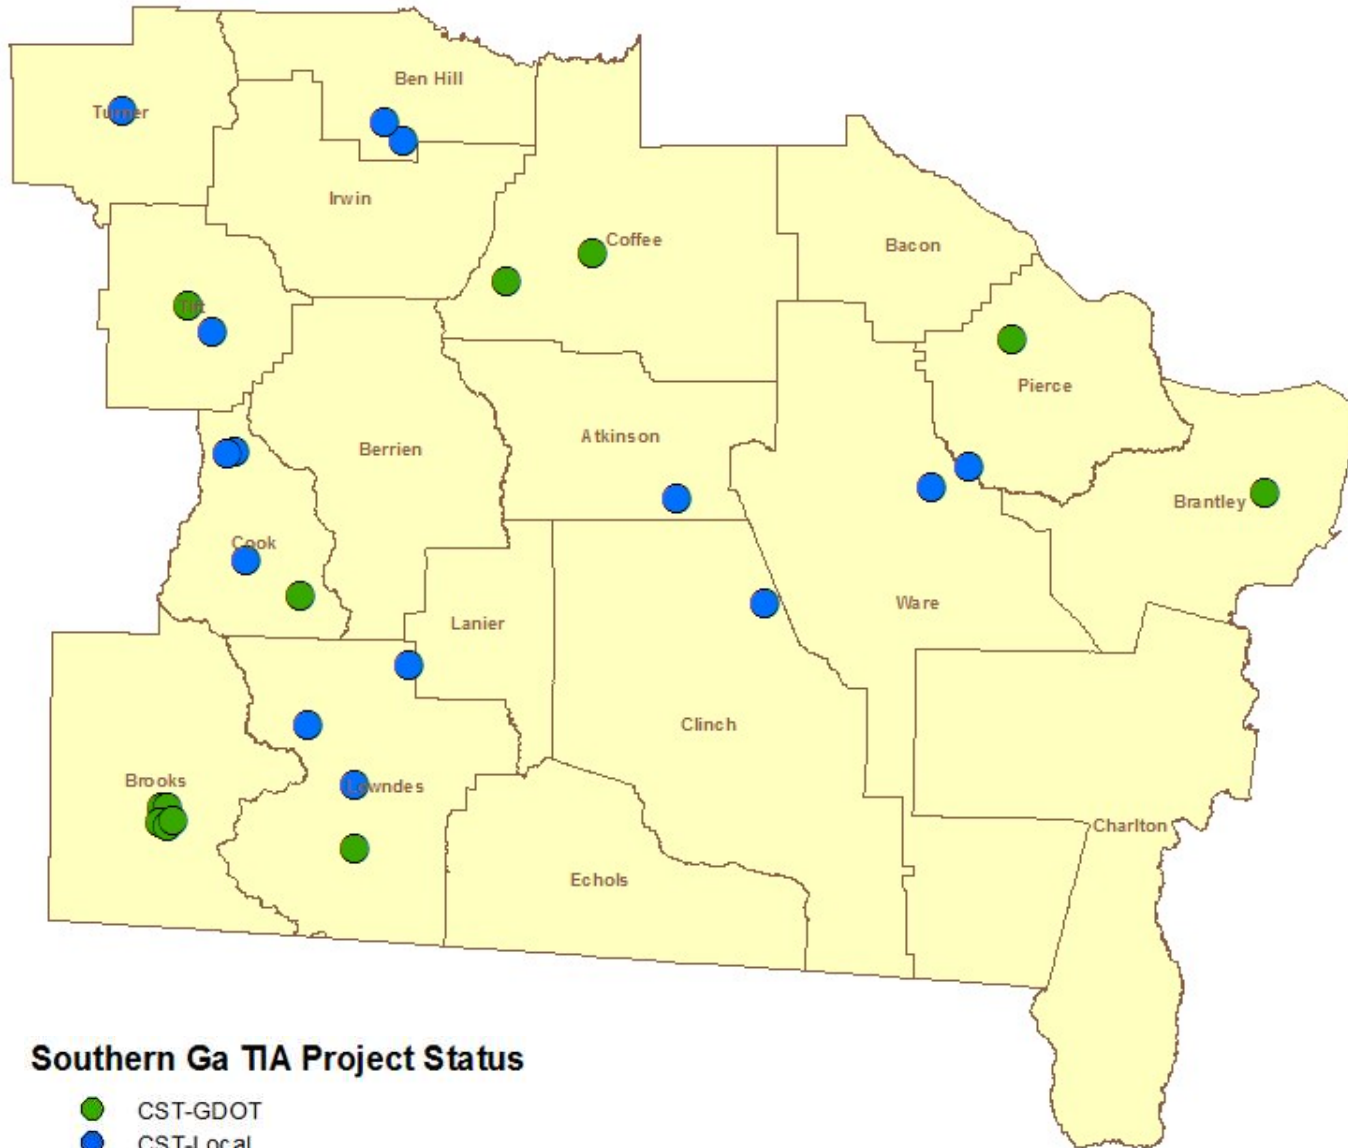

## Southern Ga TIA Project Status

- CST-GDOT
- CST-Local

# Completed Projects

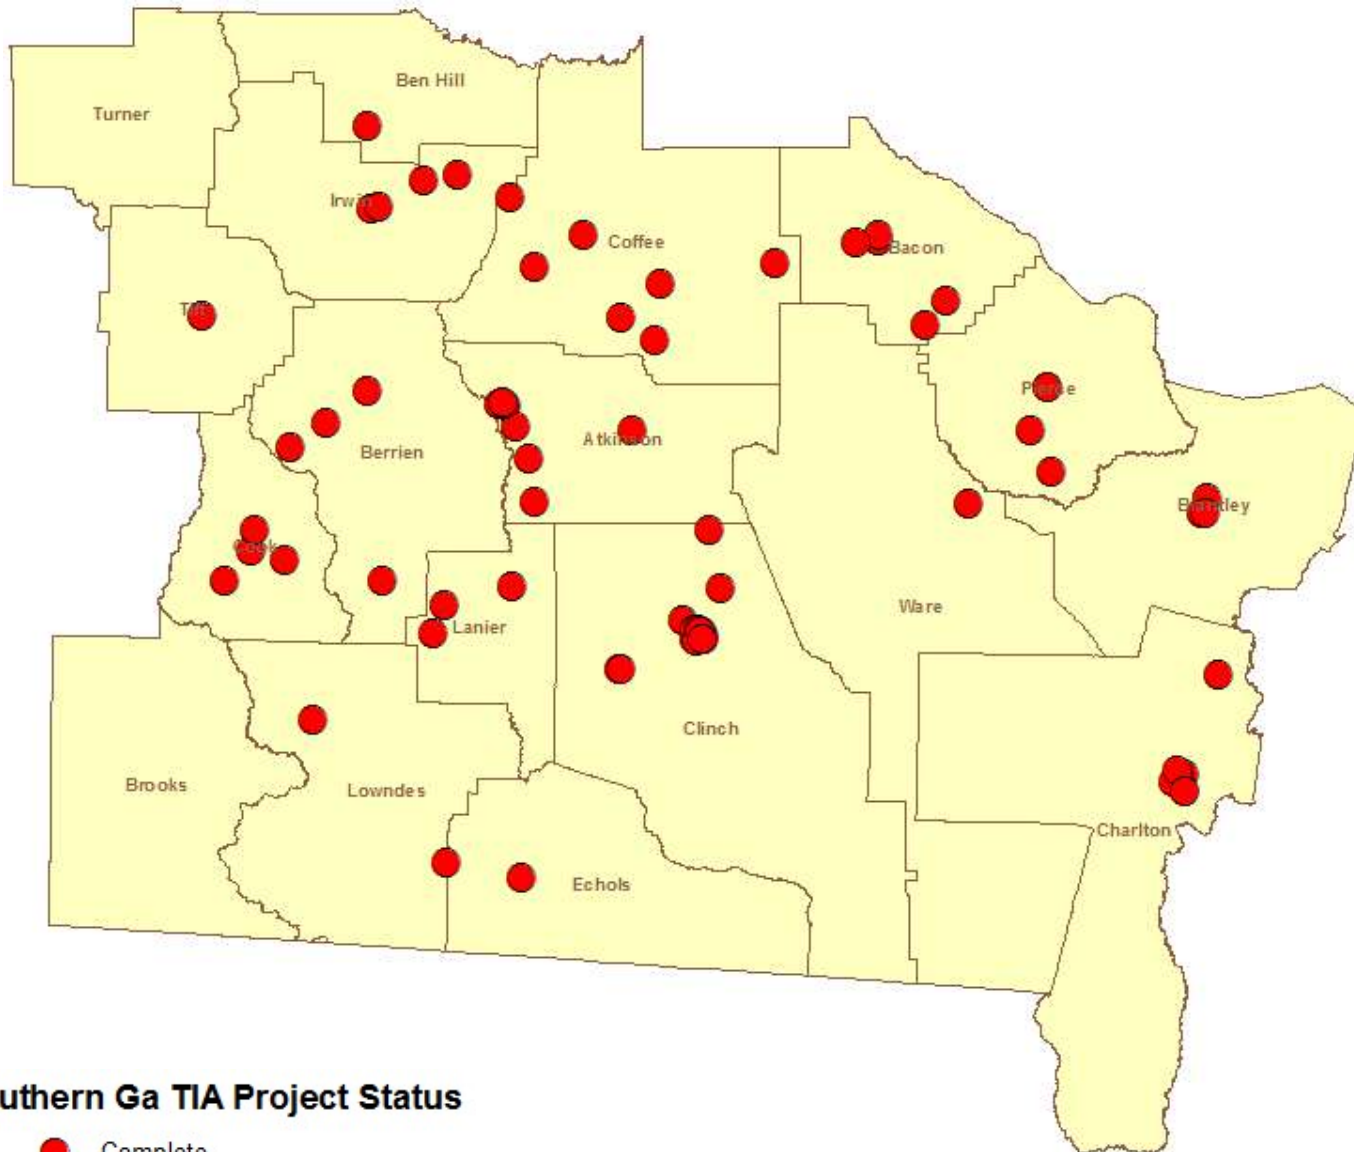

**Southern Ga TIA Project Status**

● Complete

# Questions?

**SOUTHERN GEORGIA**



**TRANSPORTATION  
INVESTMENT ACT**

*Your Penny, Your Progress*
